
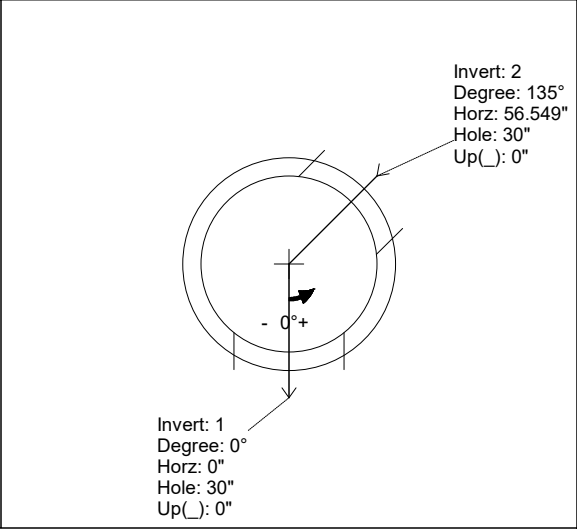
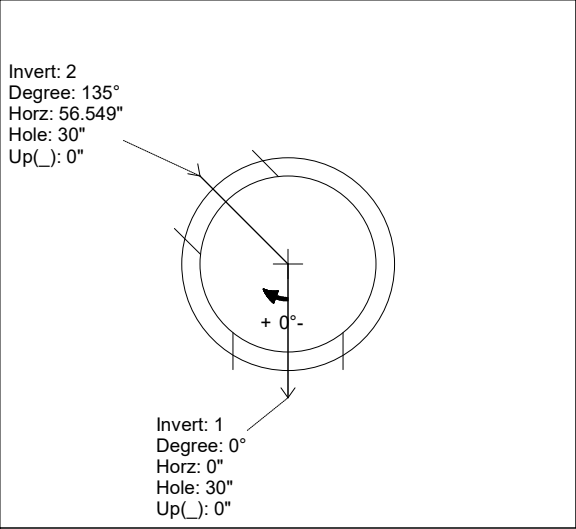
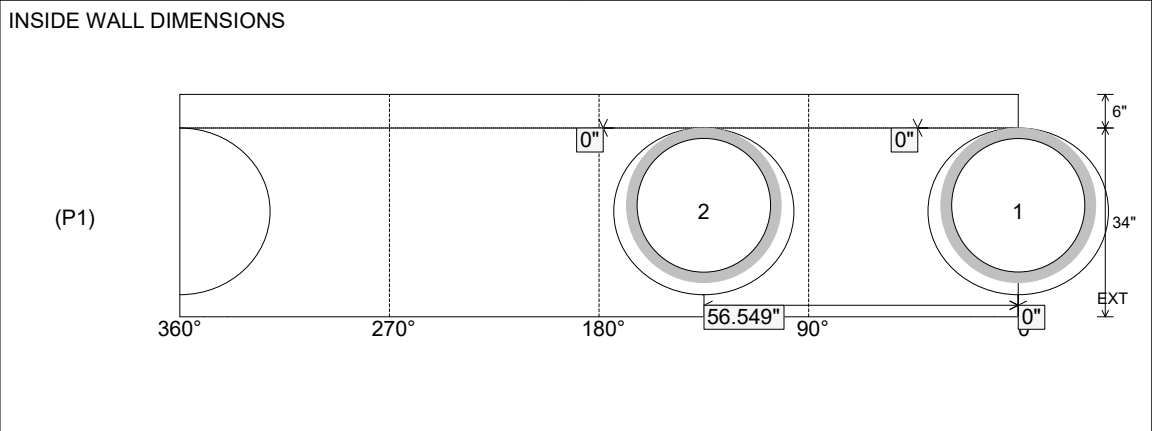


Job Name: 26-2484 Bass Pro Shops Outpost Paducah Job Location: Paducah, KY Contractor: Central Paving Co. of Paducah, Inc.					Plant: Beaver Dam 6/16/2026 8:02:29 AM		Tech: S. Felletter PC: A. Chambers														
Structure ID: X4 ST-CI																					
P1 MH048BAVF		MH BASE Custom Ht F/n																			
P3) 24" x 24" - CASTING HEIGHT - 5" P2) 48" - MH FLAT TOP w/24"x24" Hole F/F - 7" P1) 48" - MH BASE Custom Ht F/n - 34" 1) CASTING - HOE KY-465 SET (CBI TY F) 1) 48" - Conseal CS-102 1.00" 1) 24" x 24" - Conseal CS-102 1.00" 2) Hole - 30						0 lb 1214 lb 3073 lb 465 lb 0 lb 0 lb 0 lb ----- Structure Total: 4752 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE 465 F/G/H). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.													
Rim: 368.7'		Rim to Invert: 3.7'		Slack: 0.3"		Sump: 1.9"		Step Position: 0°													
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset											
Invert 1	365'	0°	0"	24" HDPE	27.8"	Hole 30	30"	32.406"	0"	0"											
Invert 2	365'	135°	68.33"	24" HDPE	27.8"	Hole 30	30"	32.406"	0"	0"											
Invert 3																					
Invert 4																					
Invert 5																					
Invert 6																					
Invert 7																					
Invert 8																					
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimenions)  INVERT 2 Degree: 135° Horz: 56.549" Hole: 30" Up(): 0" INVERT 1 Degree: 0° Horz: 0" Hole: 30" Up(): 0" INVERT 2 Degree: 135° Horz: 56.549" Hole: 30" Up(): 0" INVERT 1 Degree: 0° Horz: 0" Hole: 30" Up(): 0" INSIDE WALL DIMENSIONS  (P1) 360° 270° 180° 90° 6" 34" EXT 0" 0" 56.549" 0" 2 1												Coating (Int): Coating (Ext):		Seam Up: Flat Seam Dn: n/a		Wall Thickness: 5" Floor Height: 6"		Height (Int): 34" Height (Ext): 40"		Weight (Net): 3073 lb Volume (Net): 0.78cu.yd	
