

Job Name: 26-2485 855358 Fuqua Development
Job Location: Nicholasville, KY
Contractor: Contech Engineering Solutions

Plant: Beaver Dam
6/5/2026 8:57:14 AM

Tech: S. Felletter
PC: C. Goff



Structure ID: 15-CS-12

P2 MH144RS54

MH RISER T/G

- P6) 24" - CASTING HEIGHT - 4"
P5) 144" - MH FLAT TOP SPEC. (2 - 24"Ø HOLES) F/G - 18"
P4) 144" - MH RISER T/G - 36"
P3) 144" - MH RISER T/G - 78"
P2) 144" - MH RISER T/G - 54"
P1) 144" - MH MONOBASE 14F, Custom Ht T/n - 24"
1) ASSEMBLY REQUIRED - BRACKETS ONLY
1) CVSTENCILING
4) 144" - Conseal CS-102 1.00"
1) 24" - Conseal CS-102 1.00"
2) Hole - 48

- 0 lb
23623 lb
19370 lb
37954 lb
29054 lb
39578 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb
- Structure Notes: .
1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. 4" CASTING BY OTHERS
4. LIFTING ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE
5. ICAST TO INSTALL BRACKETS ONLY
6. CONTECH'S LOGO AS WELL AS THE INLET AND OUTLET MUST BE STENCILED ONTO THE STRUCTURE



Structure Total: 149579 lb

- REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
- RISER/WALLS (As .36)
- FLOOR (As .47) #5 BARS AT 8" C.C.E.W.


Rim: 1019.05' Rim to Invert: 9.75' Slack: 11.036" Sump: 108.036" Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

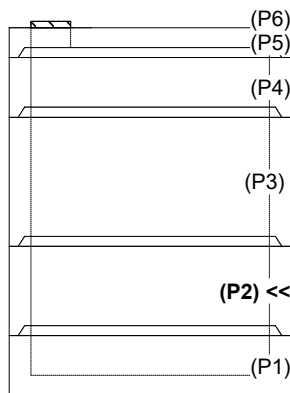

INSIDE WALL DIMENSIONS



Coating (Int):
Coating (Ext):

Seam Up: Tongue
Seam Dn: Groove

Wall Thickness: 13"
Floor Height: 0"

Height (Int): 54"
Height (Ext): 54"

Weight (Net): 29054 lb
Volume (Net): 7.42cu.yd
