

Job Name: 26-2485 855358 Fuqua Development
Job Location: Nicholasville, KY
Contractor: Contech Engineering Solutions

Plant: Beaver Dam

6/5/2026 8:56:50 AM

Tech: S. Felletter

PC: C. Goff



Structure ID: 15-CS-12

P5 MH144LD18SP

MH FLAT TOP SPEC. (2 - 24"Ø HOLES) F/G

- P6) 24" - CASTING HEIGHT - 4"
P5) 144" - MH FLAT TOP SPEC. (2 - 24"Ø HOLES) F/G - 18"
P4) 144" - MH RISER T/G - 36"
P3) 144" - MH RISER T/G - 78"
P2) 144" - MH RISER T/G - 54"
P1) 144" - MH MONOBASE 14F, Custom Ht T/n - 24"
1) ASSEMBLY REQUIRED - BRACKETS ONLY
1) CVSTENCILING
4) 144" - Conseal CS-102 1.00"
1) 24" - Conseal CS-102 1.00"
2) Hole - 48

- 0 lb
23623 lb
19370 lb
37954 lb
29054 lb
39578 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb
- Structure Notes:**
1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. 4" CASTING BY OTHERS
4. LIFTING ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE
5. ICAST TO INSTALL BRACKETS ONLY
6. CONTECH'S LOGO AS WELL AS THE INLET AND OUTLET MUST BE STENCILED ONTO THE STRUCTURE



Structure Total:

149579 lb

REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
- RISER/WALLS (As .36)
- FLOOR (As .47) #5 BARS AT 8" C.C.E.W.

GENERAL NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE 5,000 PSI AT 28 DAYS.
3. REINFORCING: #4 & #6 BAR AS SHOWN (GRADE 60).
4. WEIGHT: 23,626 LBS.

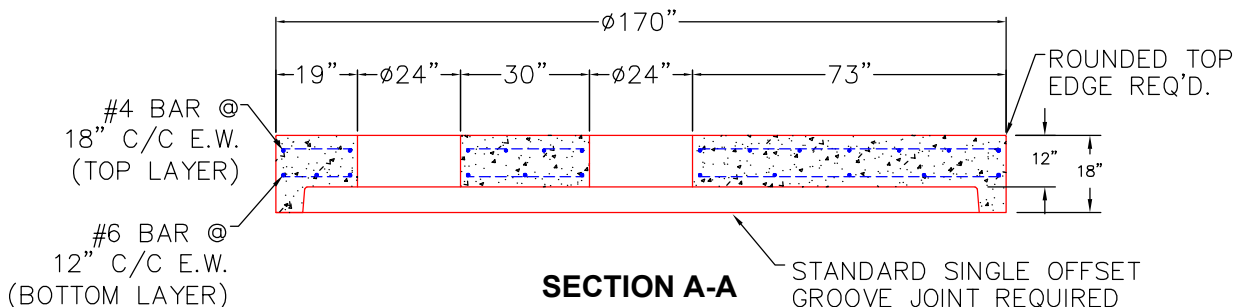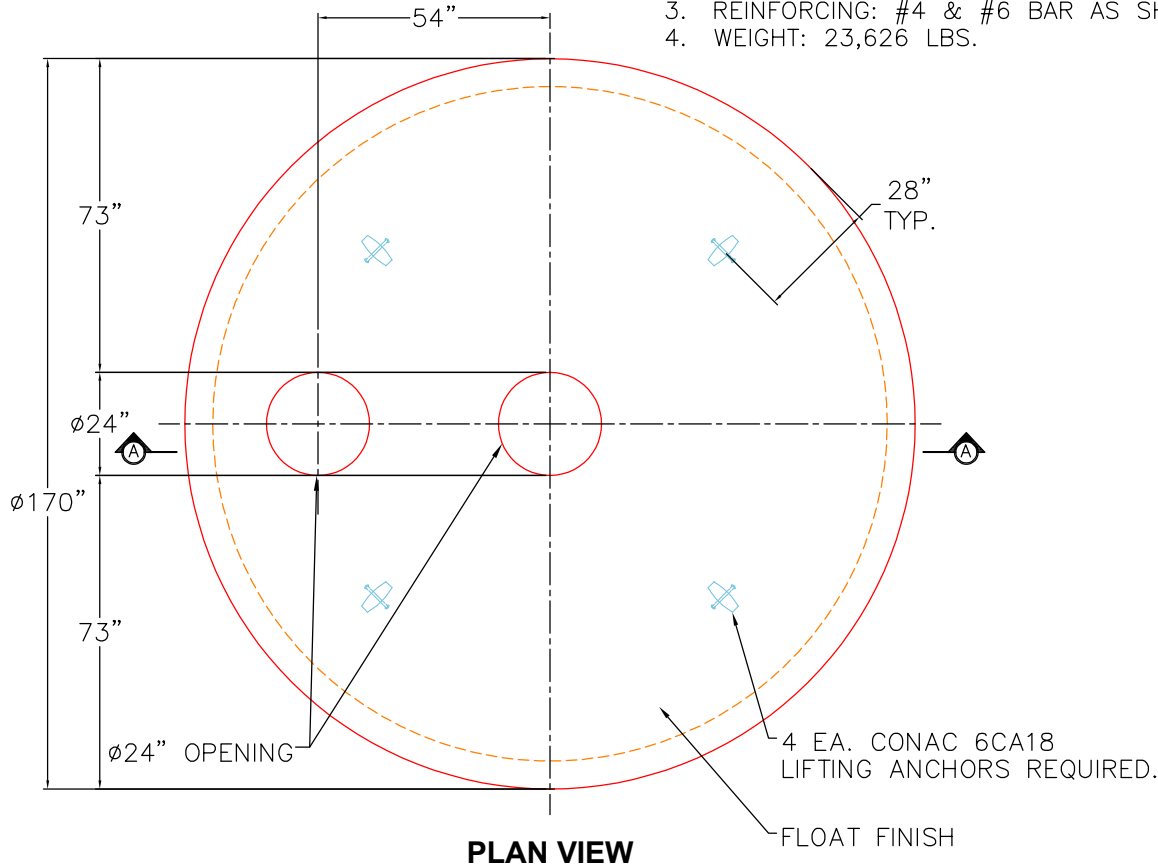

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 13"

Height (Ext): 18"

Weight (Net): 23623 lb
Volume (Net): 6.03cu.yd
