

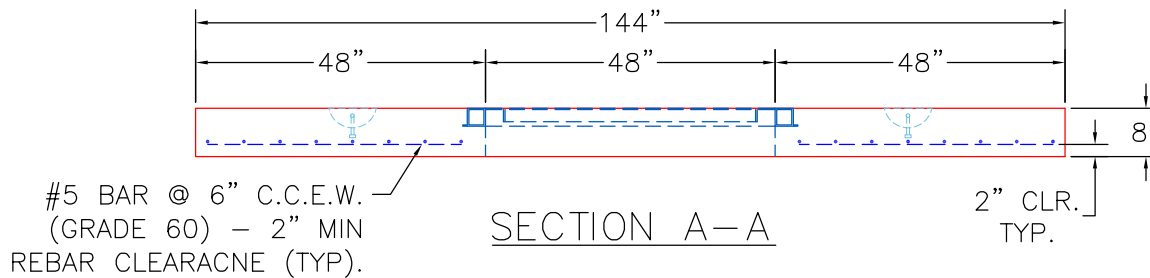


GENERAL NOTES:

1. MANUFACTURED TO ASTM C-913 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" C.C.E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP).
4. WEIGHT: 6,573 LBS
5. HATCH: 48" X 48" HATCH W/ 8" SKIRT SUPPLIED BY OTHERS, TO BE CAST INTO TOP OF LID.
6. DOUBLE ROLL CS-102 JOINT SEALANT.

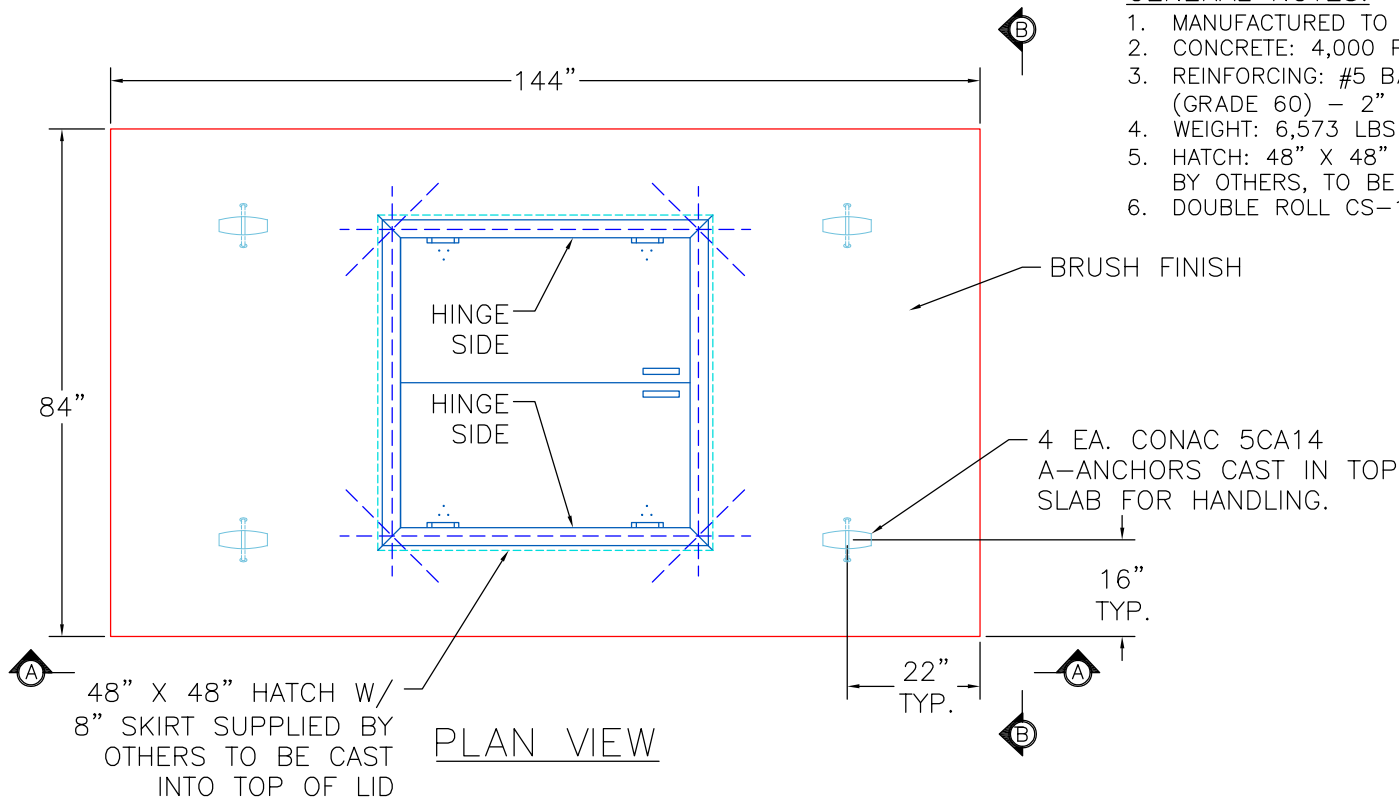

PRODUCTION WORK ORDER		PRODUCT I.D.: BX072132-08LD06S	DESCRIPTION: 84" X 144" FLAT TOP W/ 48" X 48" HATCH	
	QUALITY CONTROL CHECKLIST ☐ ALL DIMENSIONS CORRECT. ☐ LIFTERS INSTALLED. ☐ HATCH CORRECT LOCATION. ☐ REINFORCING CORRECT. ☐ SURFACE QUALITY ACCEPTABLE. ☐ EDGES CHAMFERED. ☐ ALL PATCHWORK ACCEPTABLE.	PRODUCT VIEW: RIGHT SIDE UP	CUSTOMER: CORE & MAIN (BG)	
		PLANT: BEAVER DAM, KY.	PROJECT: CAMBELL VIEW APARTMENTS VAULT	
		WEIGHT: 6,573 LBS.	STRUCTURE: QL1	
		TOP SECTION JOINT: N/A	ORDER NO: 26-2495	
		BOTTOM SECTION JOINT: FLAT	PC: T. LEWIS	DRAWING: S. FELLETER
		QC CHECK INITIALS:	DATE: 08/12/26	SCALE: NTS PG. 1 of 1
