

Contractor: Koberstein Contracting, Inc.


TECH: Jared - F

Plant: 100





Slack: 0.96"

Structure Total: 7273 lb

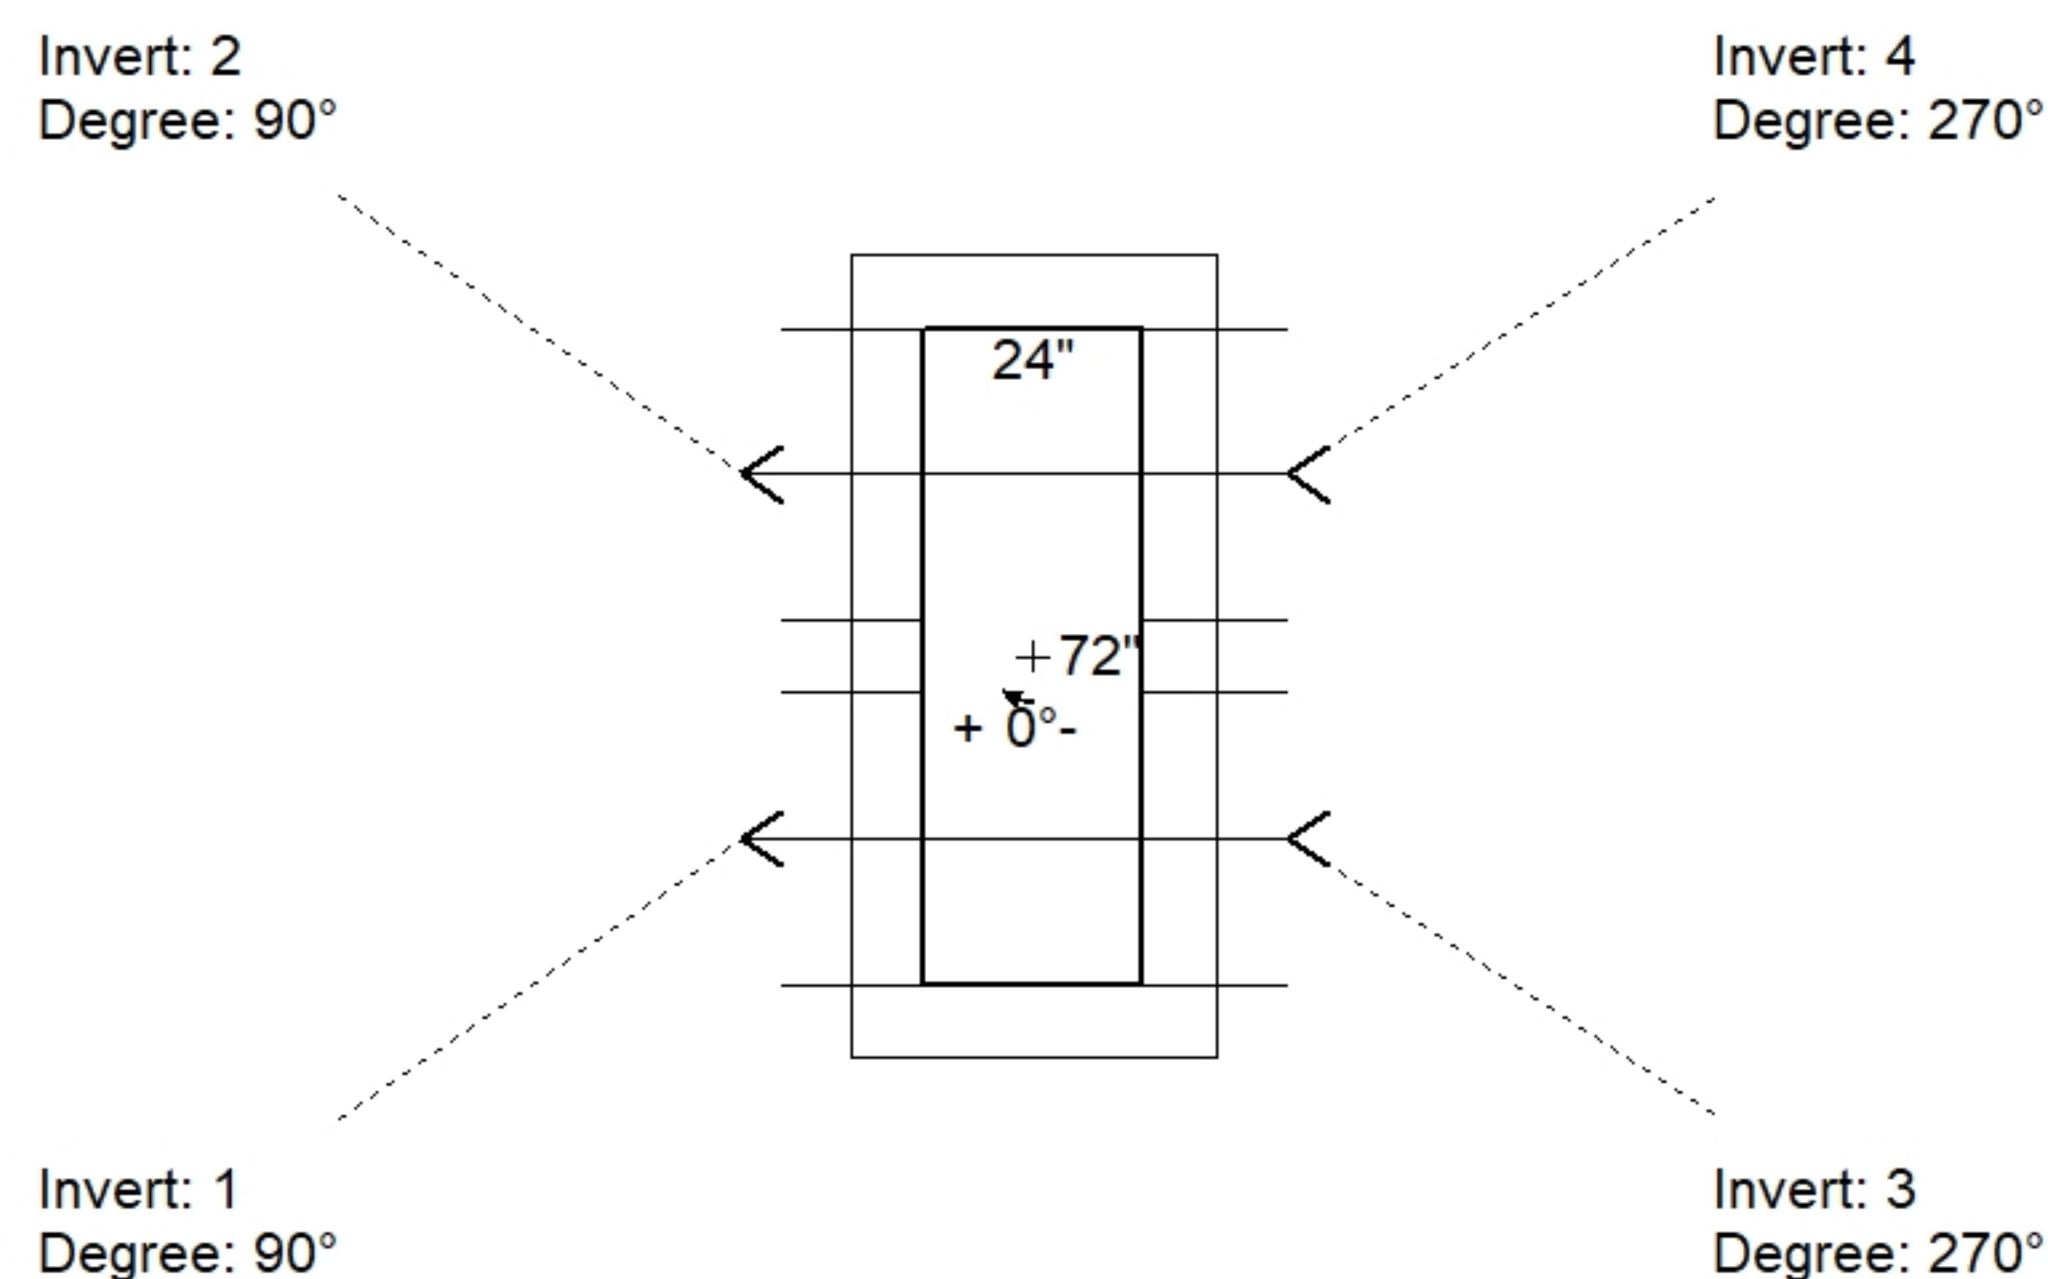

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	393.52'							
Reducer								
Invert 1	390.19'	90°	24" RCP B WALL	30"	32"	Hole 32	0"	P1
Invert 2	390.19'	90°	24" RCP B WALL	30"	32"	Hole 32	0"	P1
Invert 3	390.19'	270°	24" RCP B WALL	30"	32"	Hole 32	0"	P1
Invert 4	390.19'	270°	24" RCP B WALL	30"	32"	Hole 32	0"	P1
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

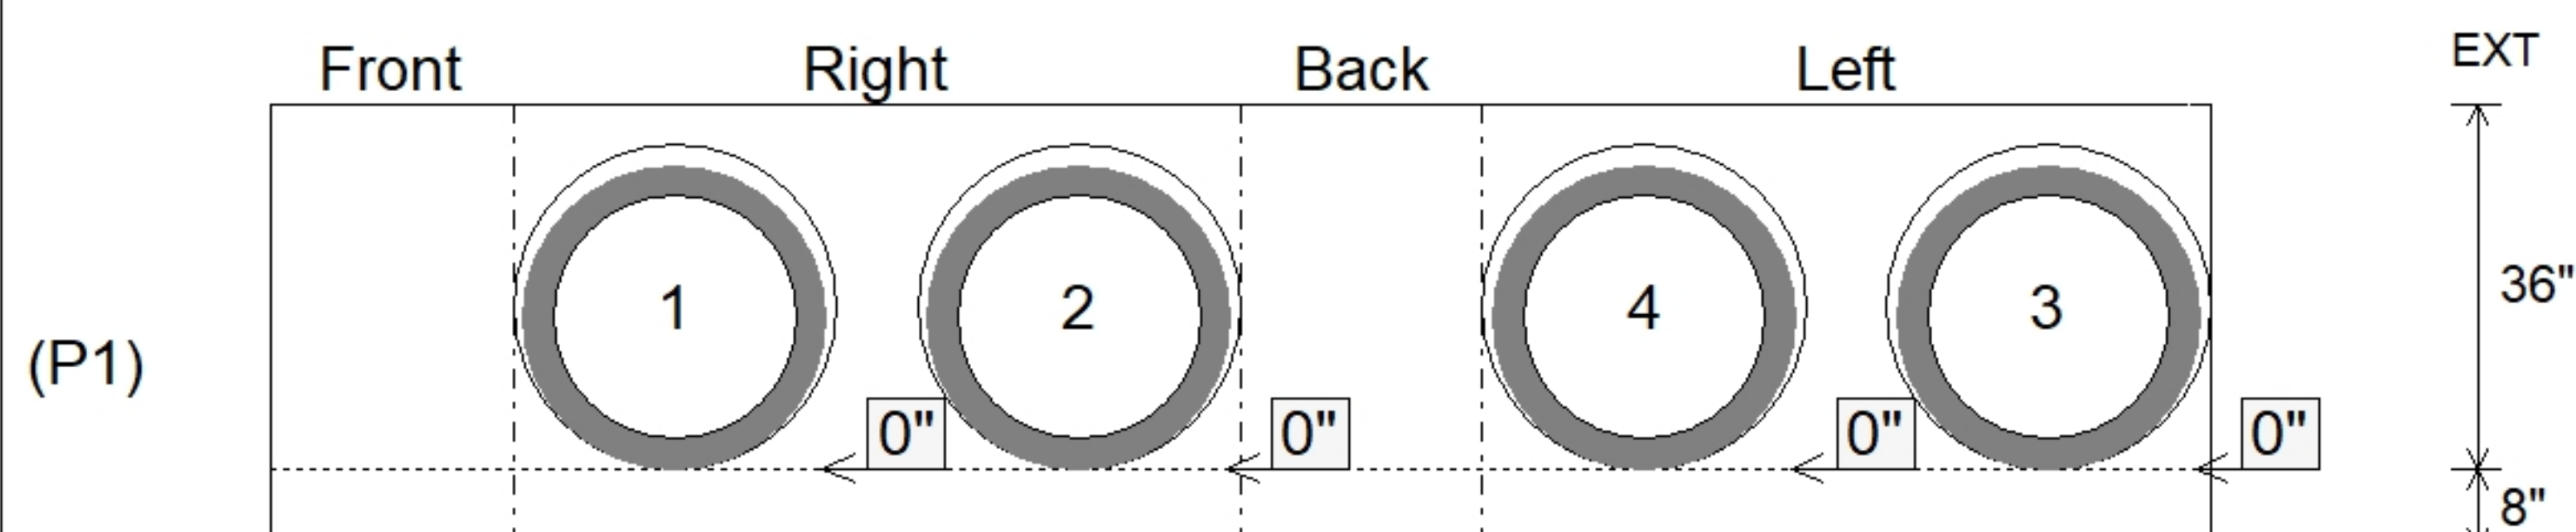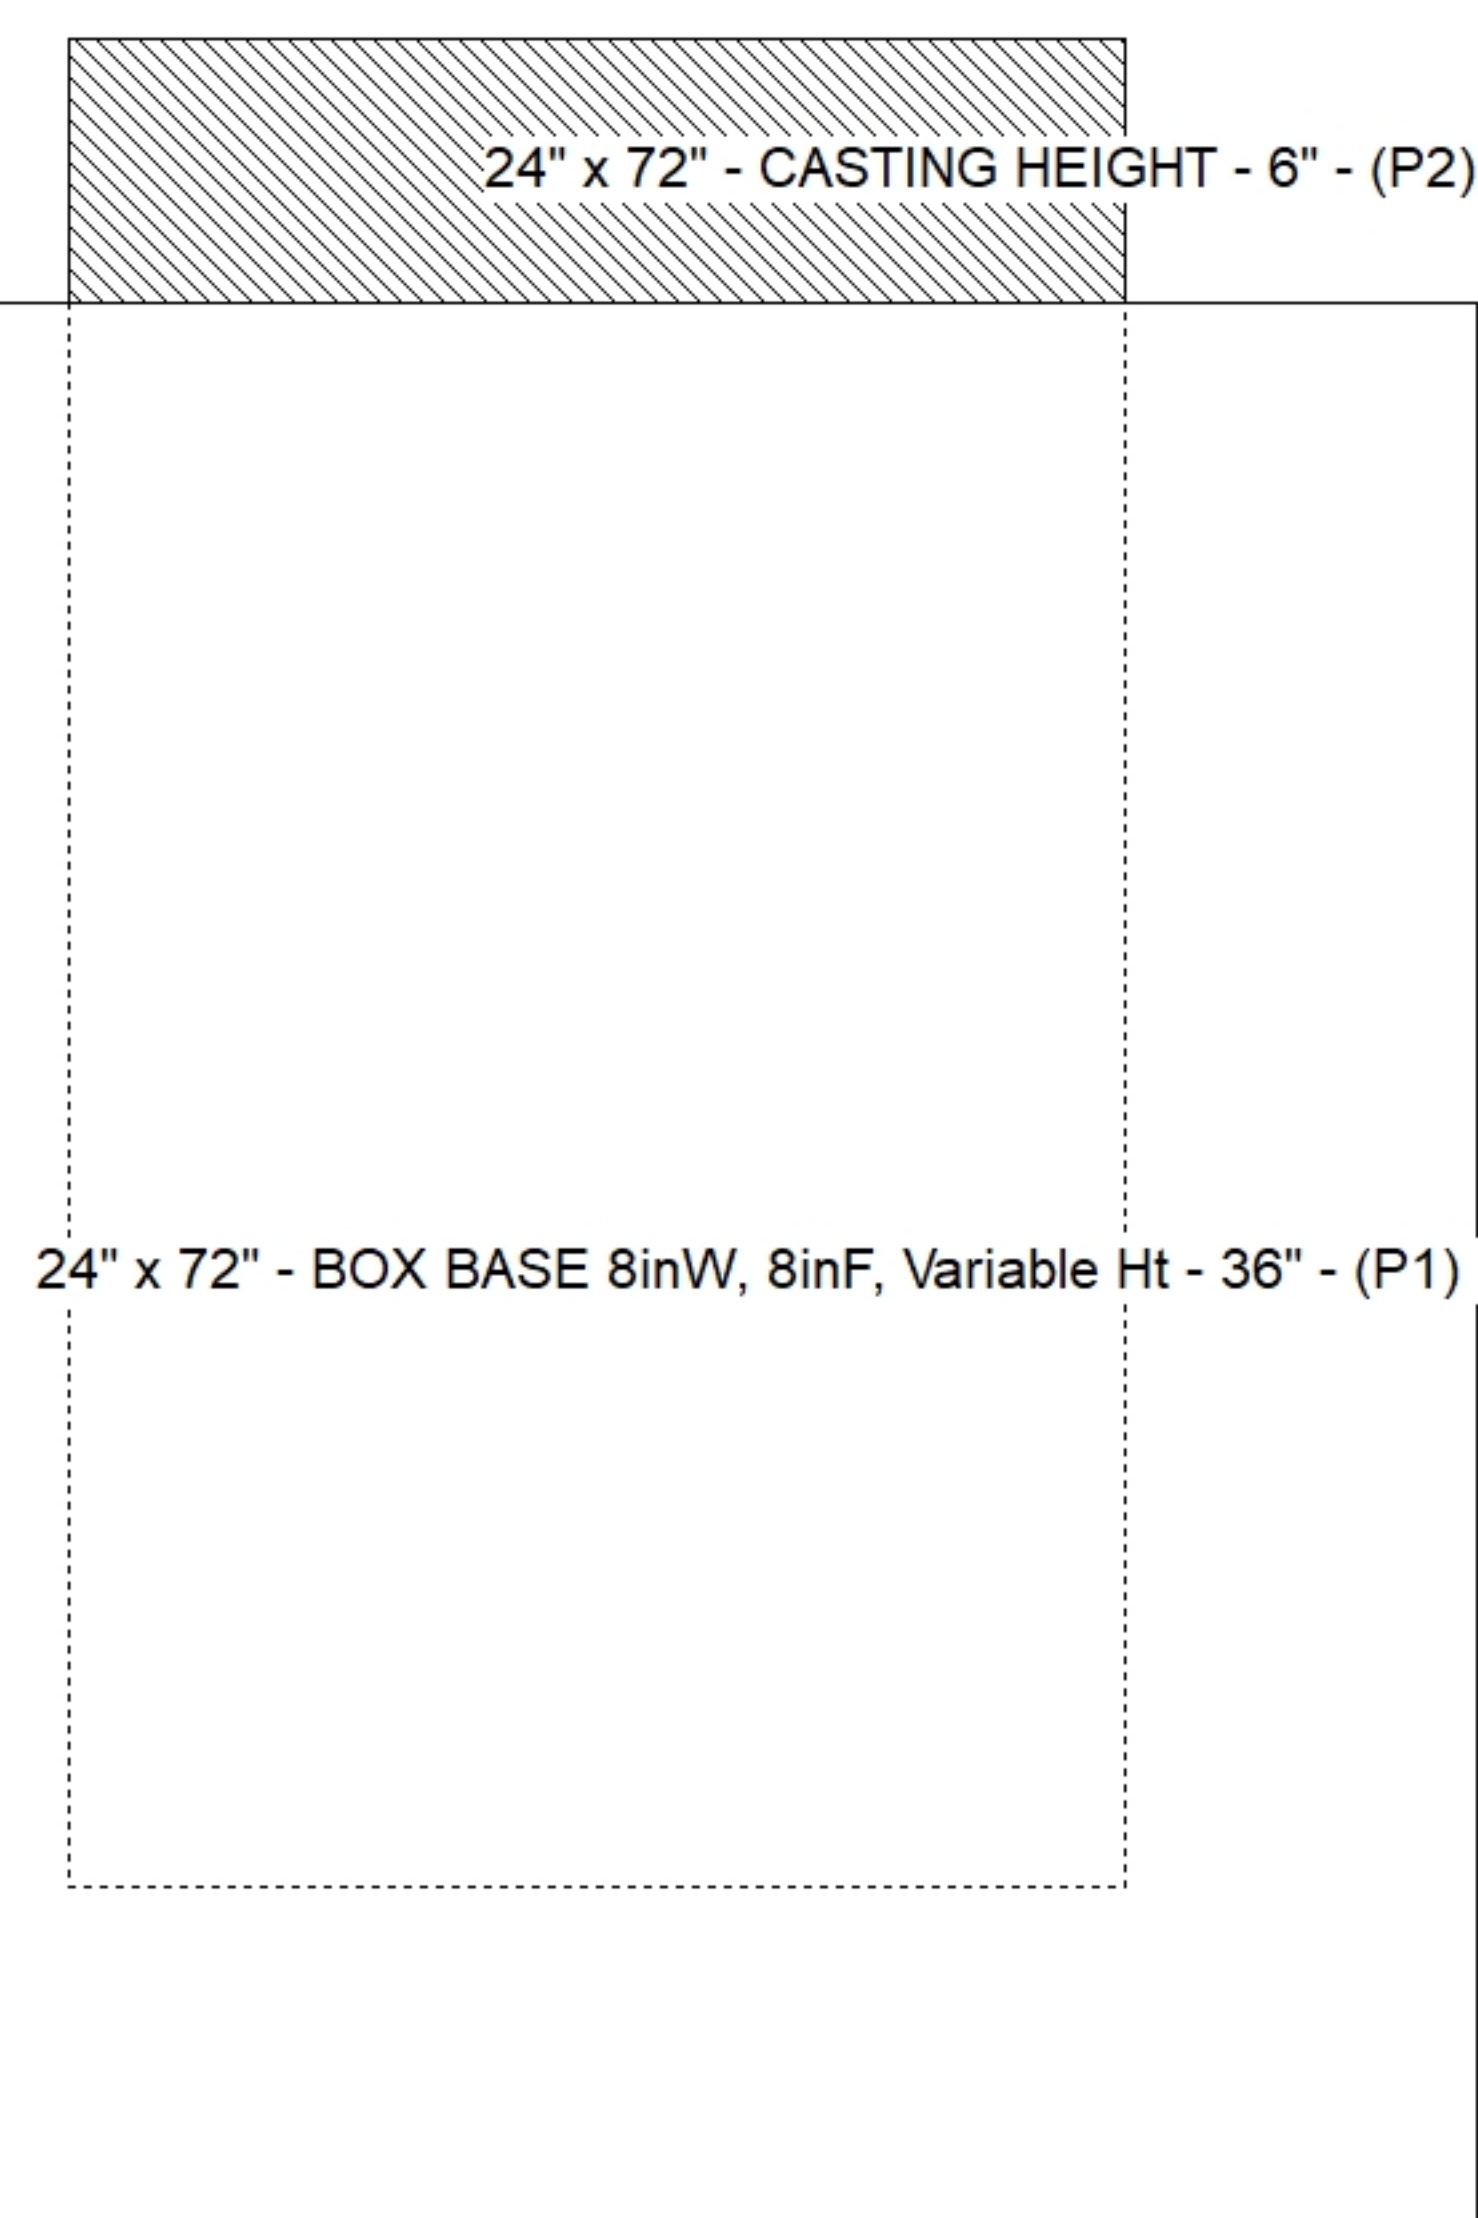

SUBMITTAL
APPROVED BY:
