

Contractor: Koberstein Contracting, Inc.

TECH: Jared - F

Plant: 100



Size: 24" x 36"

Rim to Invert: 3.31'

Floor Height: 8"


Slack: 0.72"

REINFORCING PER ASTM A615 (GRADE 60).
- WALLS (As .12) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .12) #5 BARS AT 12" C.C.E.W.

P2) 24" x 36" - CASTING HEIGHT - 6"
P1) 24" x 36" - BOX BASE 8inW, 8inF - 36"
1) CASTING - HOE 525 SET FLAT GRATE (F/G/H)
1) 24" x 36" - Conseal CS-102 1.00"
2) Hole - 32



0 lb
3990 lb
442 lb
0 lb
0 lb

Structure Total: 4432 lb

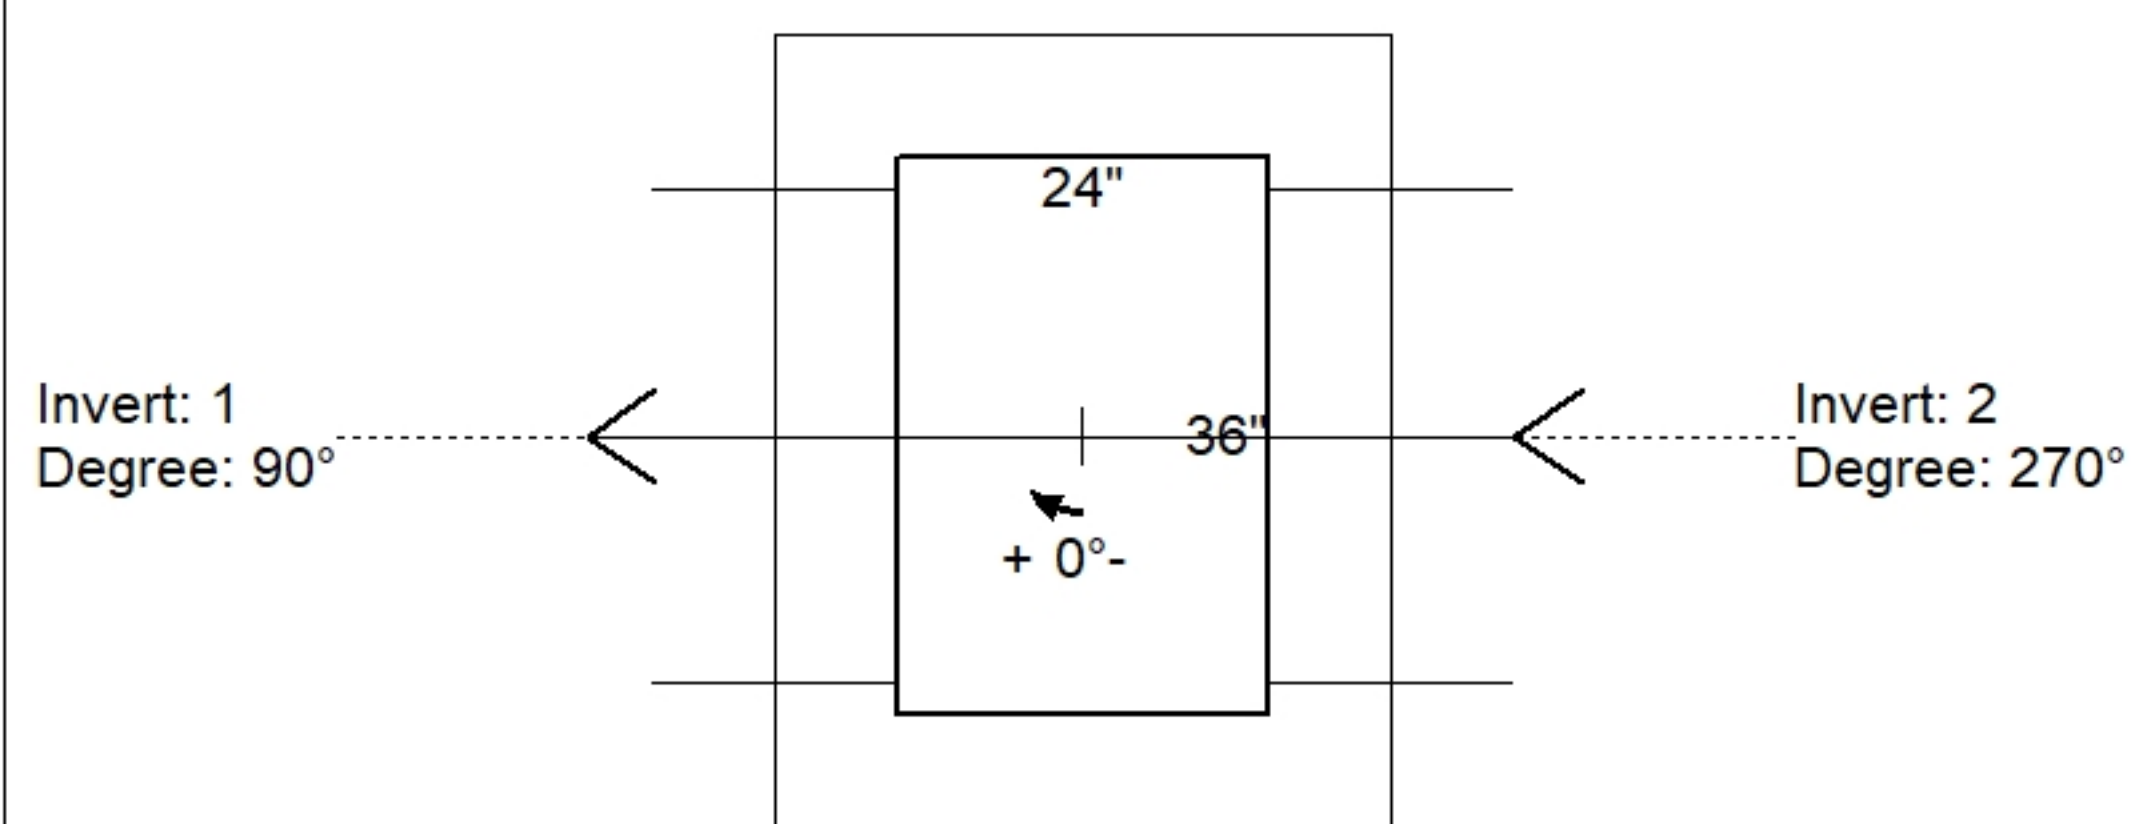

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	393.99'							
Reducer								
Invert 1	390.68'	90°	24" RCP B WALL	30"	32"	Hole 32	0"	P1
Invert 2	390.68'	270°	24" RCP B WALL	30"	32"	Hole 32	0"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

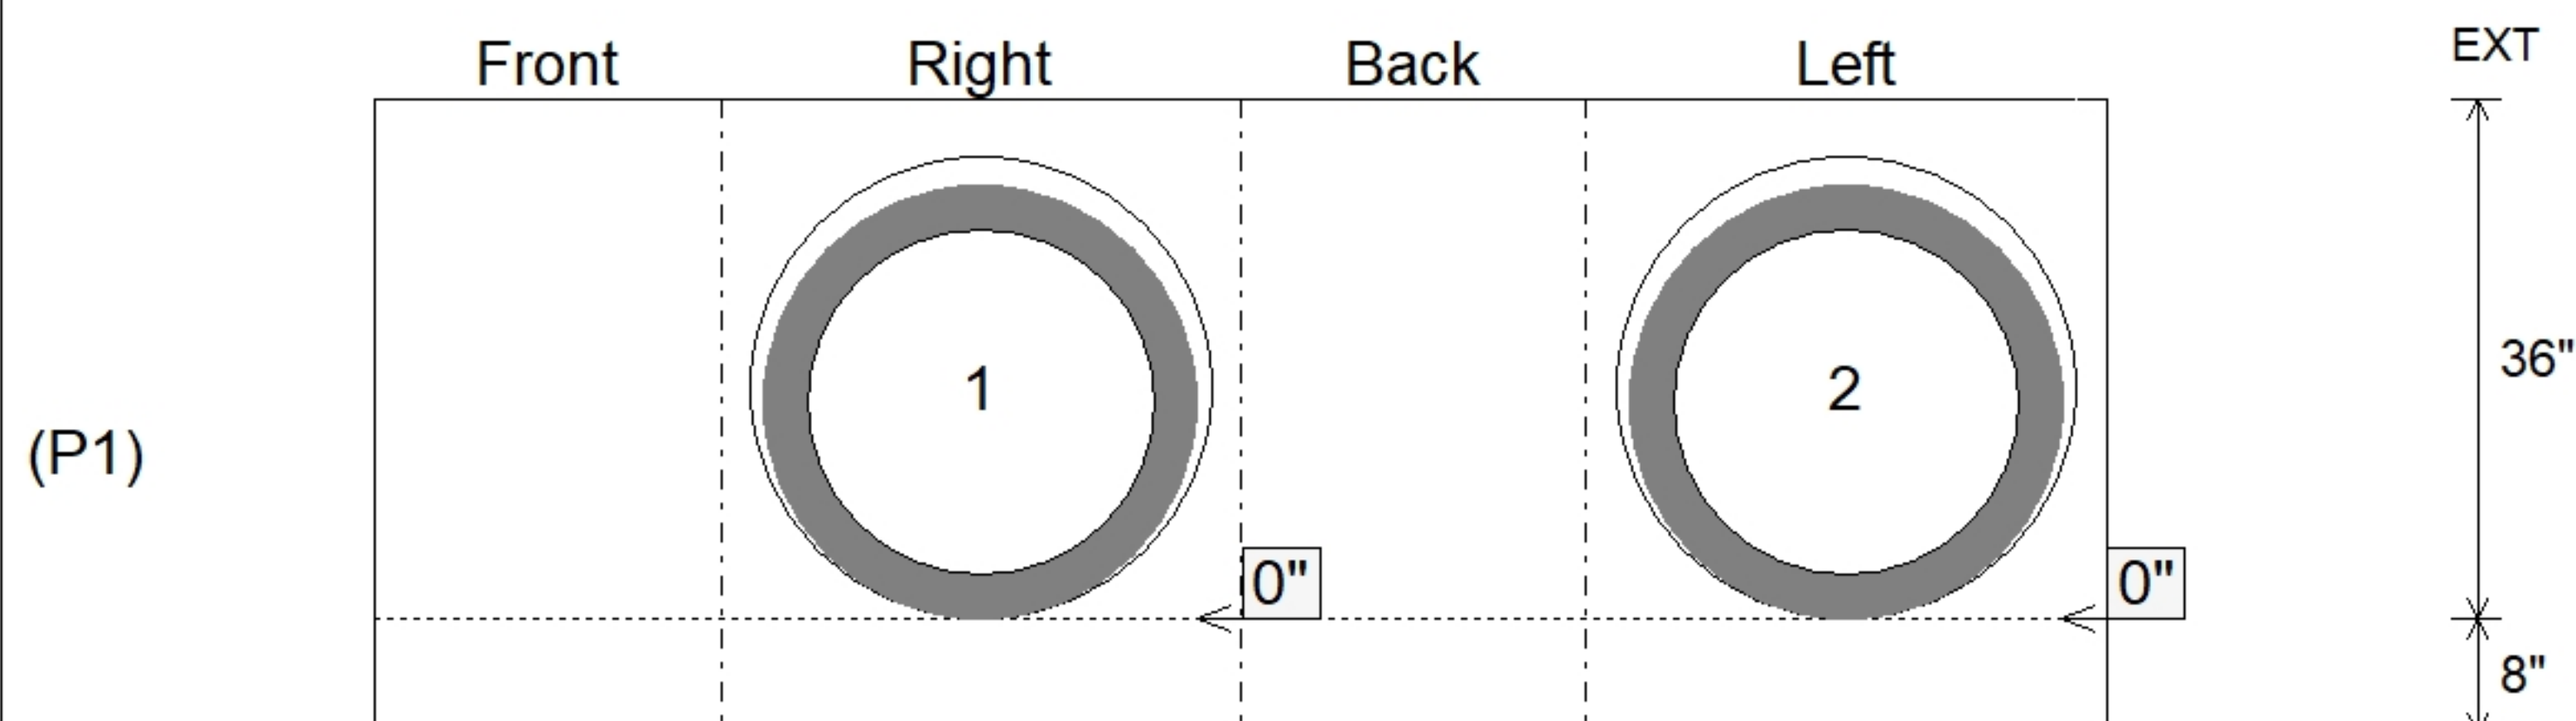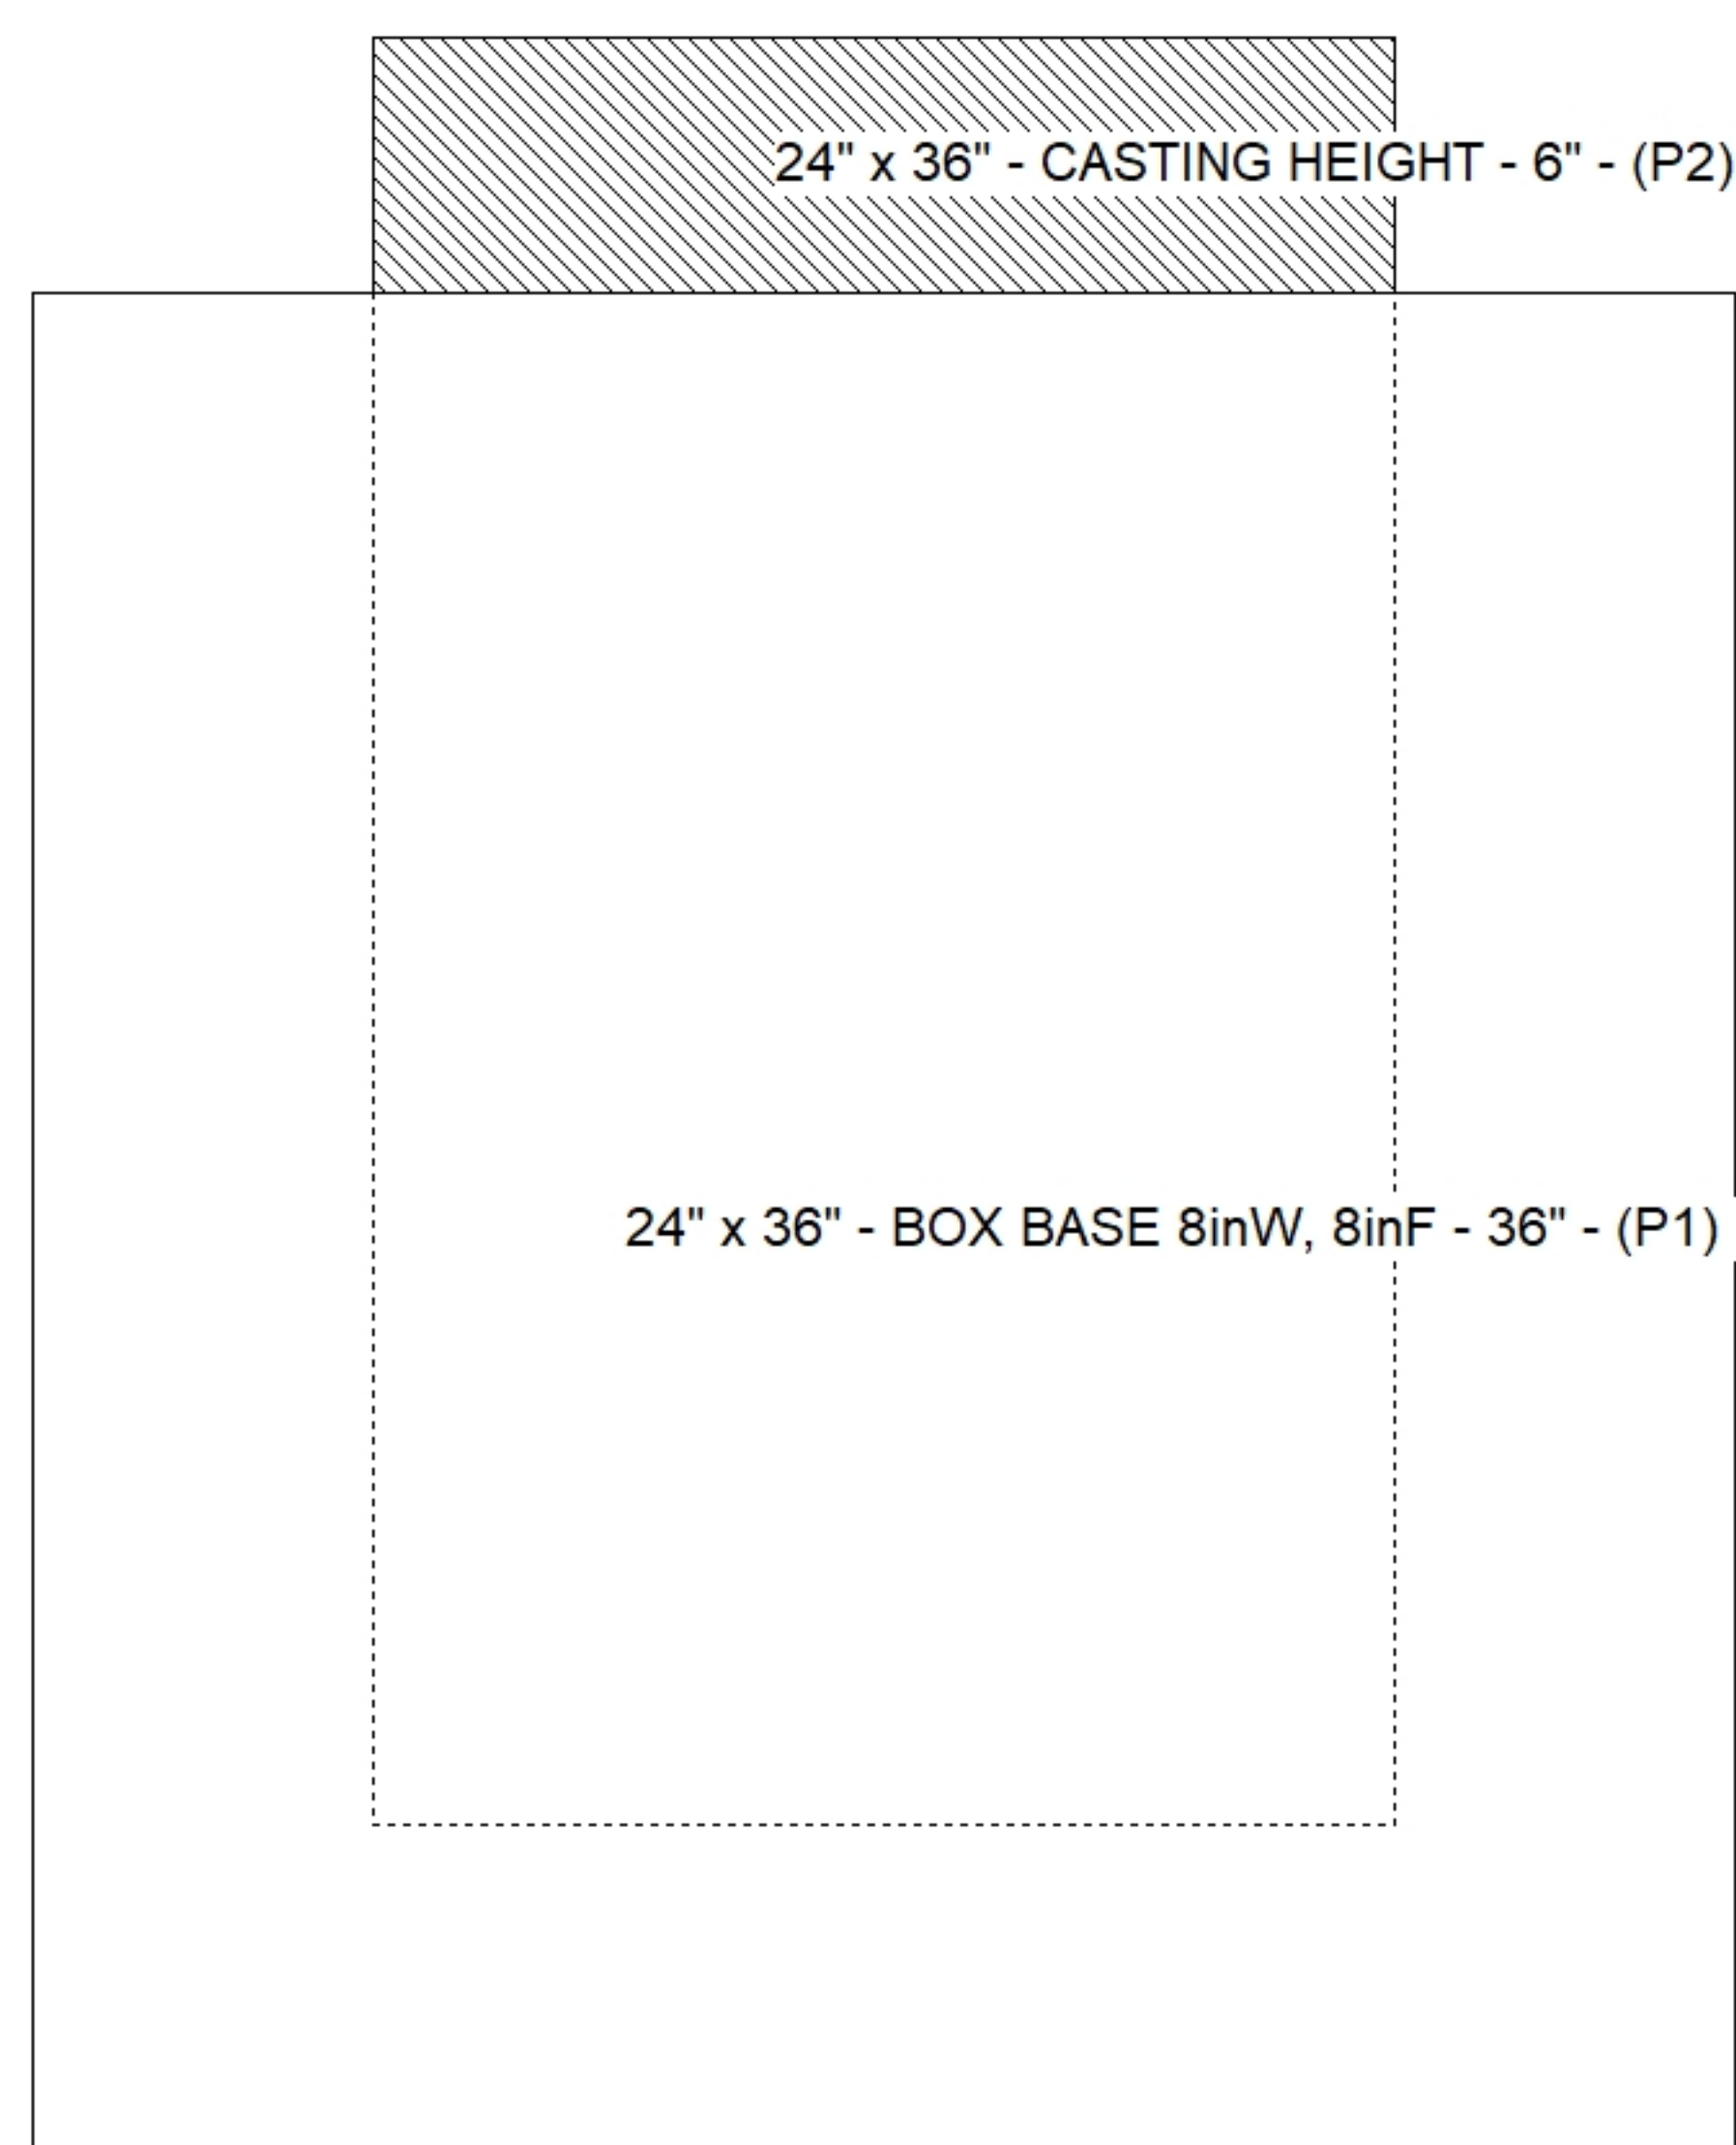

Submittal Drawing
7/22/2026 9:08:34 AM

SUBMITTAL
APPROVED BY:
