

Contractor: Koberstein Contracting, Inc.

Plant: 100



Size: 48"

Rim to Invert: 6.56'

Floor Height: 6"


Slack: 1.72"

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

6) MH Step ML-10-TDS-NCR - 10"



0 lb

Structure Total: 7957 lb

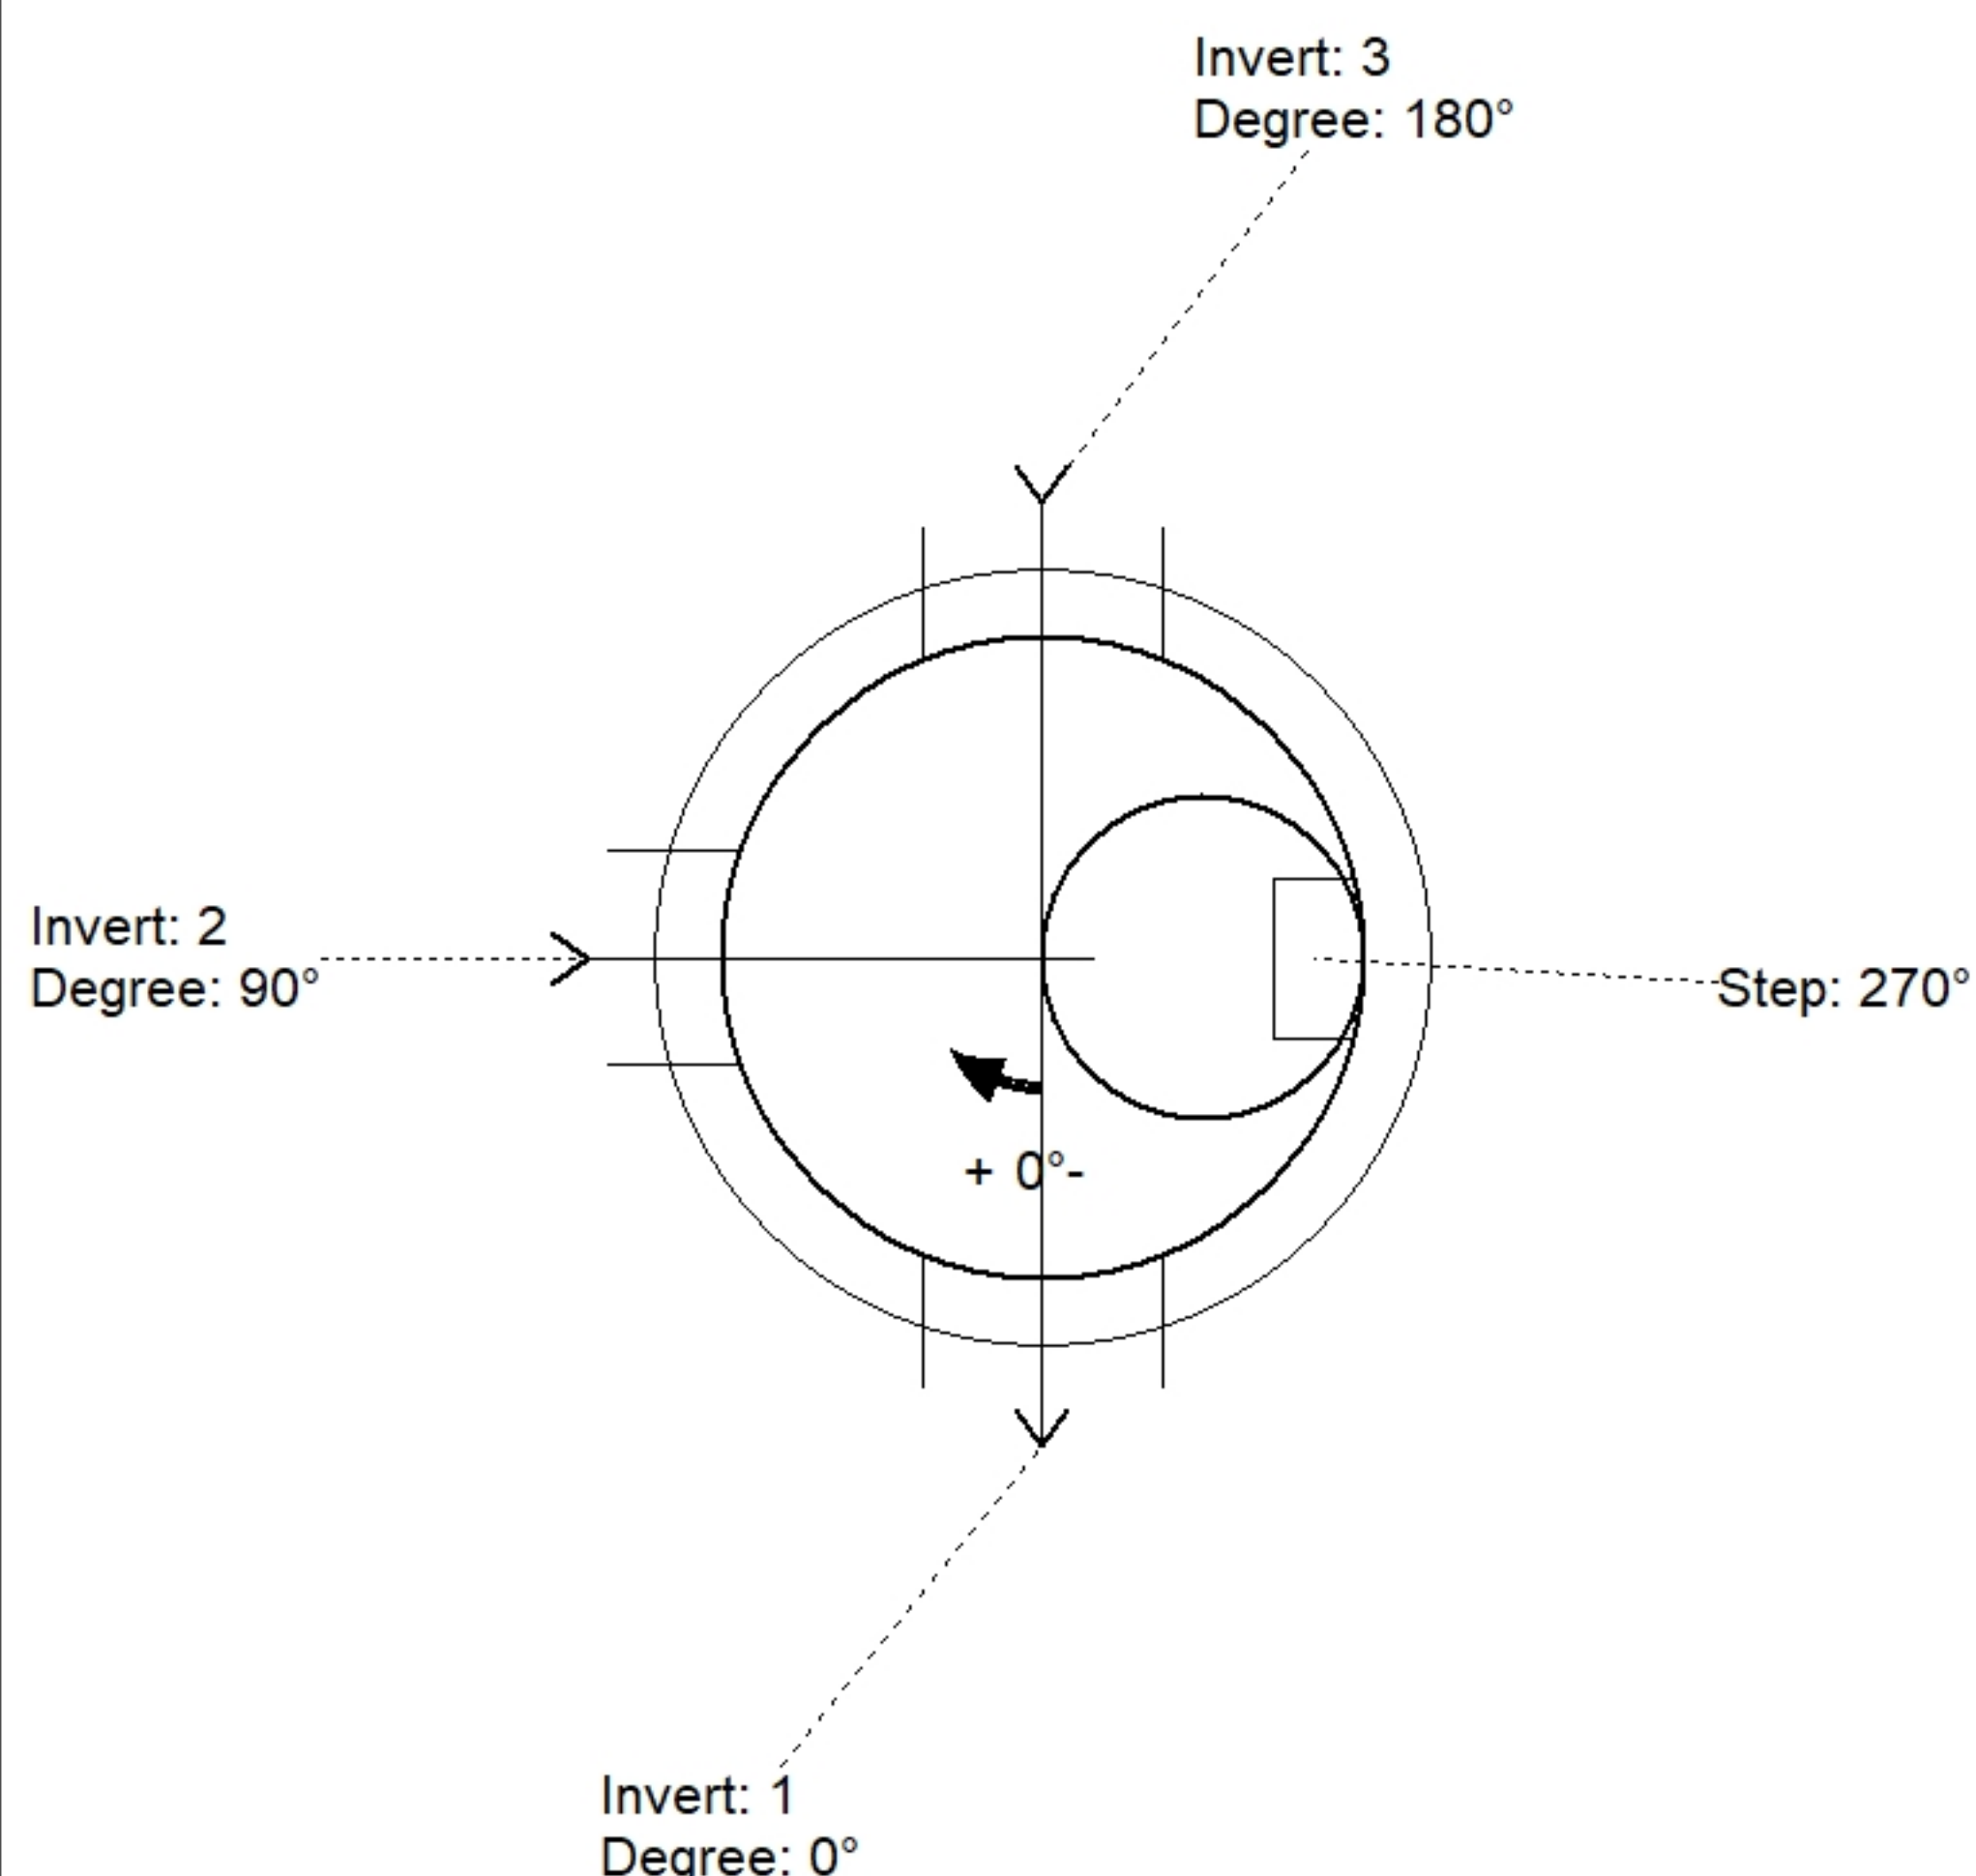

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	394.5'							
Reducer								
Invert 1	387.94'	0°	15" PVC SDR35	15.3"	18"	Kor-N-Seal2 S206-18L	0.5"	P1
Invert 2	388.14'	90°	12" PVC SDR35	12.5"	16"	PSX 16M NYLO	2.4"	P1
Invert 3	388.04'	180°	15" PVC SDR35	15.3"	18"	Kor-N-Seal2 S206-18L	1.7"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

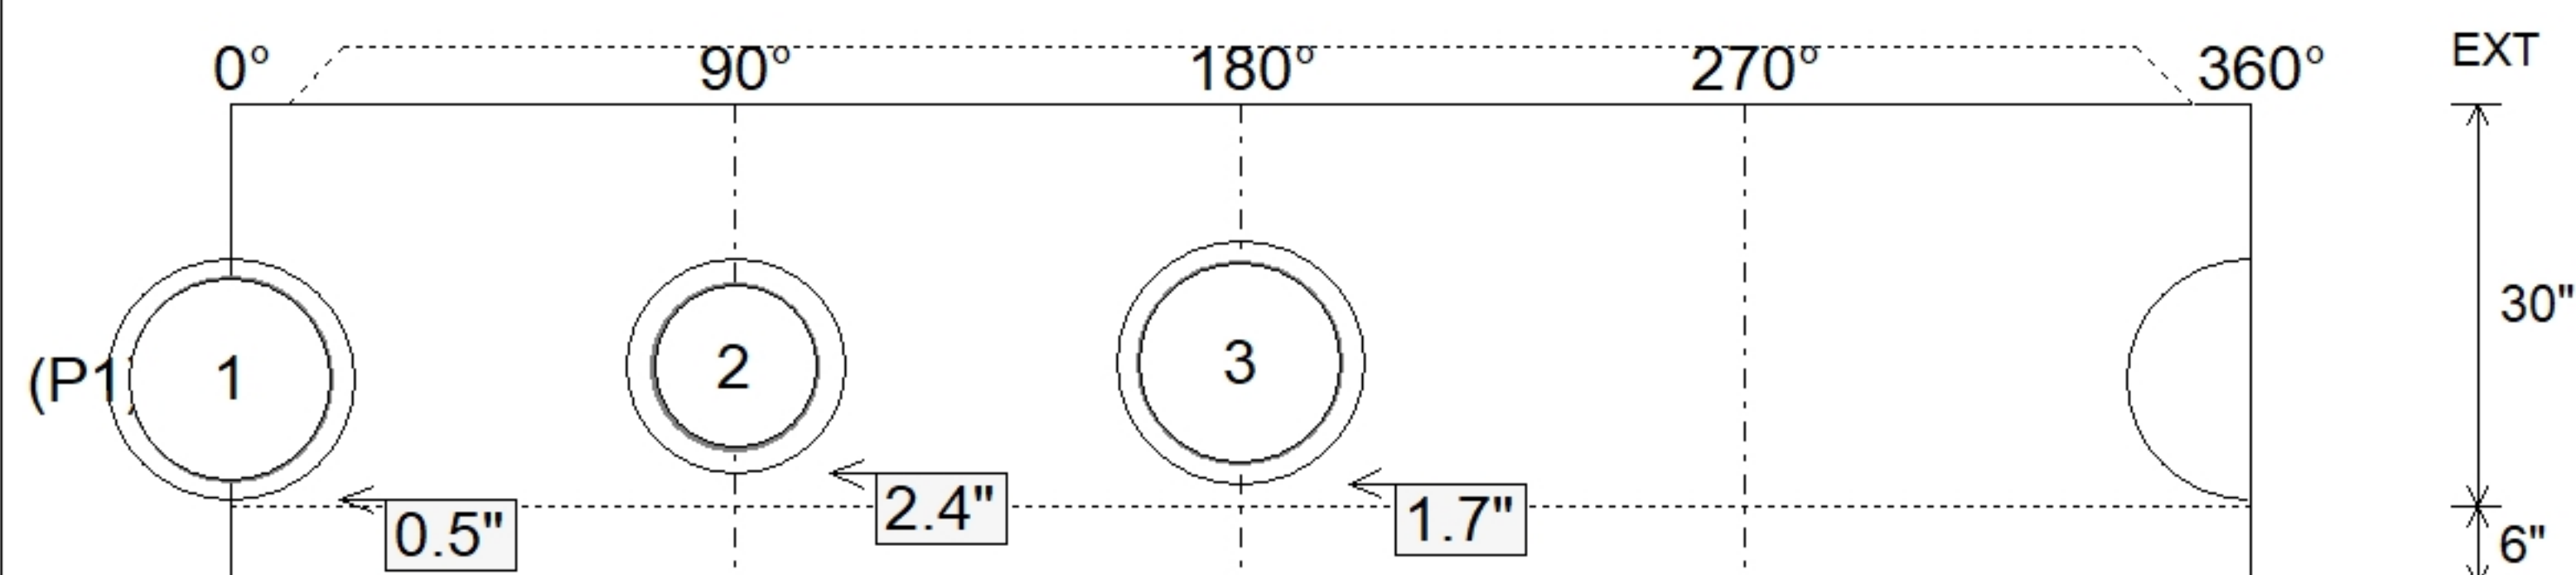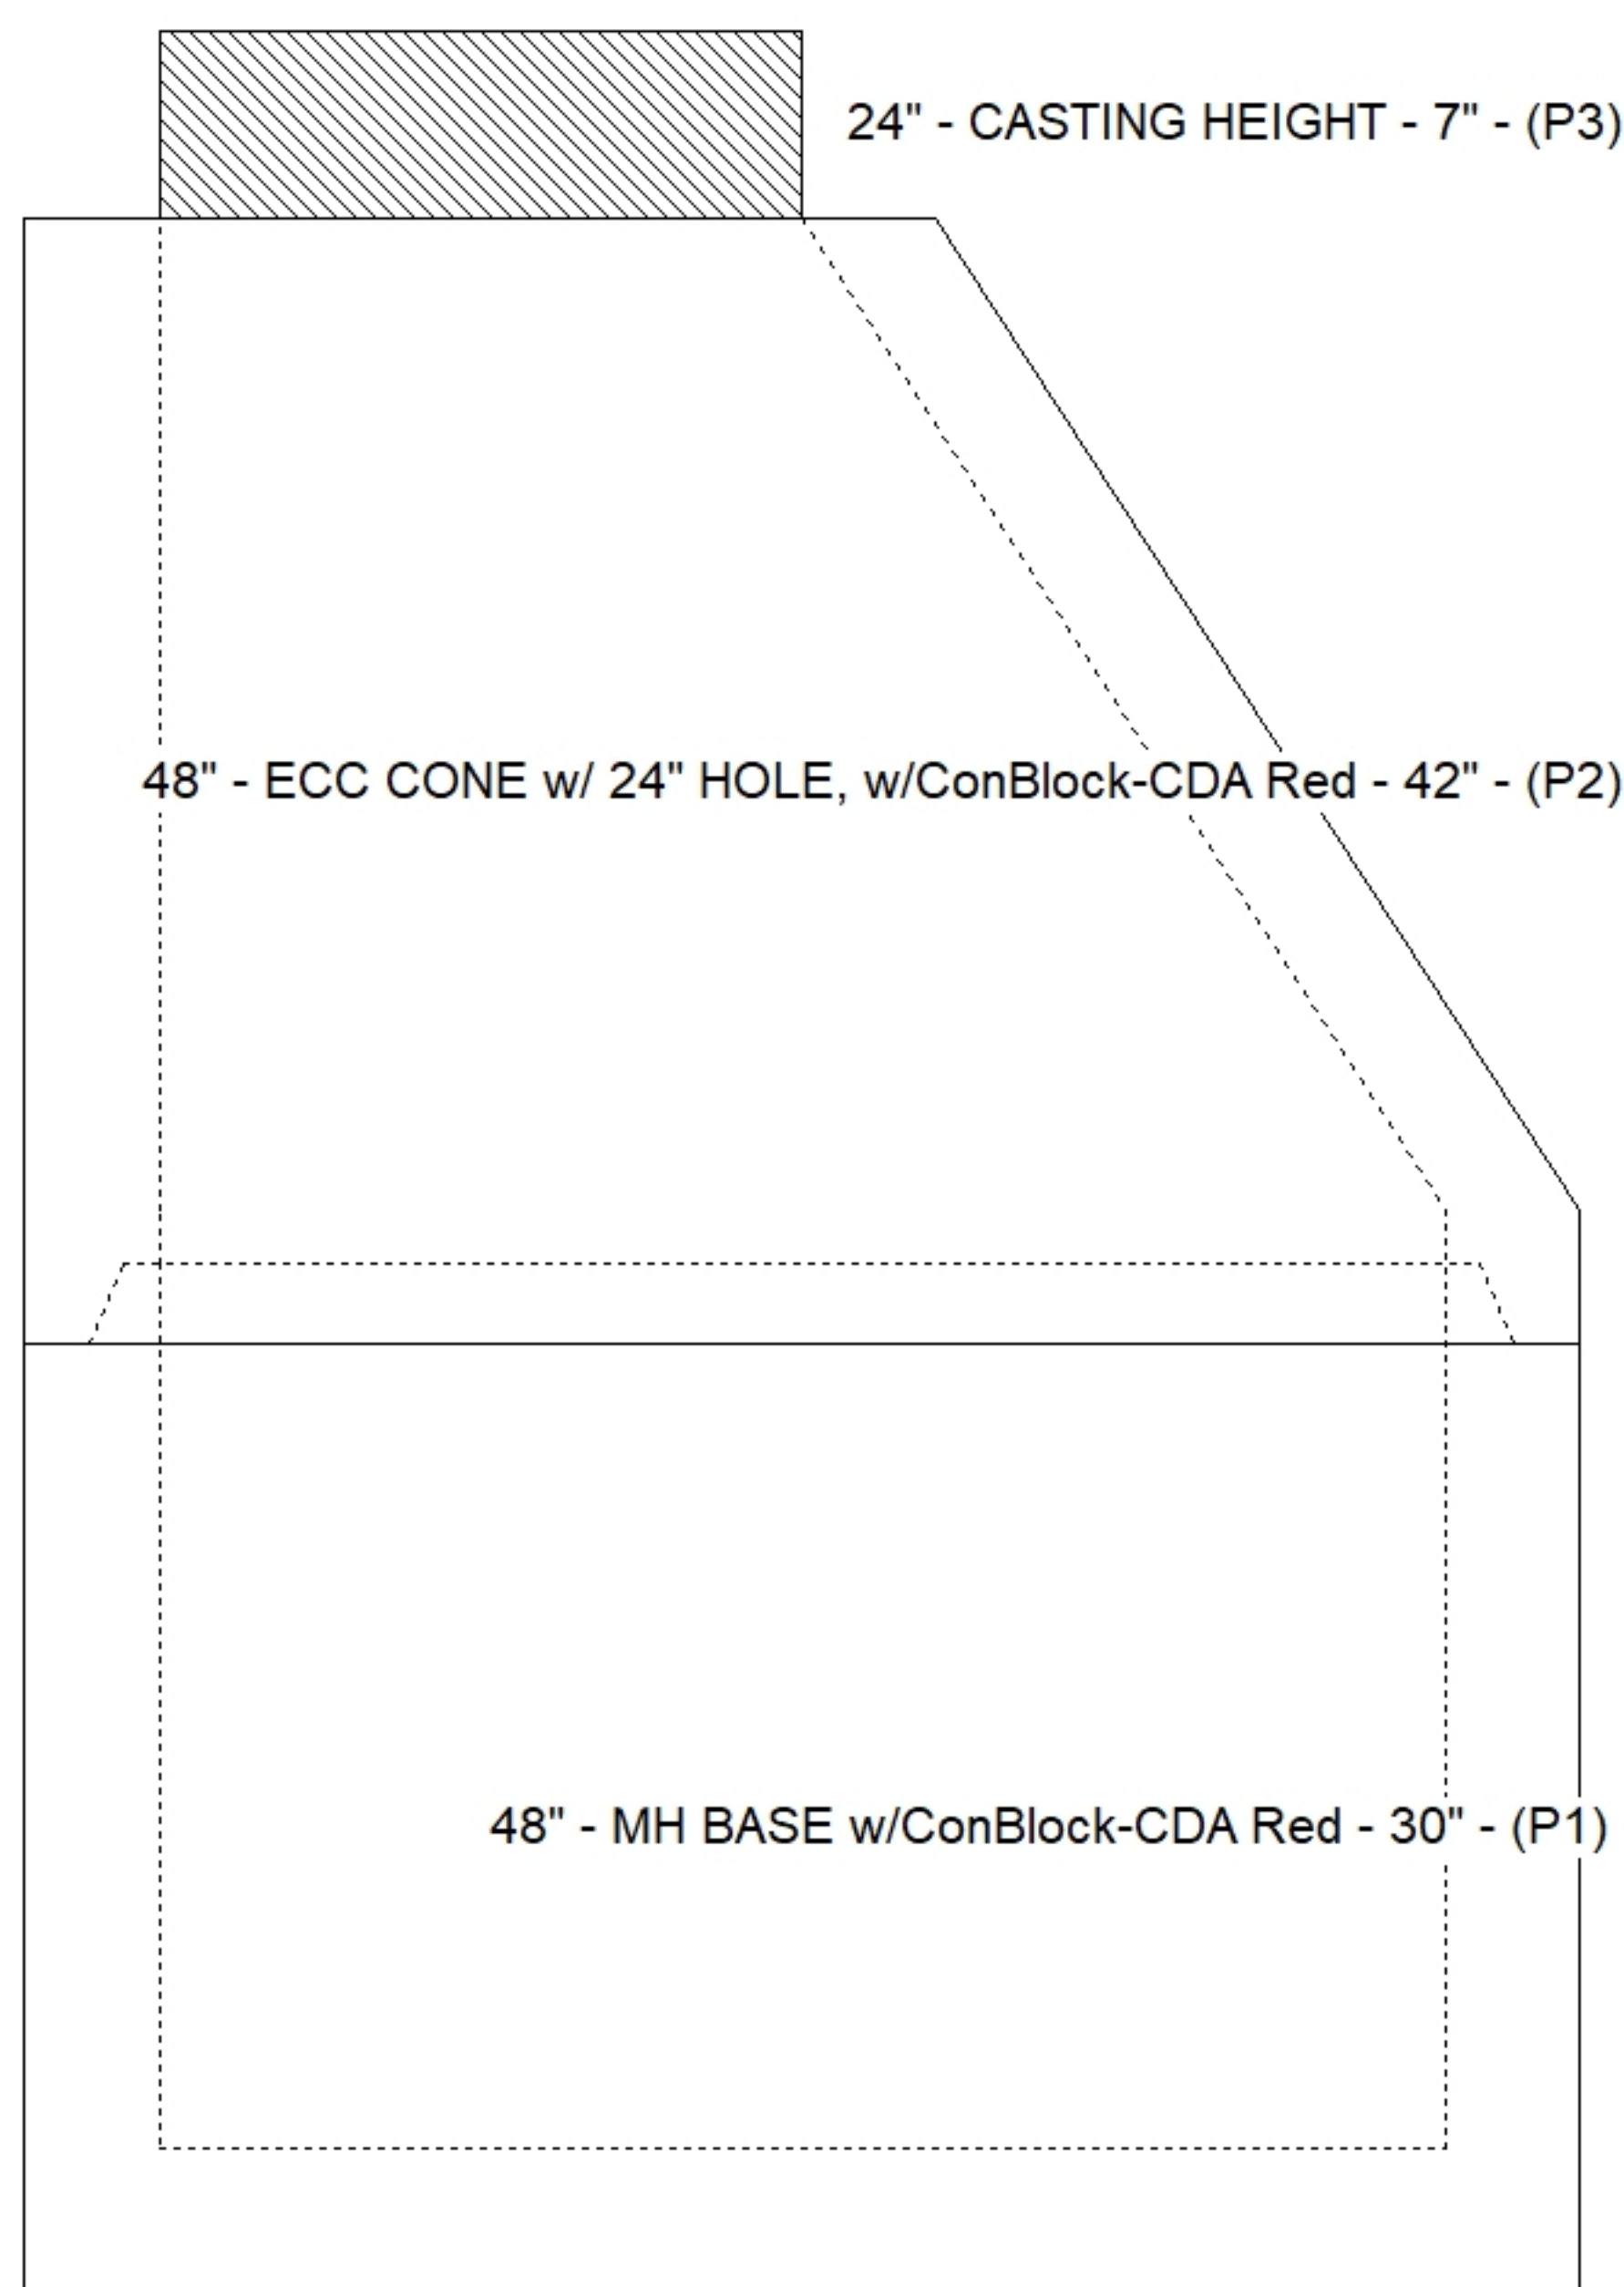

SUBMITTAL
APPROVED BY:
