




Job Name: 26-2513- Stagner Farms Subdivision Sec. 2 Job Location: Bowling Green, KY Contractor: R.A. Alexander & Sons, Inc.					Plant: 100 9/22/2026 8:16:56 AM		Tech: Jared - A PC: Trevor Lewis			
Structure ID: A4 ST-CI										
P1 MH048BA66		MH BASE								
P3) 24" x 36" - CASTING HEIGHT - 6.25" P2) 48" - MH FLAT TOP w/24"x36" Hole - 12" P1) 48" - MH BASE - 66" 1) CASTING - EJ 4510 F/G 1) 48" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 28 1) Hole - 18 5) MH Step ML-10-TDS-NCR - 10"					0 lb 1300 lb 5286 lb 445 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 7031 lb		Structure Notes: 1. EJ 4510 F/G PROVIDED BY ICAST. 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 555.85'		Rim to Invert: 7.07'		Slack: 1.09"		Sump: 0.5"		Step Position: 280°		
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	548.78'	0°	0"	24" CMP	25"	Hole 28	28"	29.896"	0"	0"
Invert 2	548.78'	101°	51.121"	15" CMP	16"	Hole 18	18"	18.451"	0"	0"
Invert 3	548.78'	198°	100.217"	24" CMP	25"	Hole 28	28"	29.896"	0"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

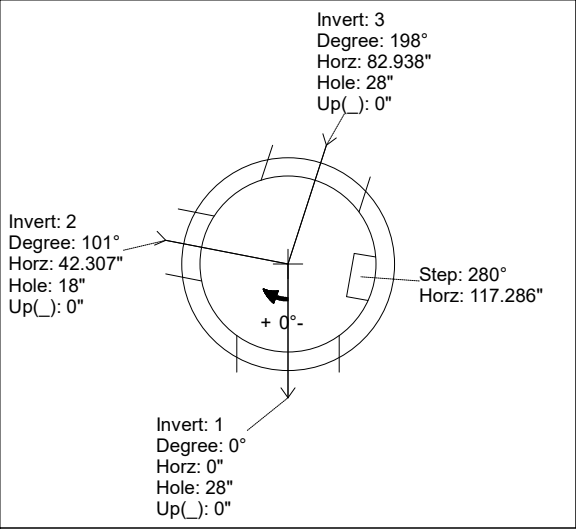

RIGHT-SIDE UP VIEW (int. dimensions)

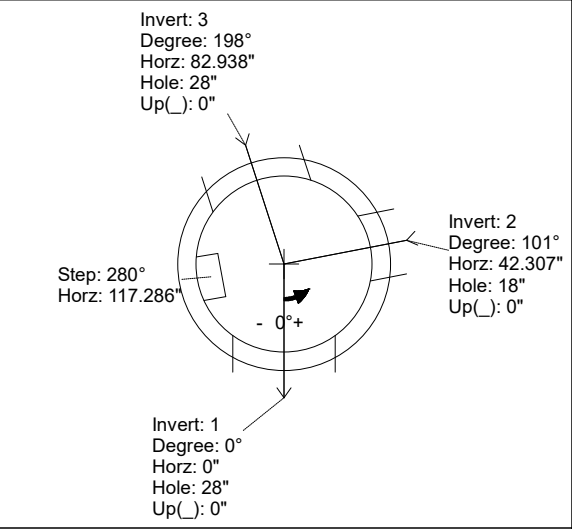

UPSIDE-DOWN VIEW (int. dimensions)

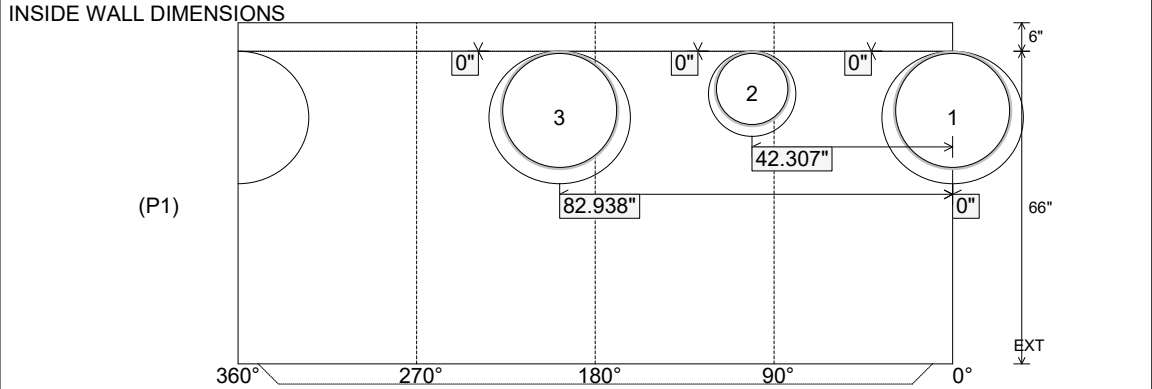

INSIDE WALL DIMENSIONS

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 66" Height (Ext): 72"	Weight (Net): 5286 lb Volume (Net): 1.35cu.yd
----------------------------------	---------------------------------	--	--	--
