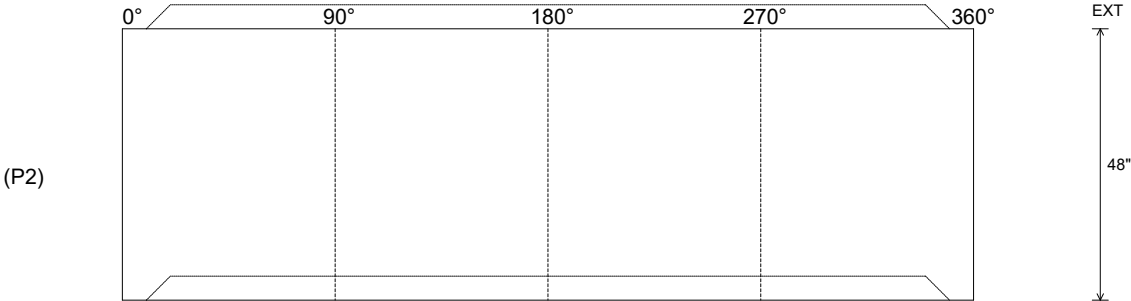


Job Name: 26-2513- Stagner Farms Subdivision Sec. 2 Job Location: Bowling Green, KY Contractor: R.A. Alexander & Sons, Inc.					Plant: 100 9/22/2026 8:20:04 AM		Tech: Jared - A PC: Trevor Lewis				
Structure ID: A6 ST-CI											
P2		MH048RS48		MH RISER							
P4) 24" x 36" - CASTING HEIGHT - 6.25" P3) 48" - MH FLAT TOP w/24"x36" Hole - 12" P2) 48" - MH RISER - 48" P1) 48" - MH BASE - 66" 1) CASTING - HOE MCS-288 F/G Cast-IN 2) 48" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 28 1) Hole - 22 9) MH Step ML-10-TDS-NCR - 10"					0 lb 1300 lb 3353 lb 5231 lb 125 lb 0 lb 0 lb 0 lb 0 lb 0 lb		Structure Notes: . 1. HOE MCS-288B F/G CAST-IN CENTERED PROVIDED BY ICAST. 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Structure Total:					10009 lb						
Rim: 560.61' Rim to Invert: 11.11' Slack: 1.57" Sump: 0.5" Step Position: 70°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)											
											
INSIDE WALL DIMENSIONS											
											
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 5" Floor Height: 0"		Height (Int): 48" Height (Ext): 48"		Weight (Net): 3353 lb Volume (Net): 0.86cu.yd		
