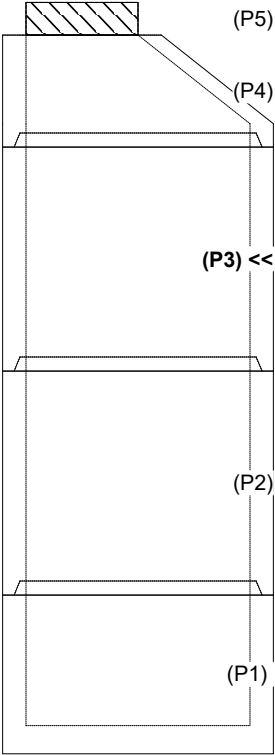

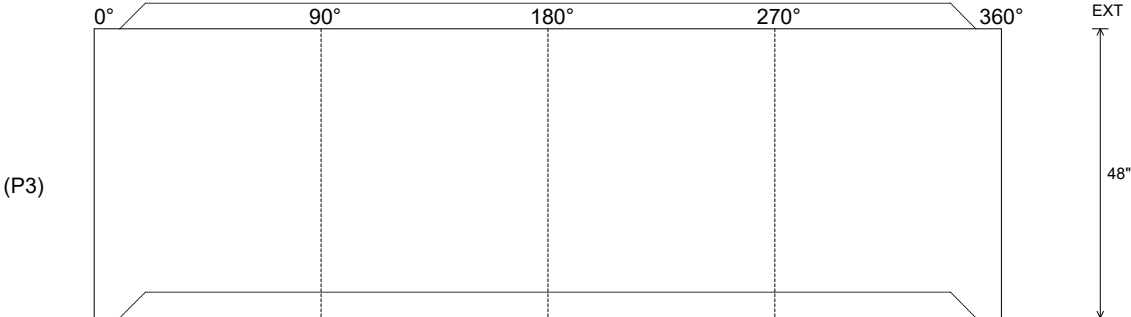


Job Name: 26-2513- Stagner Farms Subdivision Sec. 2 Job Location: Bowling Green, KY Contractor: R.A. Alexander & Sons, Inc.					Plant: 100 8/7/2026 10:23:46 AM		Tech: Jared - A PC: Trevor Lewis						
Structure ID: AA3 SS-MH													
P3			MH048RS48			MH RISER							
P5) 24" - CASTING HEIGHT - 7" P4) 48" - ECC CONE w/ 24" HOLE - 24" P3) 48" - MH RISER - 48" P2) 48" - MH RISER - 48" P1) 48" - MH BASE Custom Ht - 28" 1) JOINT WRAP - 12" WD x 048" MAC WRAP 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-375 F/C Sanitary 3) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) A-Lok - 0285 12) MH Step ML-10-TDS-NCR - 10"						0 lb 1550 lb 3353 lb 3353 lb 3223 lb 0 lb 1440 lb 271 lb 0 lb 0 lb 2 lb 0 lb		Structure Notes: . 1. HOE MC-375 F/C SANITARY PROVIDED BY ICAST. 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.					
Rim: 561.5' Rim to Invert: 12.77' Slack: 0.24" Sump: 2" Step Position: 0						Structure Total: 13193 lb							
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset			
Invert 1													
Invert 2													
Invert 3													
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													
RIGHT-SIDE UP VIEW (int. dimensions)													
													
INSIDE WALL DIMENSIONS													
													
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 5" Floor Height: 0"		Height (Int): 48" Height (Ext): 48"		Weight (Net): 3353 lb Volume (Net): 0.86cu.yd				
