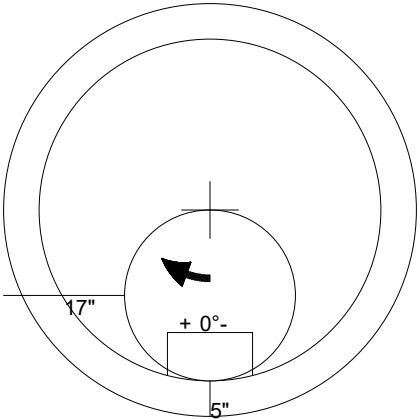



Job Name: 26-2513- Stagner Farms Subdivision Sec. 2 Job Location: Bowling Green, KY Contractor: R.A. Alexander & Sons, Inc.		Plant: 100 8/7/2026 10:22:07 AM	Tech: Jared - A PC: Trevor Lewis	
Structure ID: BB2 SS-MH				
P3 MH048CN24		ECC CONE w/ 24" HOLE		
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE - 24" P2) 48" - MH RISER - 48" P1) 48" - MH BASE Custom Ht - 29" 1) JOINT WRAP - 12" WD x 048" MAC WRAP 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-375 F/C Sanitary 2) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) A-Lok - 0285 8) MH Step ML-10-TDS-NCR - 10"		0 lb 1550 lb 3353 lb 3293 lb 0 lb 1440 lb 271 lb 0 lb 0 lb 0 lb 2 lb 0 lb ----- 9909 lb Structure Total:	<u>Structure Notes:</u> . 1. HOE MC-375 F/C SANITARY PROVIDED BY ICAST. 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.	
				
				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 24"	Weight (Net): 1550 lb Volume (Net): 0.33cu.yd
