




Job Name: 26-2513- Stagner Farms Subdivision Sec. 2 Job Location: Bowling Green, KY Contractor: R.A. Alexander & Sons, Inc.					Plant: 100 9/22/2026 8:17:04 AM		Tech: Jared - A PC: Trevor Lewis			
Structure ID: C2 ST-CB										
P1 MH048BAVF		MH BASE Custom Ht								
P3) 24" - CASTING (cast in) - 4" P2) 48" - MH MONOTOP W/ MCS-288 CAST IN, Custom Ht - 38" P1) 48" - MH BASE Custom Ht - 25" 1) CASTING - HOE MCS-288 F/G Cast-IN 1) 48" - Conseal CS-102 1.00" 1) 24" - Conseal CS-102 1.00" 1) Hole - 22 1) Vert. Slot - 4"x8" 4) Weir - 30"x6"						0 lb 3003 lb 2912 lb 125 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 6040 lb		Structure Notes: . 1. HOE MCS-288B F/G CAST-IN CENTERED PROVIDED BY ICAST. 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.		
Rim: 554'		Rim to Invert: 5.26'		Slack: 0.62"		Sump: 0.5"		Step Position:		
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1	548.74'	0°	0"	18" CMP	19"	Hole 22	22"	22.854"	0"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

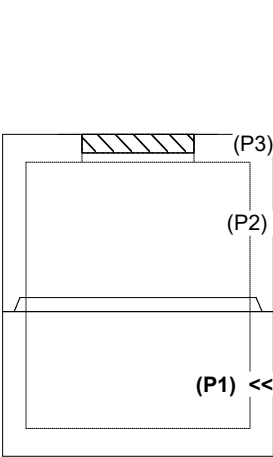

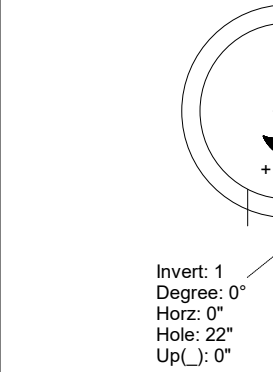



Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 25" Height (Ext): 31"	Weight (Net): 2912 lb Volume (Net): 0.74cu.yd
----------------------------------	---------------------------------	--	--	--
