

Job Name: 26-2560 Ashtree Subdivision Unit 3 Ph. 1  
Job Location: Nicholasville, KY  
Contractor: The Allen Company, Inc.

Plant: Beaver Dam  
8/24/2026 8:11:58 AM

Tech: J. ROSS  
PC: E. BRADLEY



## Structure ID: AA2 ST-MH

**P3 GR4**

### GRADE RING

P4) 24" - CASTING HEIGHT - 7"  
P3) 24" - GRADE RING - 4"  
P2) 48" - MH FLAT TOP w/ 24" ECC Hole - 12"  
P1) 48" - MH BASE - 24"  
1) CASTING - HOE MC-315 F/C Storm  
1) 48" - Con Seal CS-102 1.00"  
2) 24" - Con Seal CS-102 1.00"  
2) Hole - 22

Structure Total:


0 lb  
270 lb  
1561 lb  
2678 lb  
258 lb  
0 lb  
0 lb  
0 lb  
-----  
4767 lb

#### Structure Notes:


1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. REINFORCING PER ASTM A615 (GRADE 60).
  - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
  - RISER/WALLS (As .12)
  - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.
4. \*\*NO STEPS\*\*
5. CASTING BY OTHERS

#### NOTES:


1. GRADE RINGS MEET OR EXCEED THE FOLLOWING SPECIFICATIONS:
  - CONCRETE: 4,000 PSI @ 28 DAYS.
  - REINFORCING: (1) #3 HOOP CENTERED (GRADE 60)
2. WEIGHT: 4" 270 Lbs.

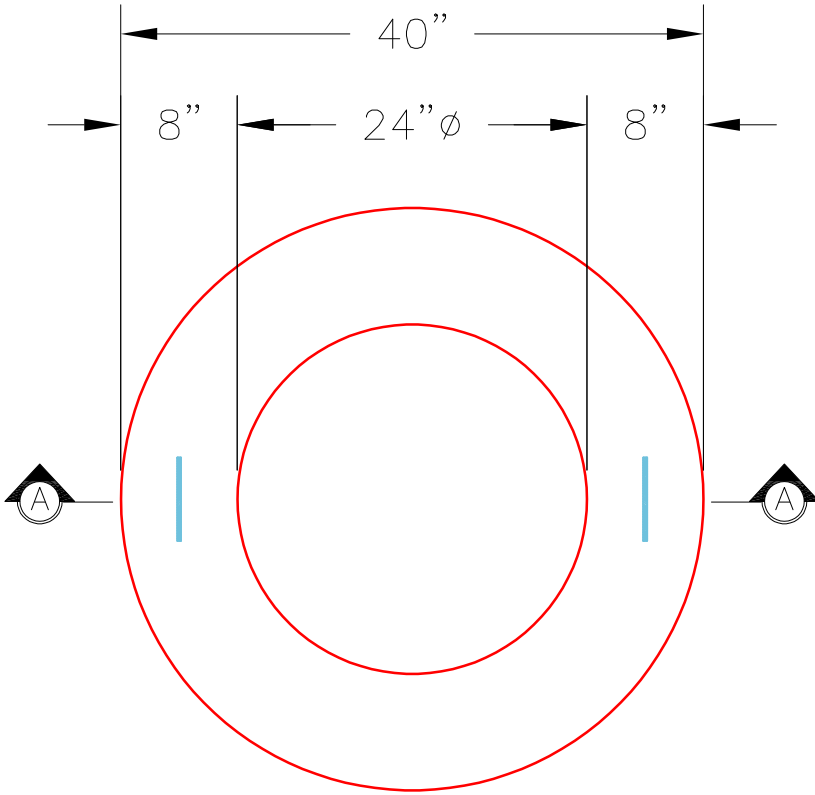

**PLAN VIEW**

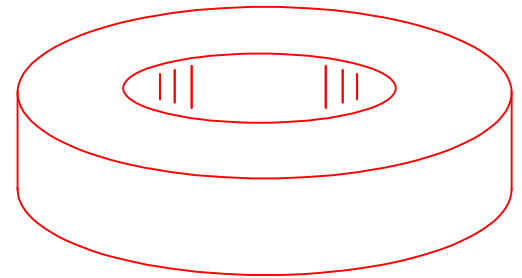

**ISOMETRIC VIEW**

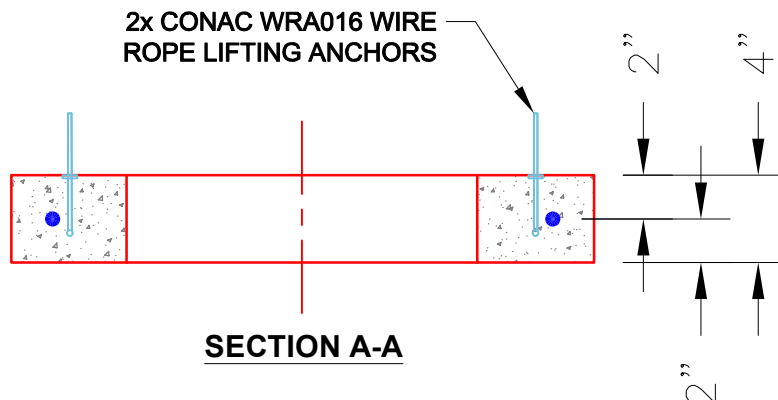

**SECTION A-A**

Coating (Int):  
Coating (Ext):

Seam Up: Flat  
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 4"

Weight (Net): 270 lb  
Volume (Net): 0.07cu.yd
