

Contractor: The Allen Company, Inc.

Plant: Beaver Dam



Size: 48"

Rim to Invert: 6.26'

Floor Height: 6"


Slack: 0.12"

1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. REINFORCING PER ASTM A615 (GRADE 60).
 - CONE (As .12)
 - RISER/WALLS (As .12)
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.
4. CASTING BY OTHERS
5. ADMIXTURE = CONBLOCK-CDA RED


6) MH Step ML-10-TDS-NCR - 10"

0 lb


Structure Total: 7695 lb

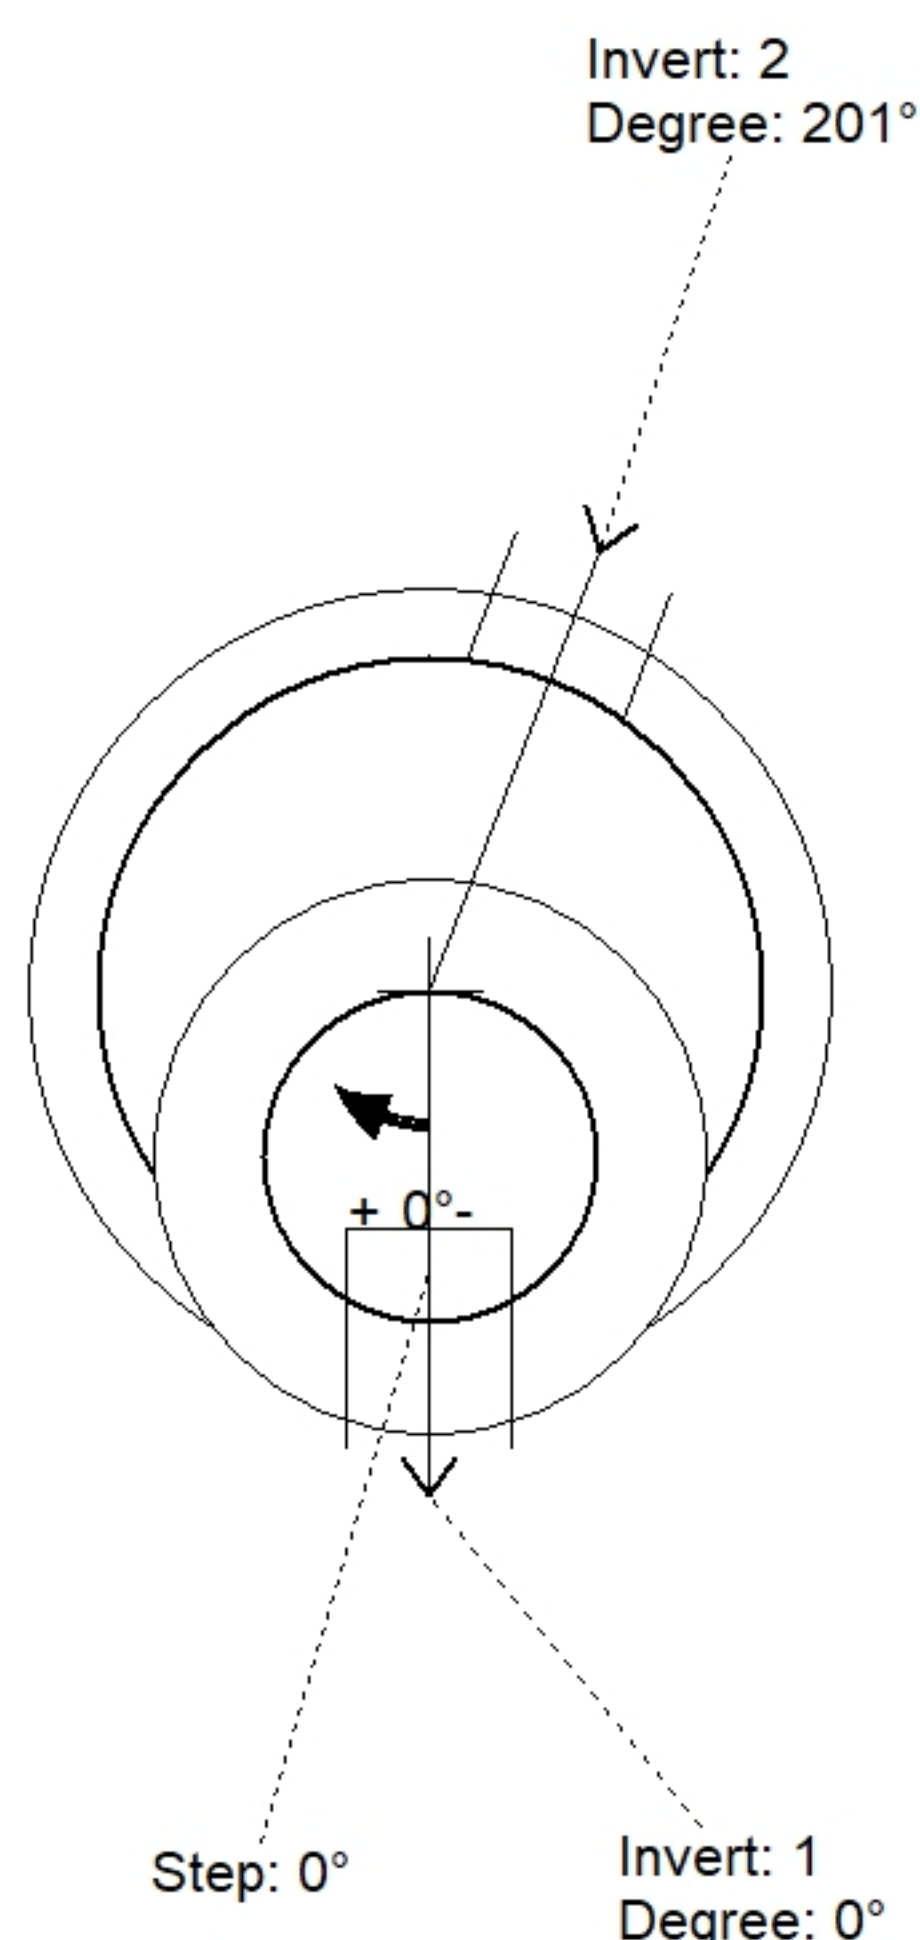

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	929.1'							
Reducer								
Invert 1	922.84'	0°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	0"	P1
Invert 2	924.14'	201°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	15.6"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

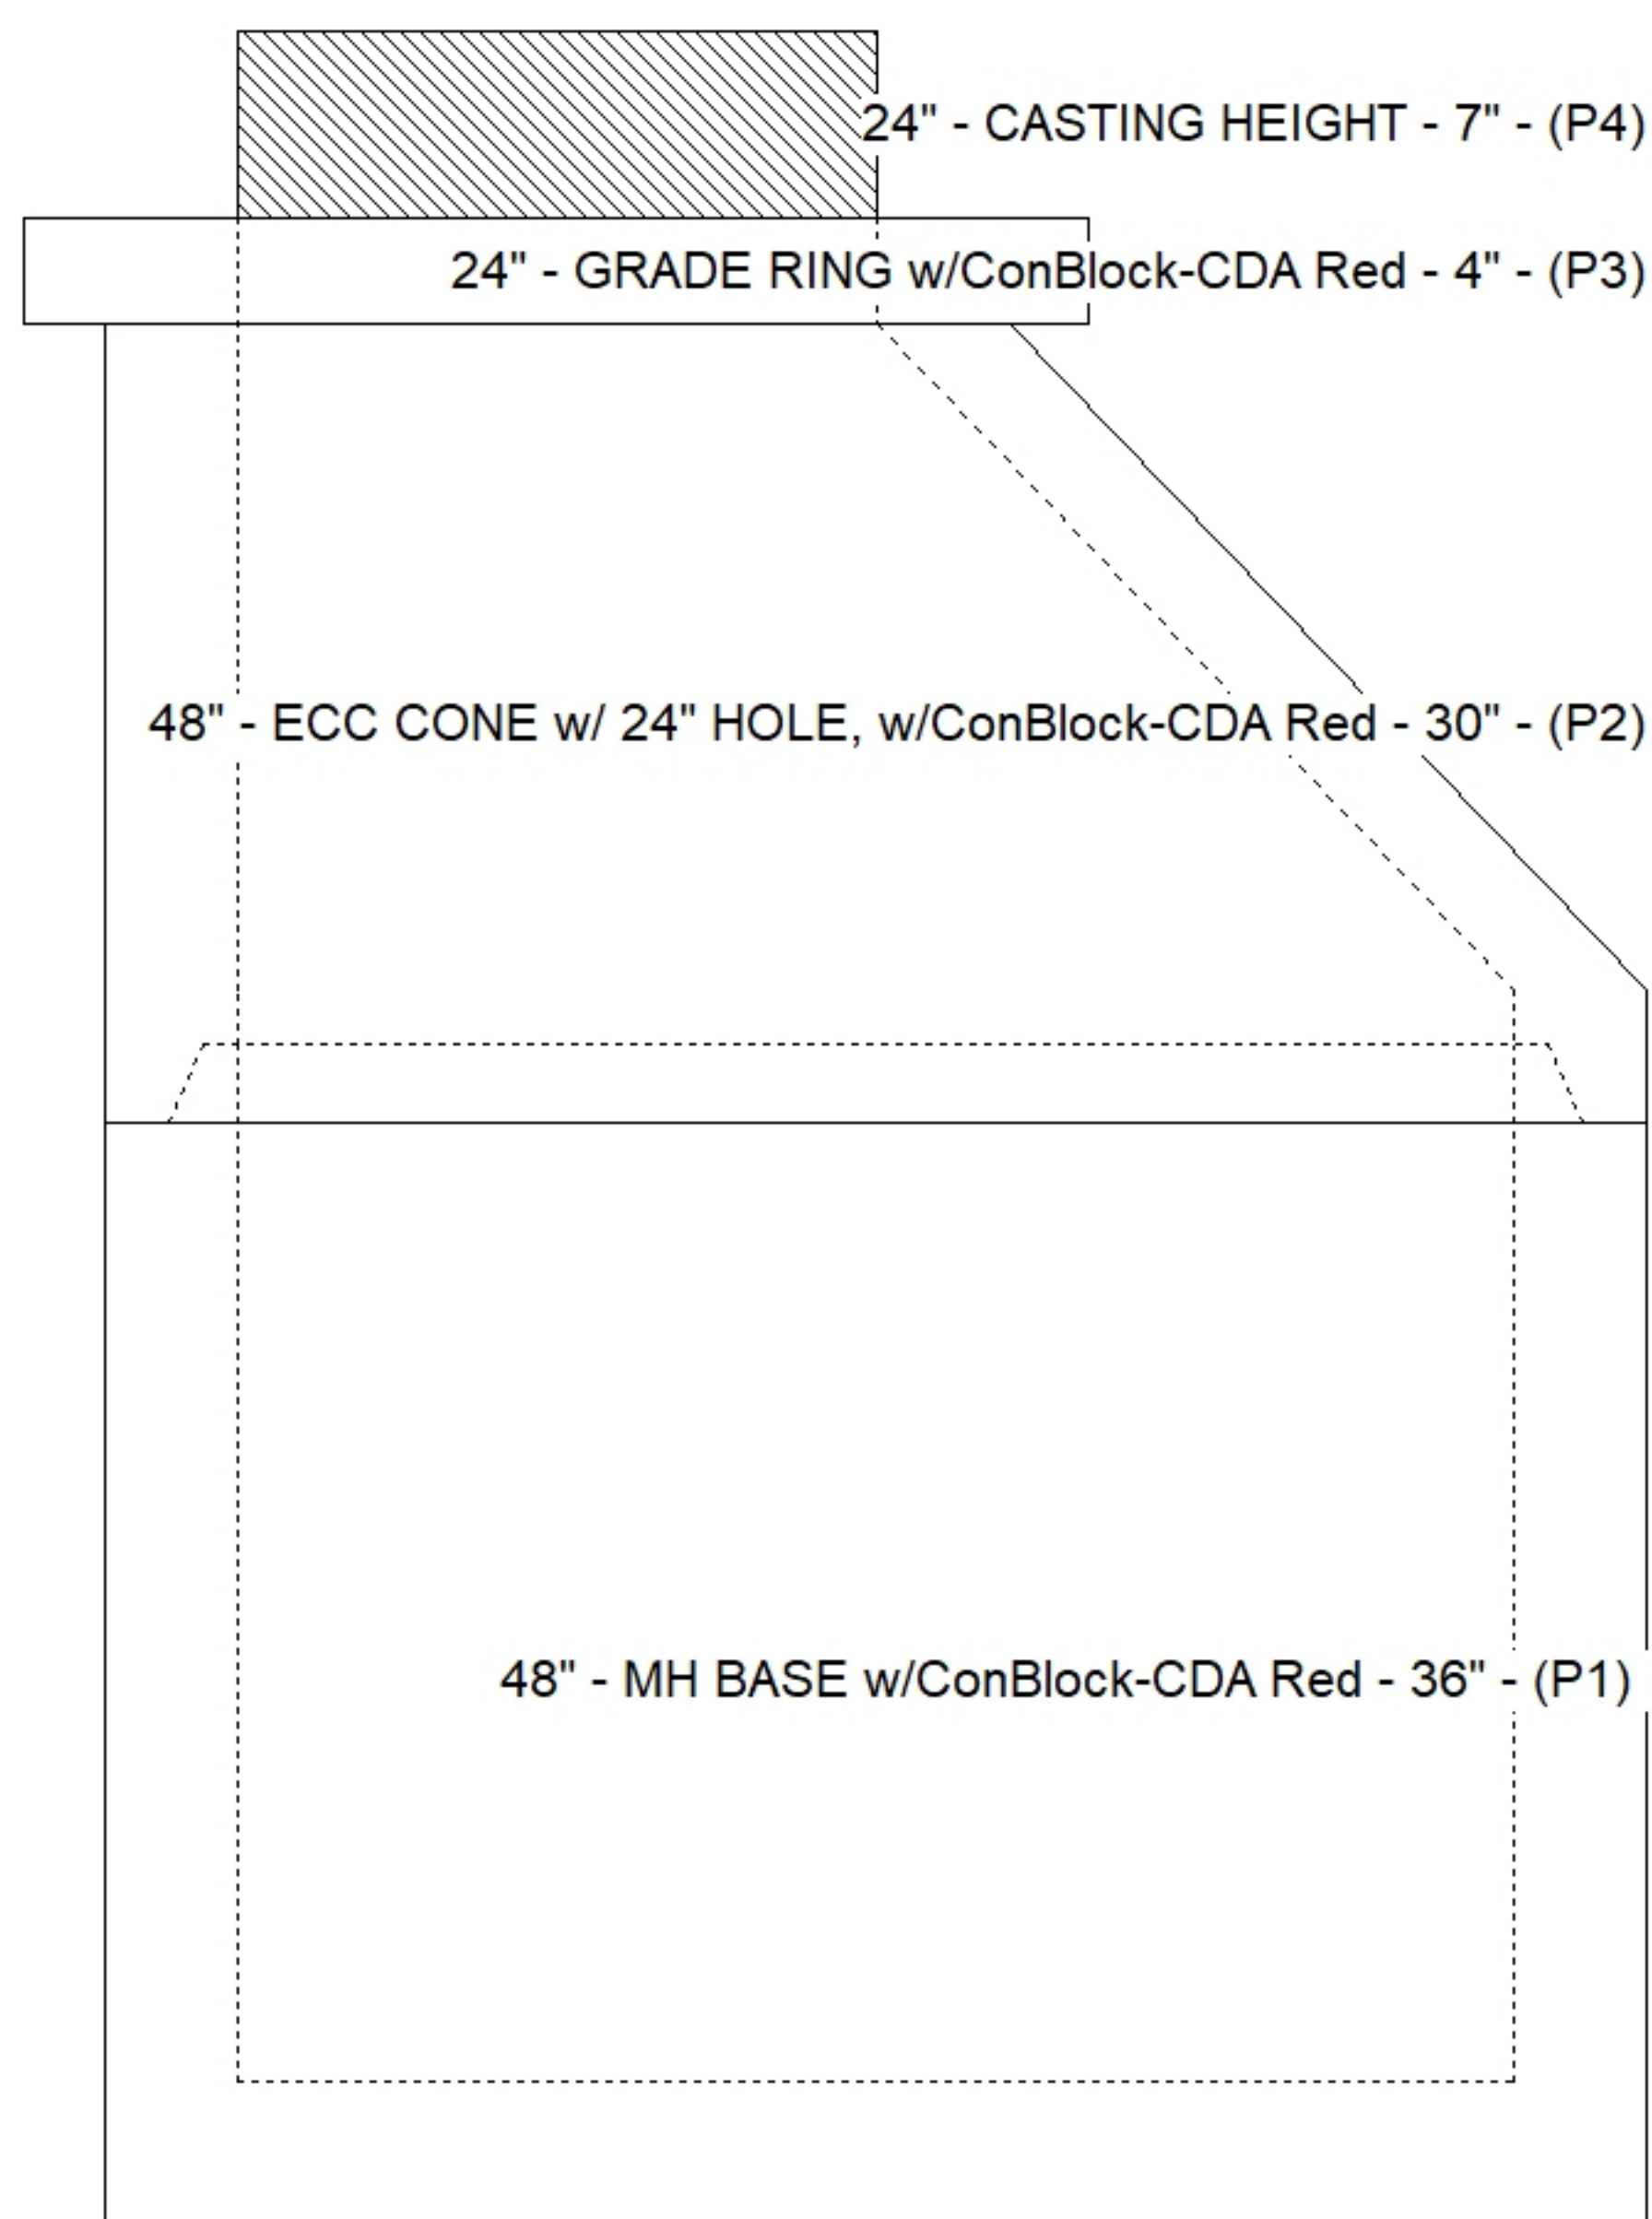

Default - Interior Dimensions

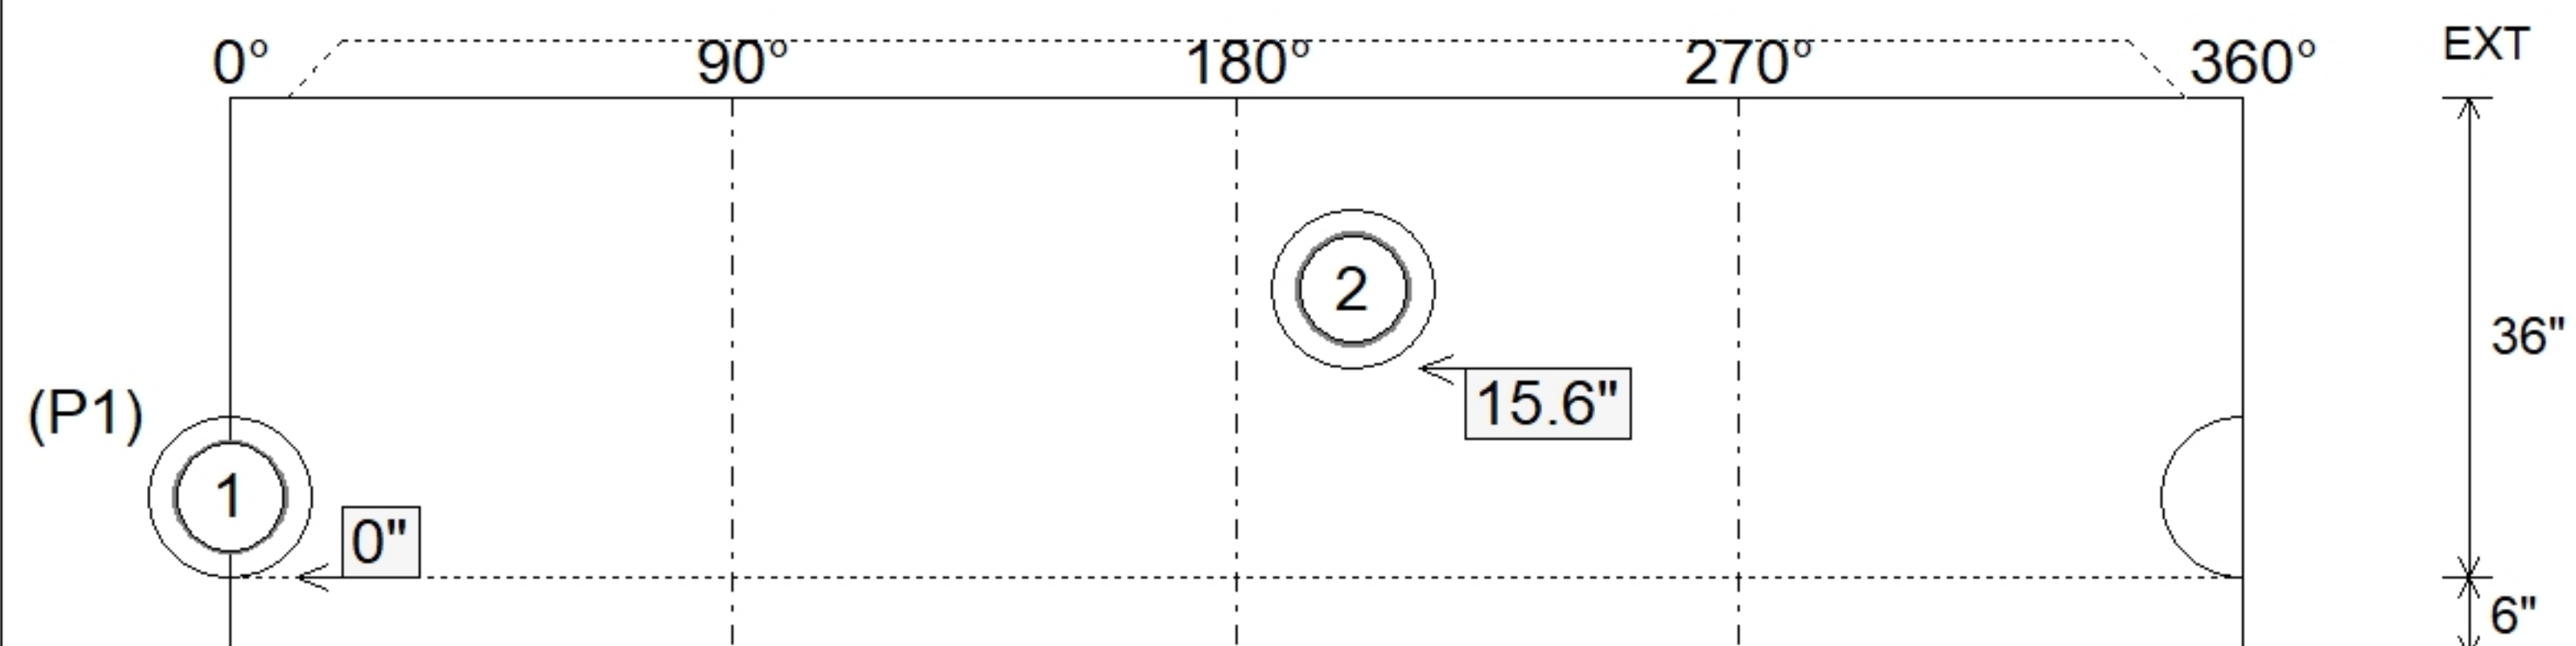

SUBMITTAL
APPROVED BY:
