



Job Name: 26-2560 Ashtree Subdivision Unit 3 Ph. 1 Job Location: Nicholasville, KY Contractor: The Allen Company, Inc.					Plant: Beaver Dam 8/24/2026 8:08:21 AM		Tech: J. ROSS PC: E. BRADLEY				
Structure ID: EE3 LEXA											
P1 BX3636-08BA30 BOX BASE 8inW, 8inF											
P3) 36" x 120" - CB INLET LEX A 10' TOP SAG - 12" P2) 36" x 120" - CB INLET LEX A 10' BOTTOM SAG - 18" P1) 36" x 36" - BOX BASE 8inW, 8inF - 30" 1) CASTING - HOE KY-206 F/C (KY CBI A) 1) 36" x 36" - Conseal CS-102 1.00" 2) Hole - 22 1) Hole - 6 4) MH Step ML-10-TDS-NCR - 10"						2700 lb 3650 lb 4830 lb 206 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 11386 lb		Structure Notes: - PER ASTM C913 SPECIFICATIONS. - CONCRETE = 4,000 PSI AT 28 DAYS. - REINFORCING PER ASTM A615 (GRADE 60). - TOP PHASE TOP - #5 BARS AT 6" C.C.E.W. - TOP PHASE BTM - #5 BARS AT 12" C.C.E.W. - TOP SLAB - #5 BARS AT 12" C.C.E.W.. - RISER/WALLS - #5 BARS AT 12" C.C.E.W. - FLOOR - #5 BARS AT 12" C.C.E.W. - HOE KY-206 F/C CASTING PROVIDED BY ICAST			
Rim: 956'		Rim to Invert: 5.3'		Slack: 3.6"		Sump: 0"		Step Position: 0°			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1	950.7'	0°	26"	15" RCP B WALL	19.5"	Hole 22	22"	22"	-3.5"	0"	
Invert 2	950.8'	270°	26"	15" RCP B WALL	19.5"	Hole 22	22"	22"	-2.3"	0"	
Invert 3	952.45'	180°	26"	4" HDPE	4.8"	Hole 6	6"	6"	20"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

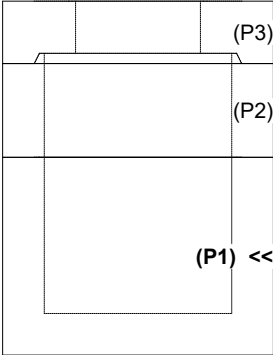


(P1) <<


RIGHT-SIDE UP VIEW (int. dimensions)

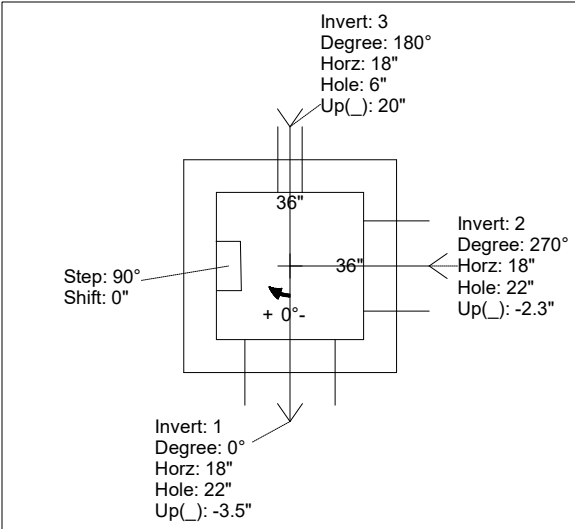

UPSIDE-DOWN VIEW (int. dimensions)

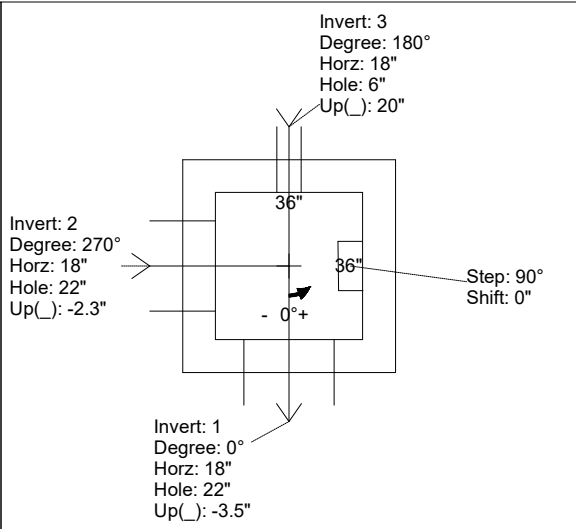

INSIDE WALL DIMENSIONS

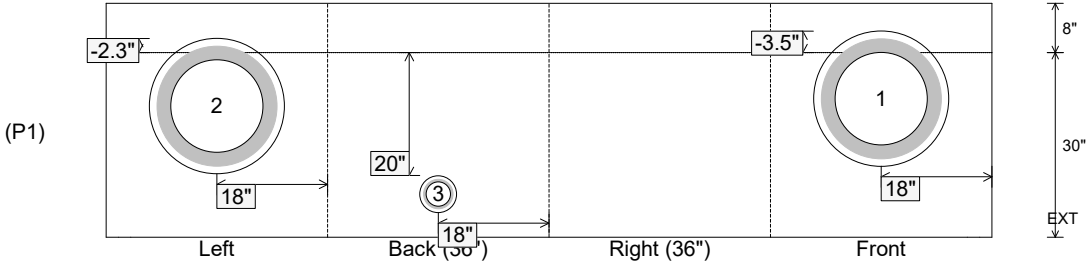

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 30" Height (Ext): 38"	Weight (Net): 4830 lb Volume (Net): 1.23cu.yd
----------------------------------	-------------------------------	--	--	--
