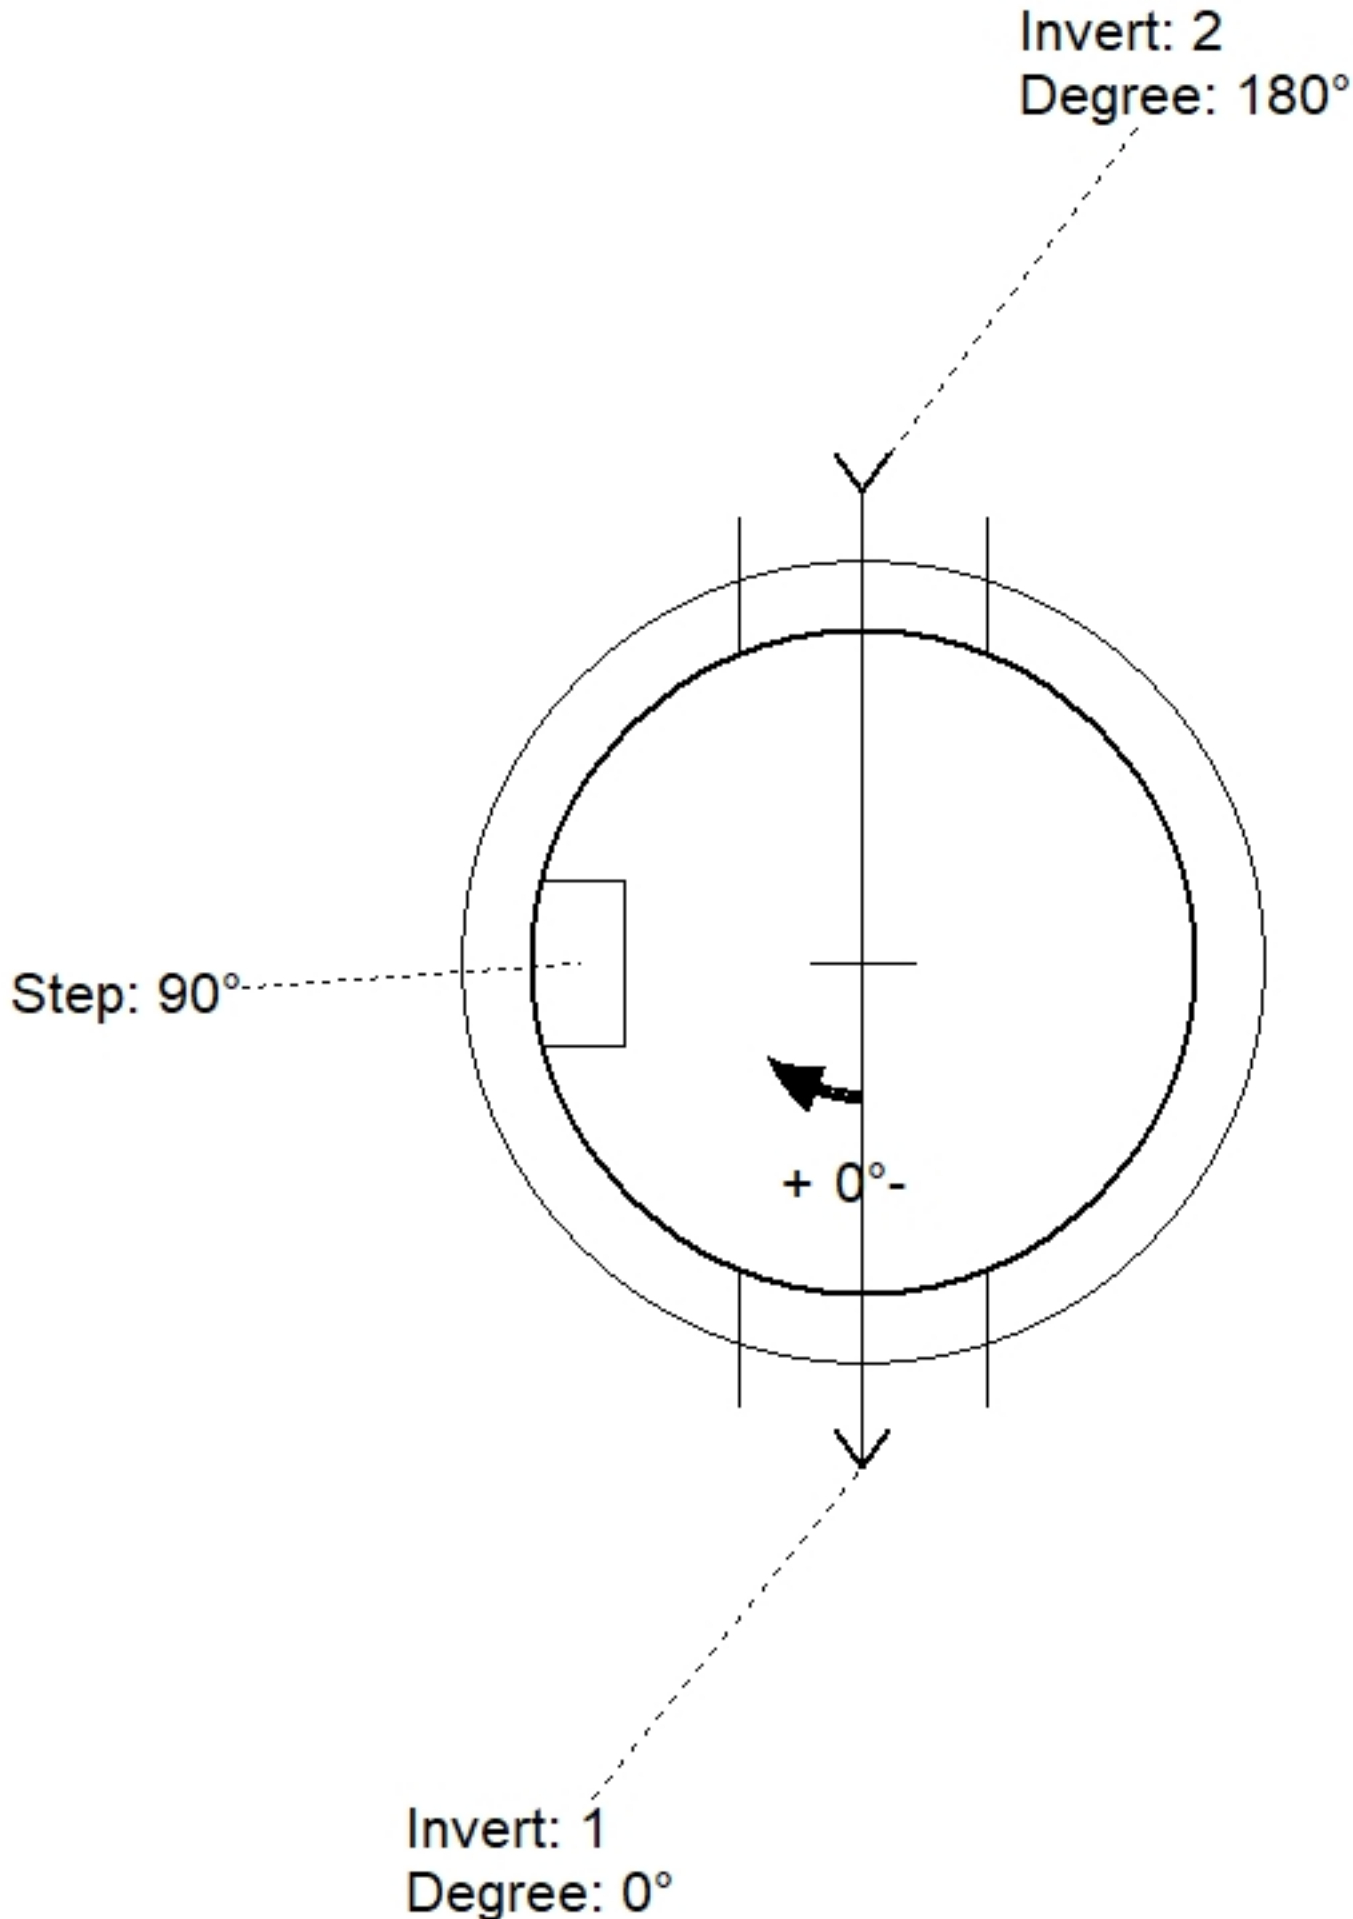
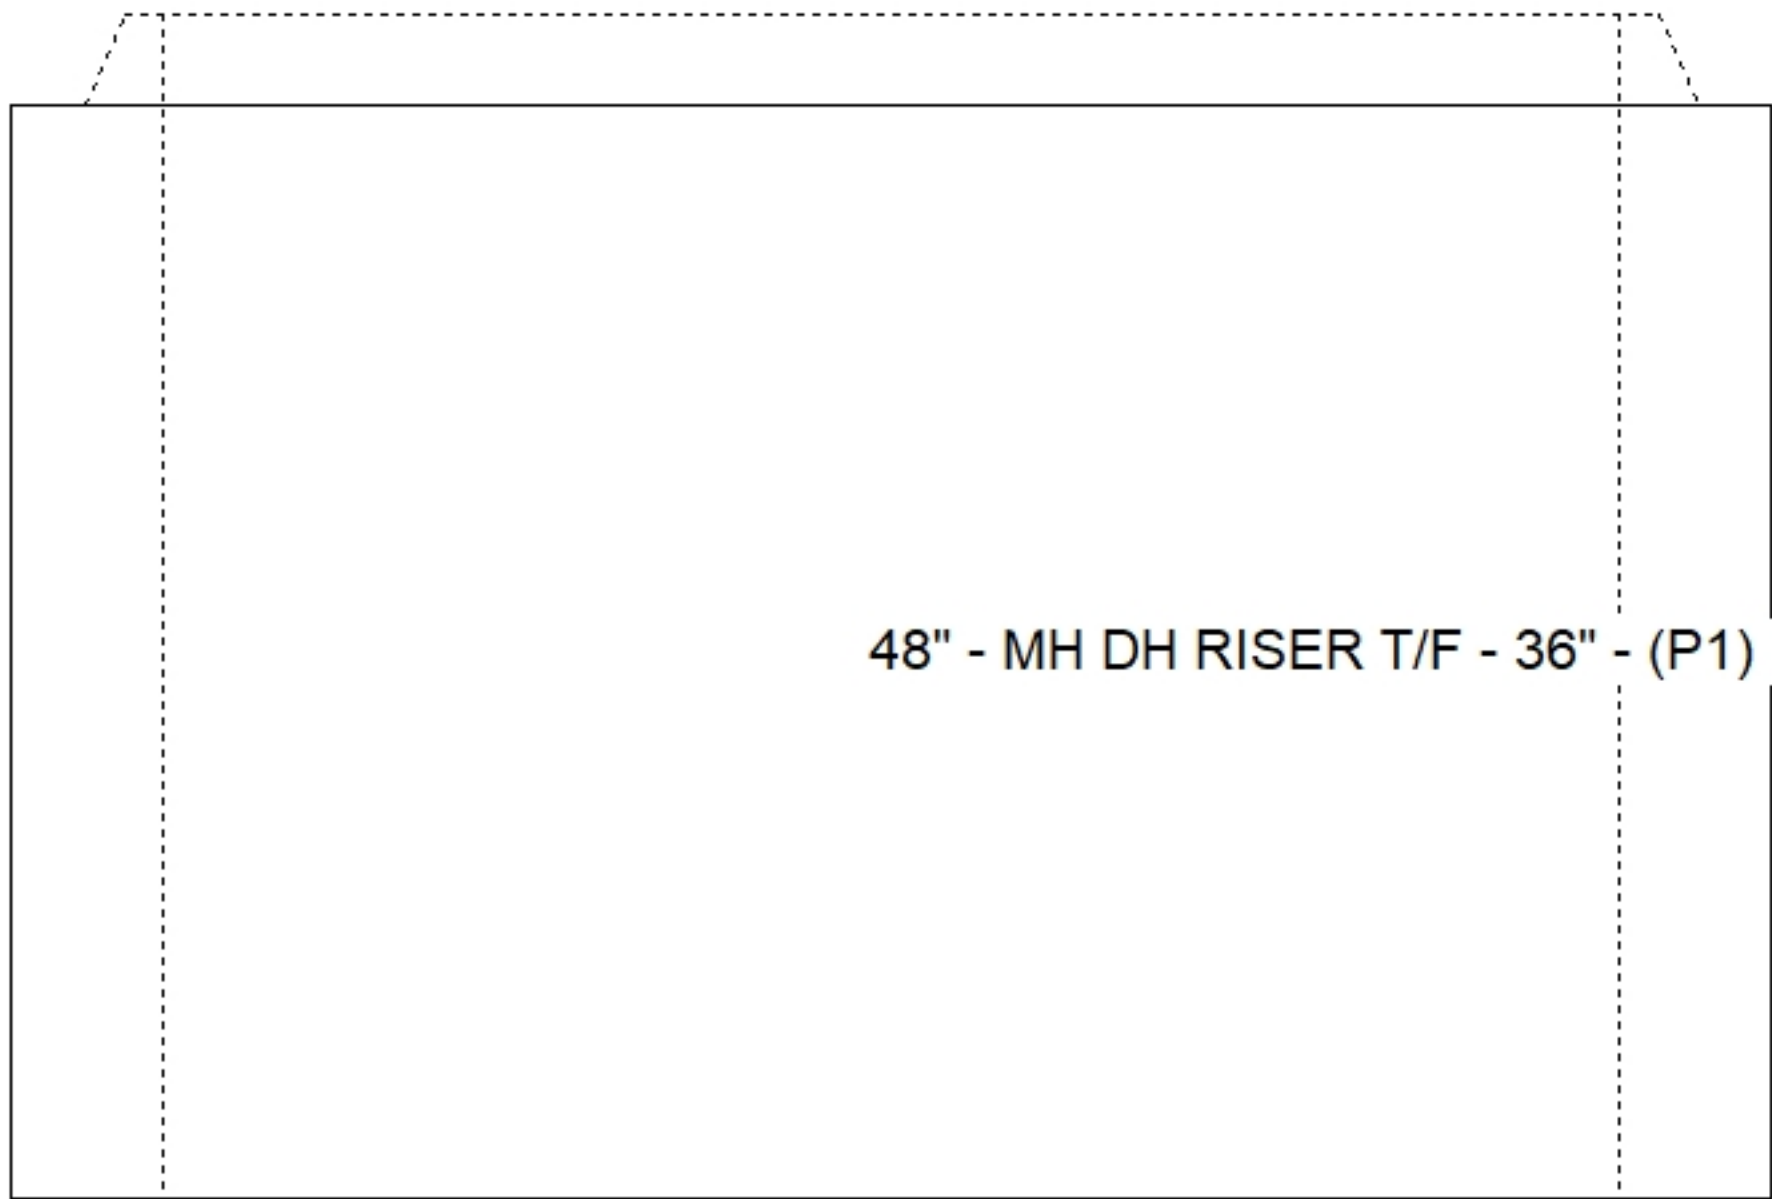
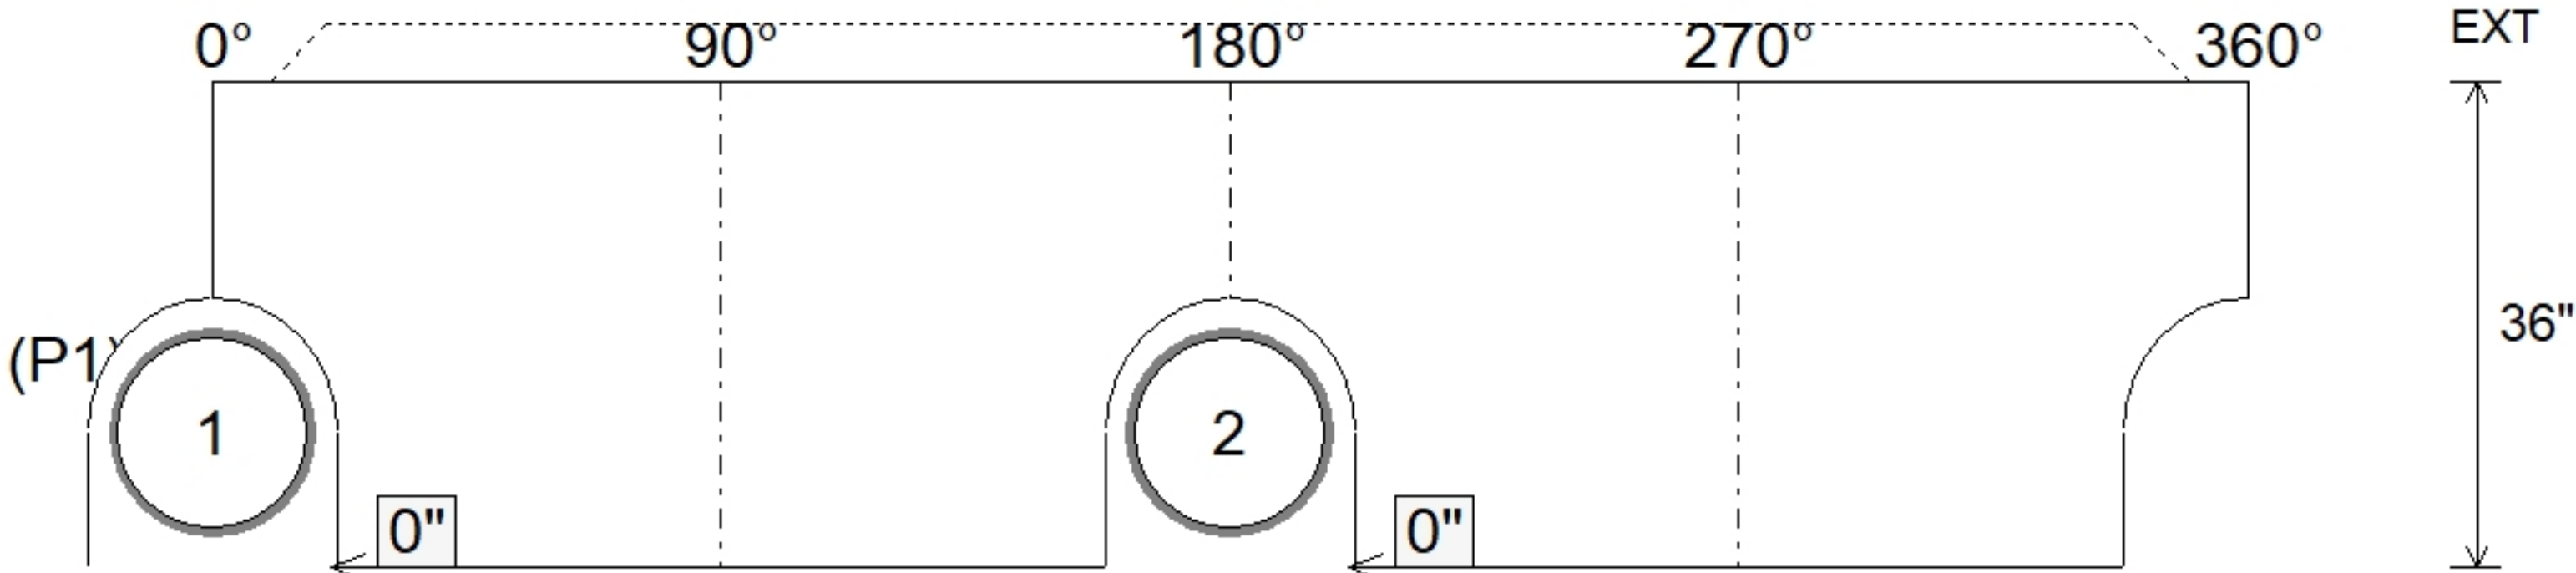


Job Name: 26-2626 Whitehouse Force Main Job Location: CPU Contractor: Cumberland Pipeline LLC				PC: C. Goff TECH: S. Felletter Plant: Beaver Dam																																																																																																						
Structure ID: QL1 SS-MHDH Spec: Sanitary Type: DH Manhole Size: 48" Rim: 3' Invert: 0' Rim to Invert: 3' Sump: 3" Floor (Top): -0.25' Floor Height: 0" Floor (Bot): -0.25' Overall Height: 3' Slack: 3"																																																																																																										
Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. . REINFORCING PER ASTM A615 (GRADE 60). - RISER/WALLS (As .12)				STRUCTURE SUMMARY: P1) 48" - MH DH RISER T/F - 36"2240 lb 2) DOGHOUSE - 18"x20"0 lb Structure Total: 2240 lb																																																																																																						
				<table><tr><th>Position</th><th>Elev</th><th>Angle</th><th>Pipe</th><th>Pipe OD</th><th>Hole</th><th>Connector</th><th>Up ()</th><th>Ref</th></tr><tr><td>Rim</td><td>3'</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr><tr><td>Reducer</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr><tr><td>Invert 1</td><td>0'</td><td>0°</td><td>14" PVC C900</td><td>15.3"</td><td>18" x 20"</td><td>DOGHOUSE 18"x20"</td><td>0"</td><td>P1</td></tr><tr><td>Invert 2</td><td>0'</td><td>180°</td><td>14" PVC C900</td><td>15.3"</td><td>18" x 20"</td><td>DOGHOUSE 18"x20"</td><td>0"</td><td>P1</td></tr><tr><td>Invert 3</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr><tr><td>Invert 4</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr><tr><td>Invert 5</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr><tr><td>Invert 6</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr><tr><td>Invert 7</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr><tr><td>Invert 8</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr></table>				Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref	Rim	3'								Reducer									Invert 1	0'	0°	14" PVC C900	15.3"	18" x 20"	DOGHOUSE 18"x20"	0"	P1	Invert 2	0'	180°	14" PVC C900	15.3"	18" x 20"	DOGHOUSE 18"x20"	0"	P1	Invert 3									Invert 4									Invert 5									Invert 6									Invert 7									Invert 8								
Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref																																																																																																		
Rim	3'																																																																																																									
Reducer																																																																																																										
Invert 1	0'	0°	14" PVC C900	15.3"	18" x 20"	DOGHOUSE 18"x20"	0"	P1																																																																																																		
Invert 2	0'	180°	14" PVC C900	15.3"	18" x 20"	DOGHOUSE 18"x20"	0"	P1																																																																																																		
Invert 3																																																																																																										
Invert 4																																																																																																										
Invert 5																																																																																																										
Invert 6																																																																																																										
Invert 7																																																																																																										
Invert 8																																																																																																										
				Default - Interior Dimensions 																																																																																																						
Submittal Drawing 6/5/2026 2:17:26 PM				SUBMITTAL APPROVED BY:																																																																																																						
