

Job Name: 26-2643 - Sinking Creek WWTP
Job Location: Somerset, KY
Contractor: Pace Contracting, LLC

Plant: 100

9/21/2026 4:22:10 PM

Tech: Jared - F

PC: T. Ryan



Structure ID: QL1

P1 CTS

CUST. TOP SLAB (SOLID) F/F

P1) 48" x 54" - CUST. TOP SLAB (SOLID) F/F - 8"

Structure Total: 1740 lb



Structure Notes:

1. PER ASTM C913 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.

REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.

NOTES:

1. MANUFACTURED PER ASTM C913 SPECIFICATIONS.
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING PER ASTM A615 (GRADE 60) - 2" MIN REBAR CLEARANCE (TYP):
TOP SLAB = #5 BARS AT 6" C.C.E.W.

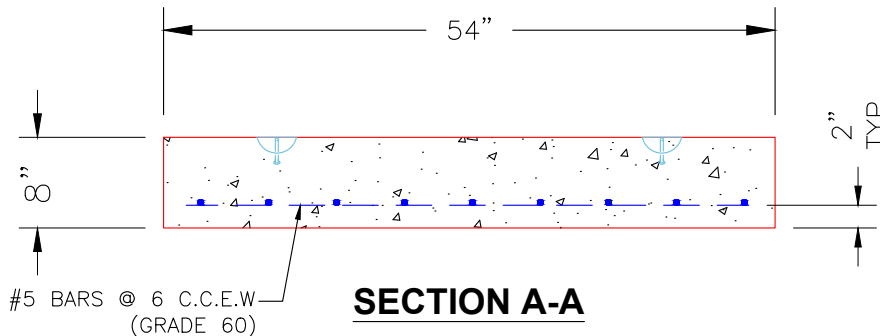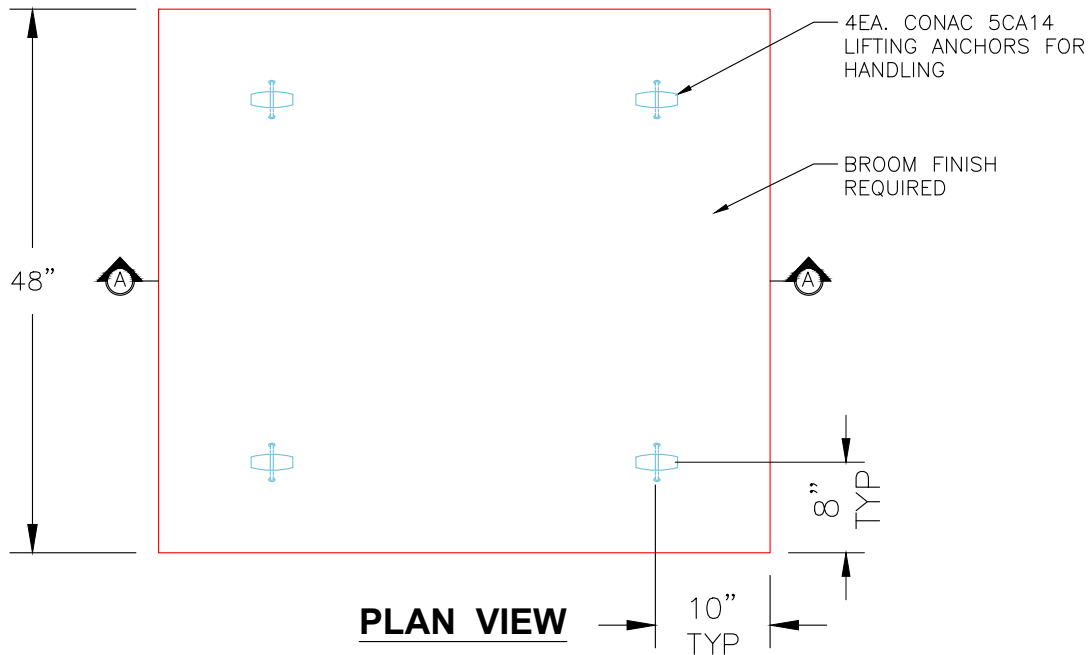

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 0"

Height (Ext): 8"

Weight (Net): 1740 lb
Volume (Net): 0.44cu.yd

Job Name: 26-2643 - Sinking Creek WWTP
Job Location: Somerset, KY
Contractor: Pace Contracting, LLC

Plant: 100

Tech: Jared - F

9/21/2026 4:22:10 PM

PC: T. Ryan



Structure ID: QL2

P1 CTS

CUST. TOP SLAB W/ 24" X 24" HATCH F/F

P2) 24" x 24" - CASTING (cast in) - 3"
P1) 48" x 54" - CUST. TOP SLAB W/ 24" X 24" HATCH F/F - 8"
1) HATCH (Alum.) - HALLIDAY W1S 24"x24"

0 lb
1353 lb
46 lb

Structure Total: 1399 lb


Structure Notes:

1. PER ASTM C913 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING BY ICAST (HALLIDAY W1S 24"x24").


REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.

NOTES:


1. MANUFACTURED PER ASTM C913 SPECIFICATIONS.
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING PER ASTM A615 (GRADE 60) - 2" MIN REBAR CLEARANCE (TYP):
TOP SLAB = #5 BARS AT 6" C.C.E.W.
4. HATCH HALLIDAY W1S 24"x24" HATCH TO BE SUPPLIED BY ICAST TO BE CAST INTO SLAB.7"
5. HATCH TO BE CAST INTO TOP SLAB.

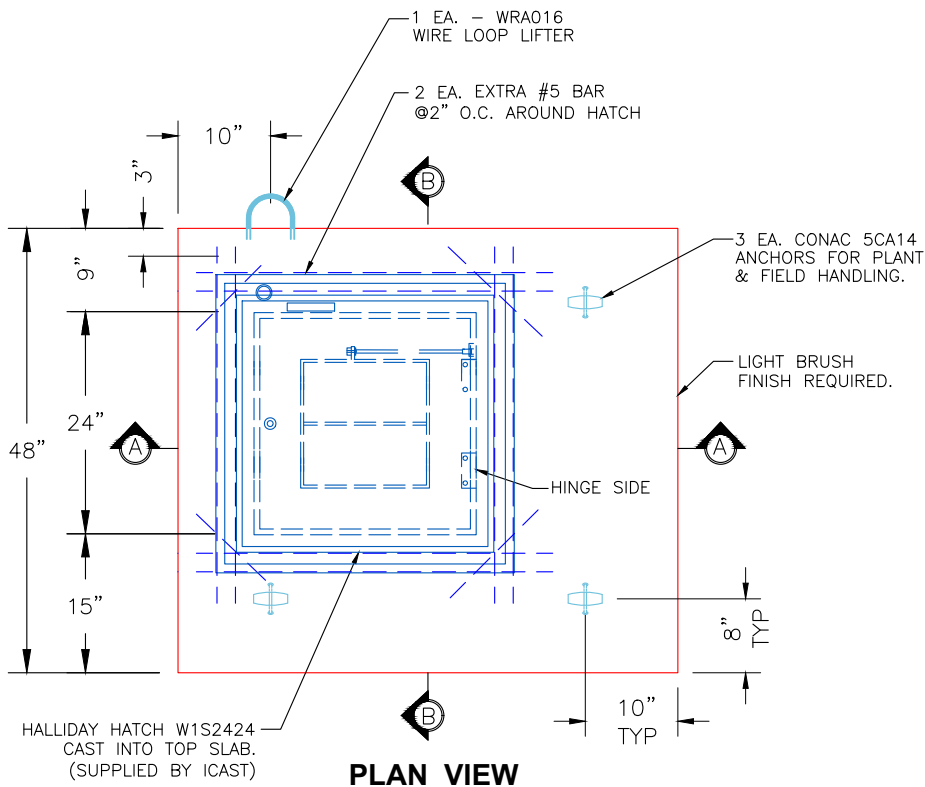

PLAN VIEW

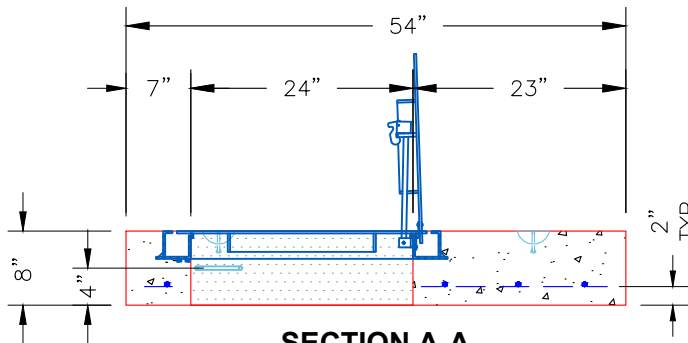

SECTION A-A

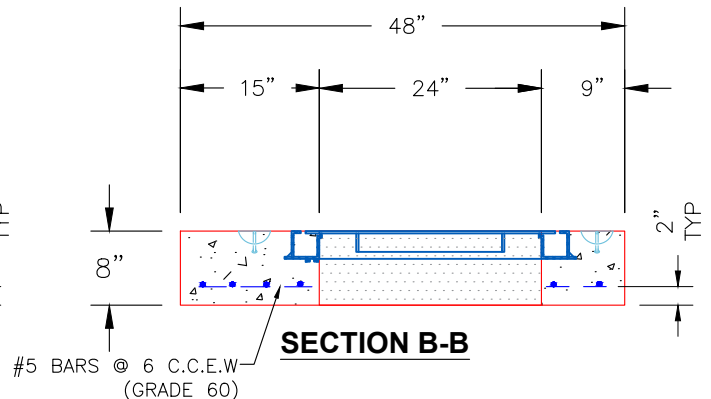

SECTION B-B

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 0"

Height (Ext): 8"

Weight (Net): 1353 lb
Volume (Net): 0.35cu.yd
