

Contractor: Steve Pleasant Excavating

Plant: Beaver Dam




Slack: 0"

REINFORCING PER ASTM A615 (GRADE 60).
- WALLS (As .31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

P2) 36" x 36" - P.I.P. - BY OTHERS - 8"
P1) 36" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/n - 34"
1) CASTING - HOE KY-328 SET (DBI 3)
1) 36" x 36" - Conseal CS-102 1.00"
1) Hole - 32



0 lb
5292 lb
328 lb
0 lb
0 lb

Structure Total: 5620 lb

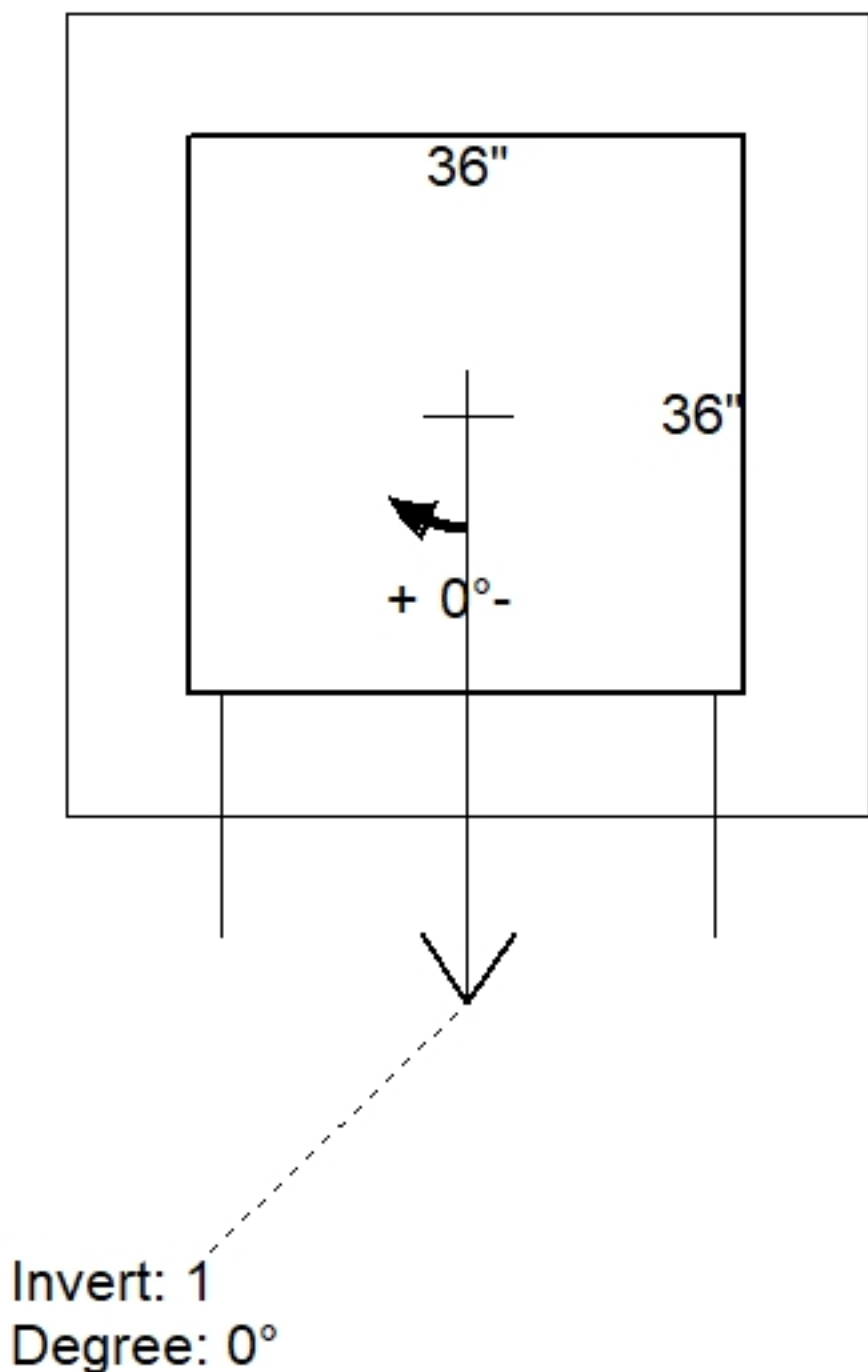

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	431.48'							
Reducer								
Invert 1	427.98'	0°	24" ADS N-12	28"	32"	Hole 32	-4"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

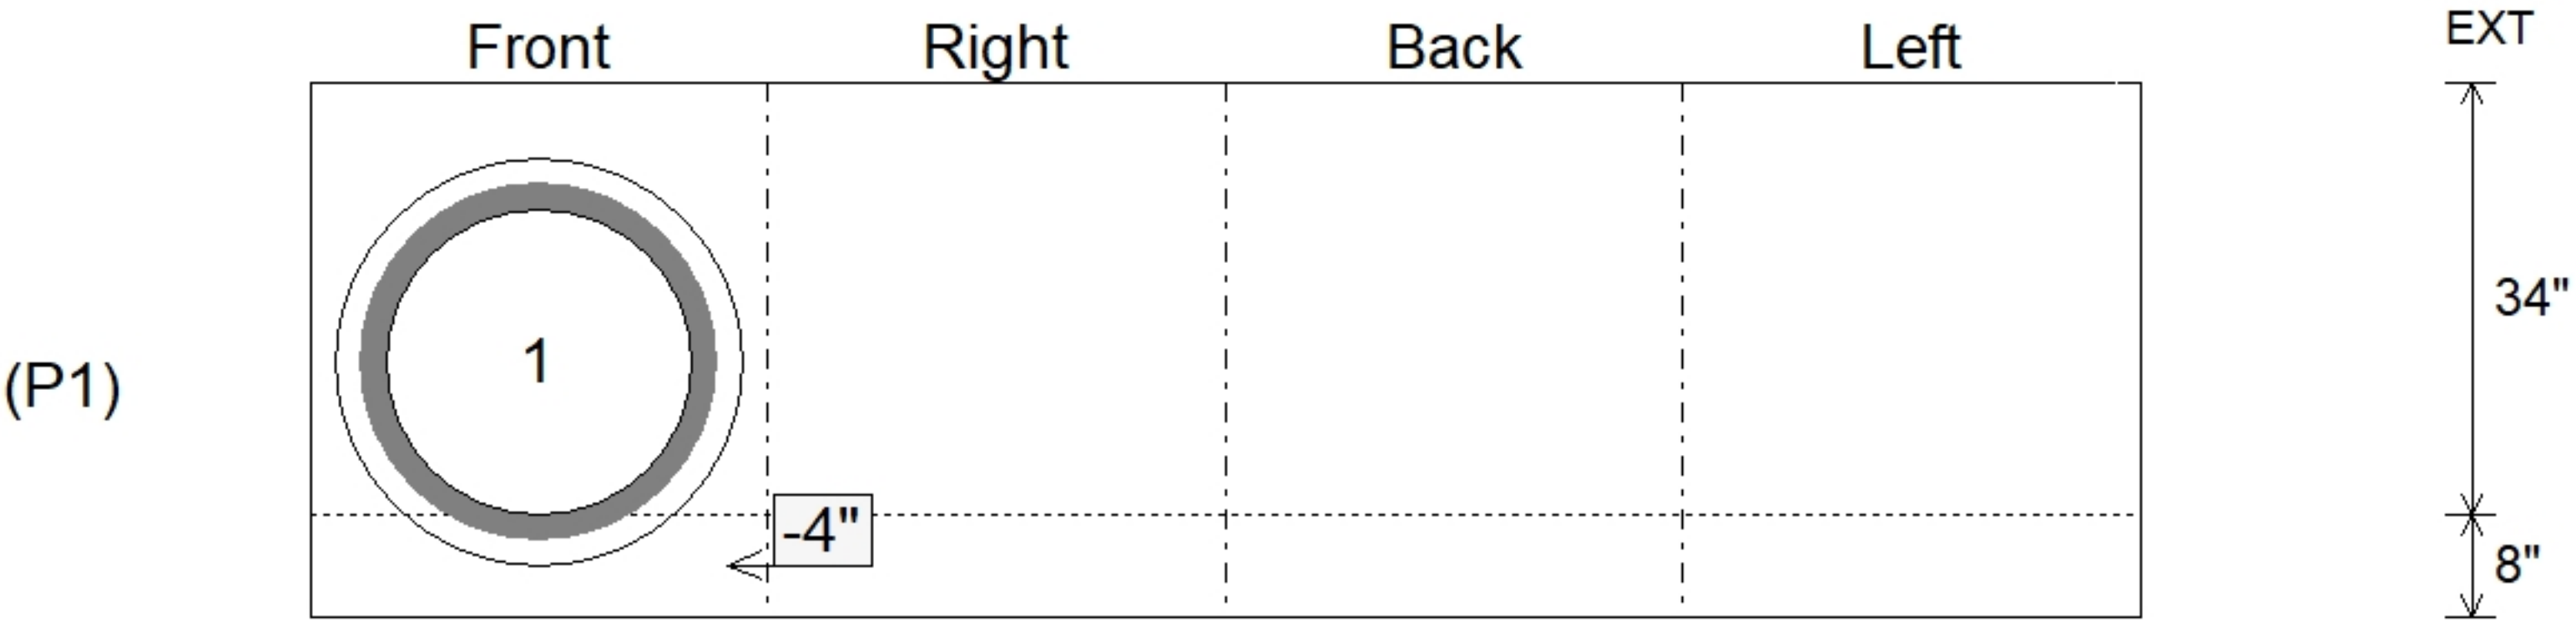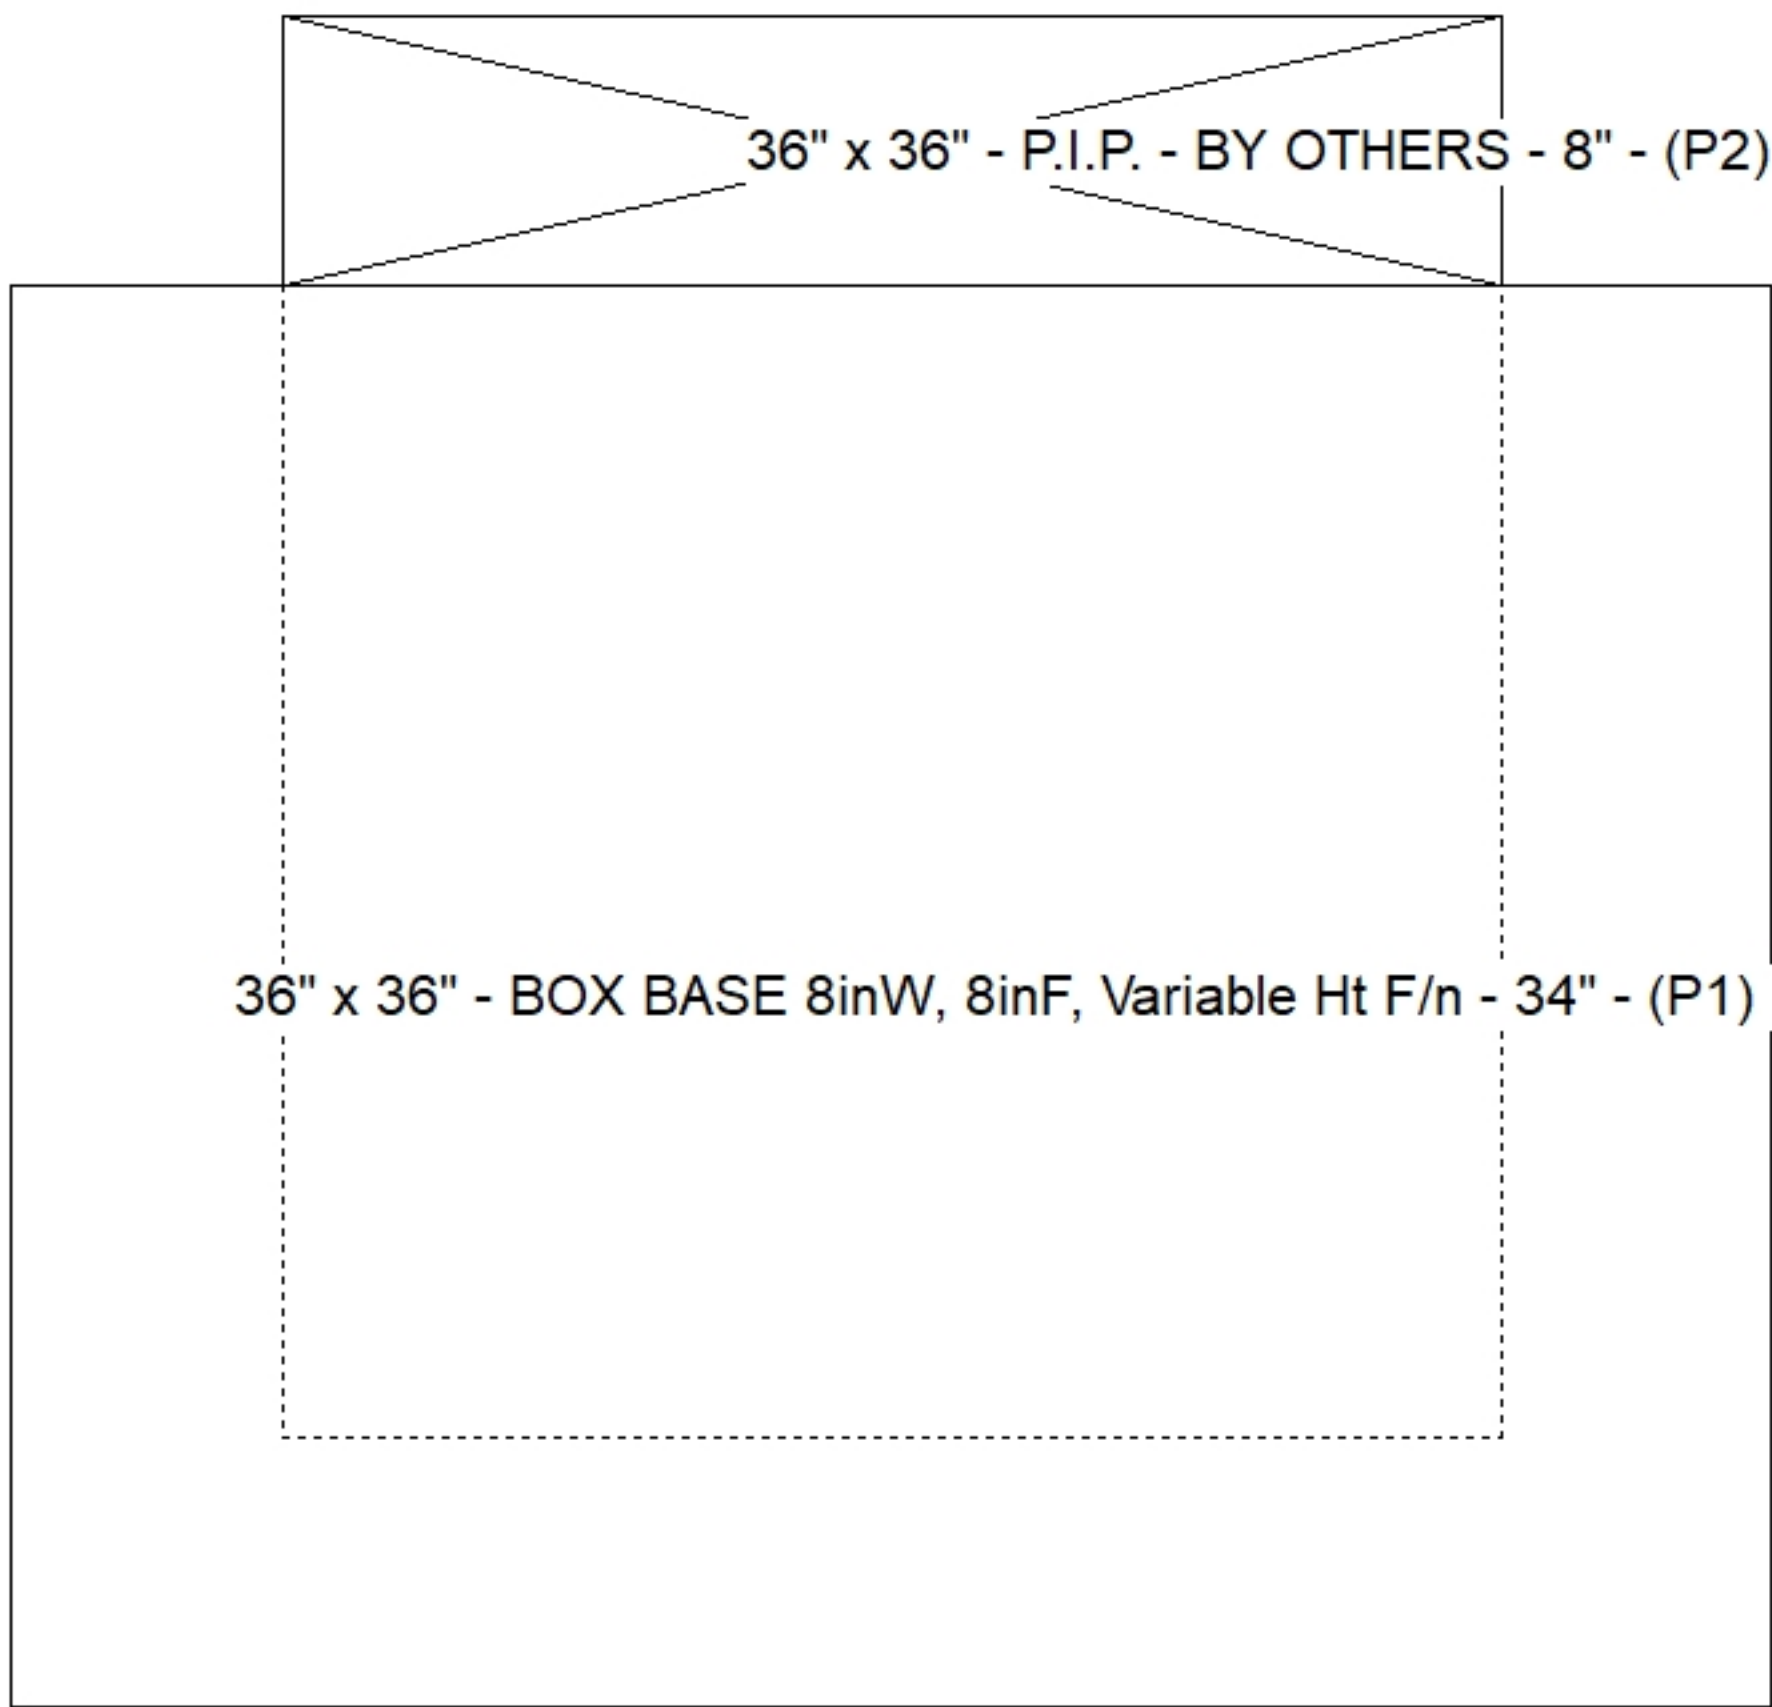

Submittal Drawing
7/20/2026 10:43:19 AM

SUBMITTAL
APPROVED BY:
