

Contractor: Steve Pleasant Excavating

Plant: Beaver Dam



Slack: 0.12"


REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
- WALLS (As .31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

P3) 19.5" - CASTING (cast in) - 2.75"
P2) 24" x 24" - CB FLAT TOP 8"W (HOE KY-210) F/F - 8"
P1) 24" x 24" - BOX BASE 8inW, 8inF, Variable Ht F/n - 22"
1) CASTING - HOE KY-210 F/G (DBI 14)
1) This Structure Includes a Cast-in Item
1) 24" x 24" - Conseal CS-102 1.00"
1) Hole - 22



0 lb
943 lb
2709 lb
178 lb
0 lb
0 lb
0 lb

Structure Total: 3830 lb

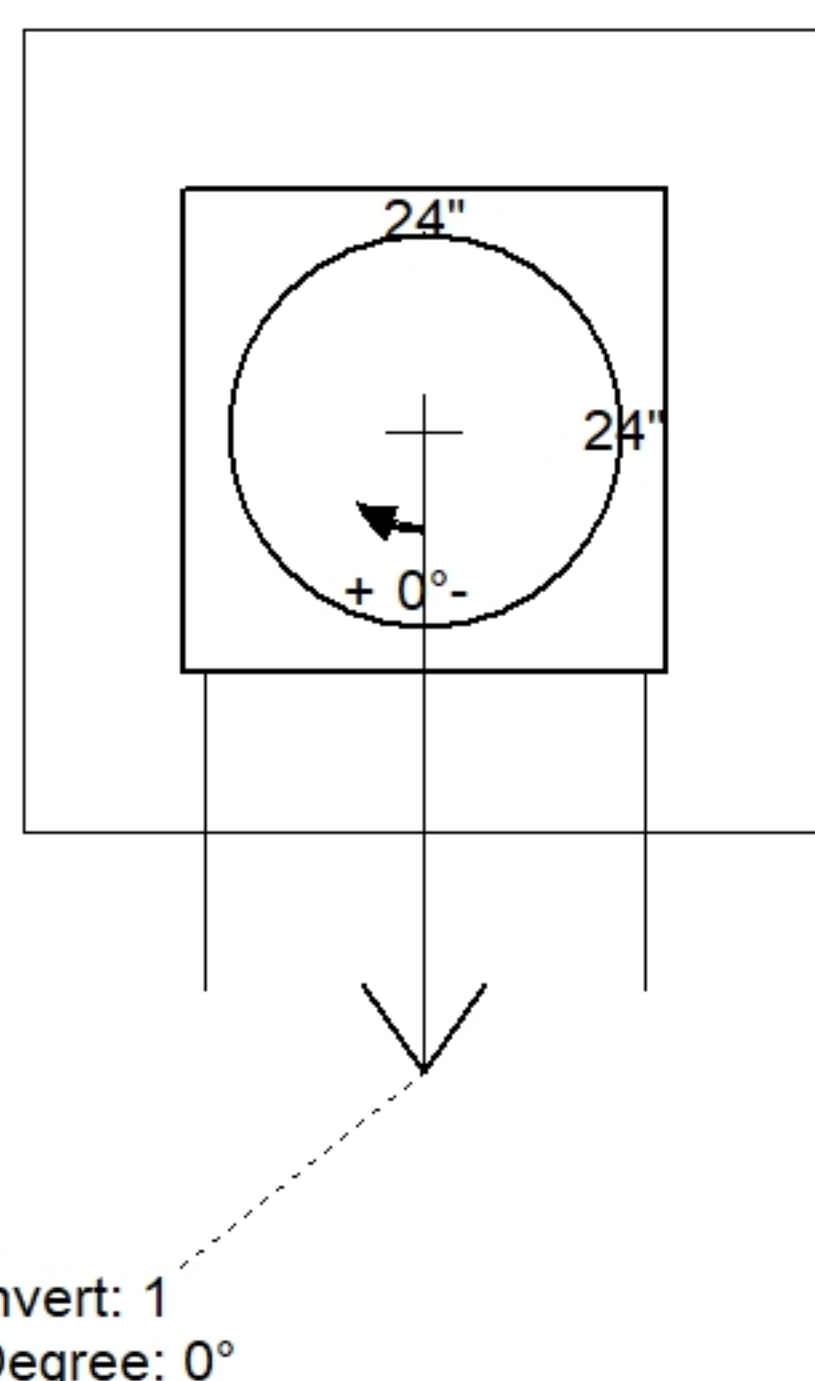

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	429.51'							
Reducer								
Invert 1	427'	0°	15" ADS N-12	18"	22"	Hole 22	-3.5"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

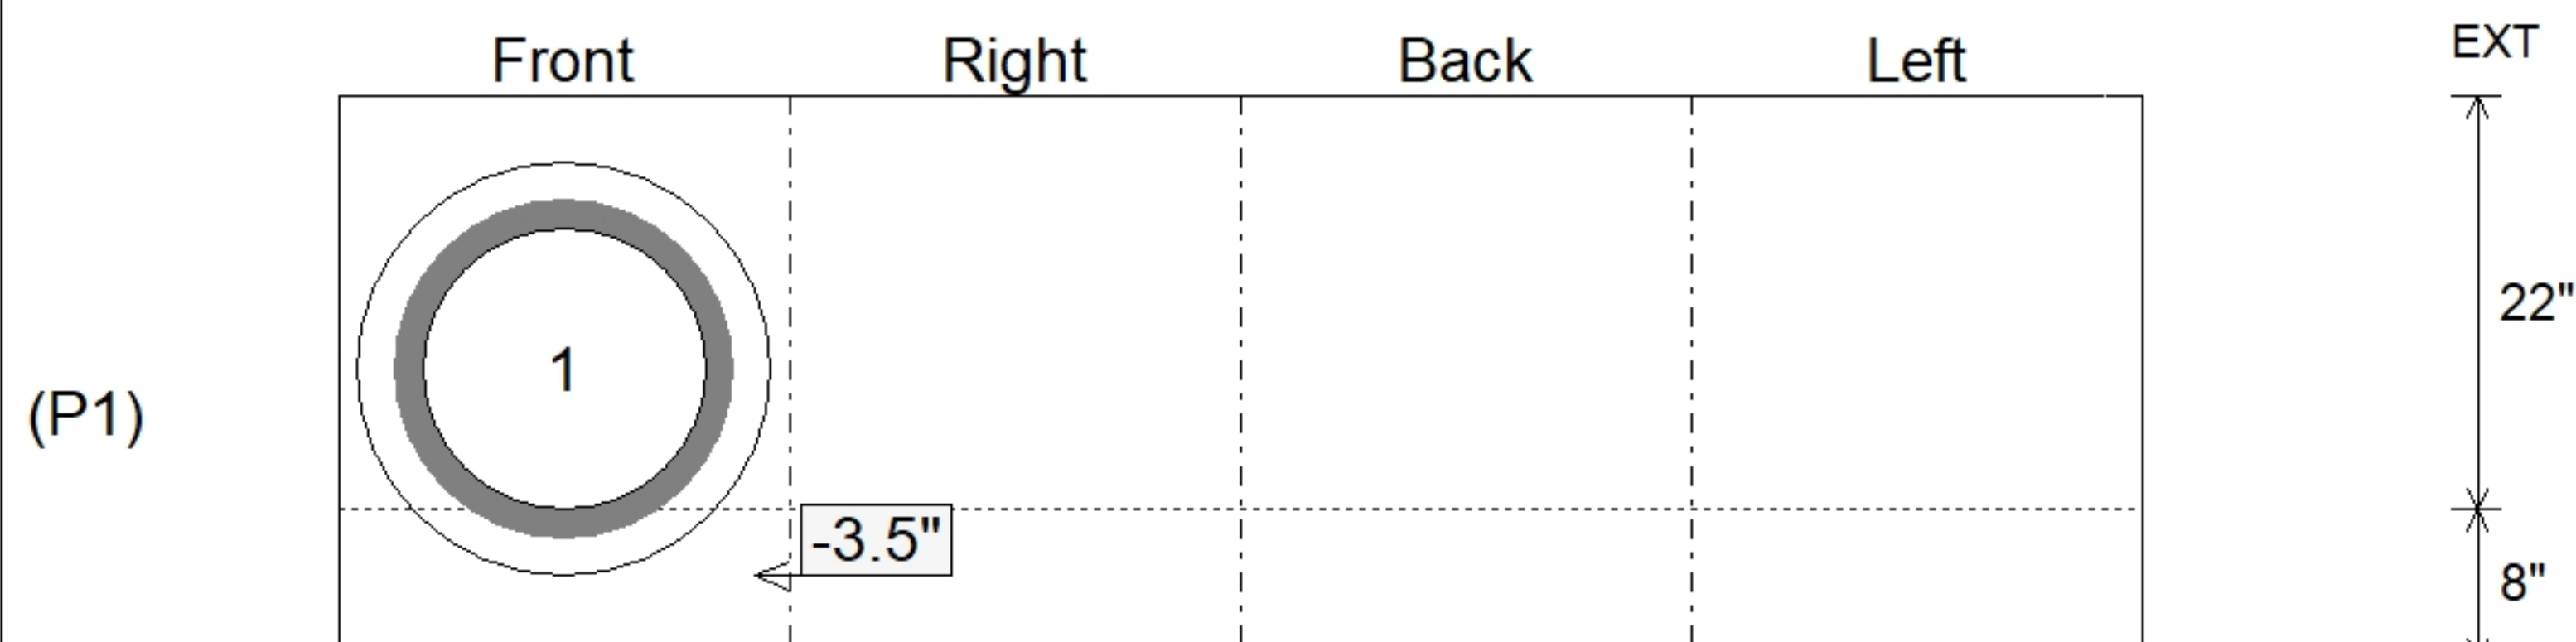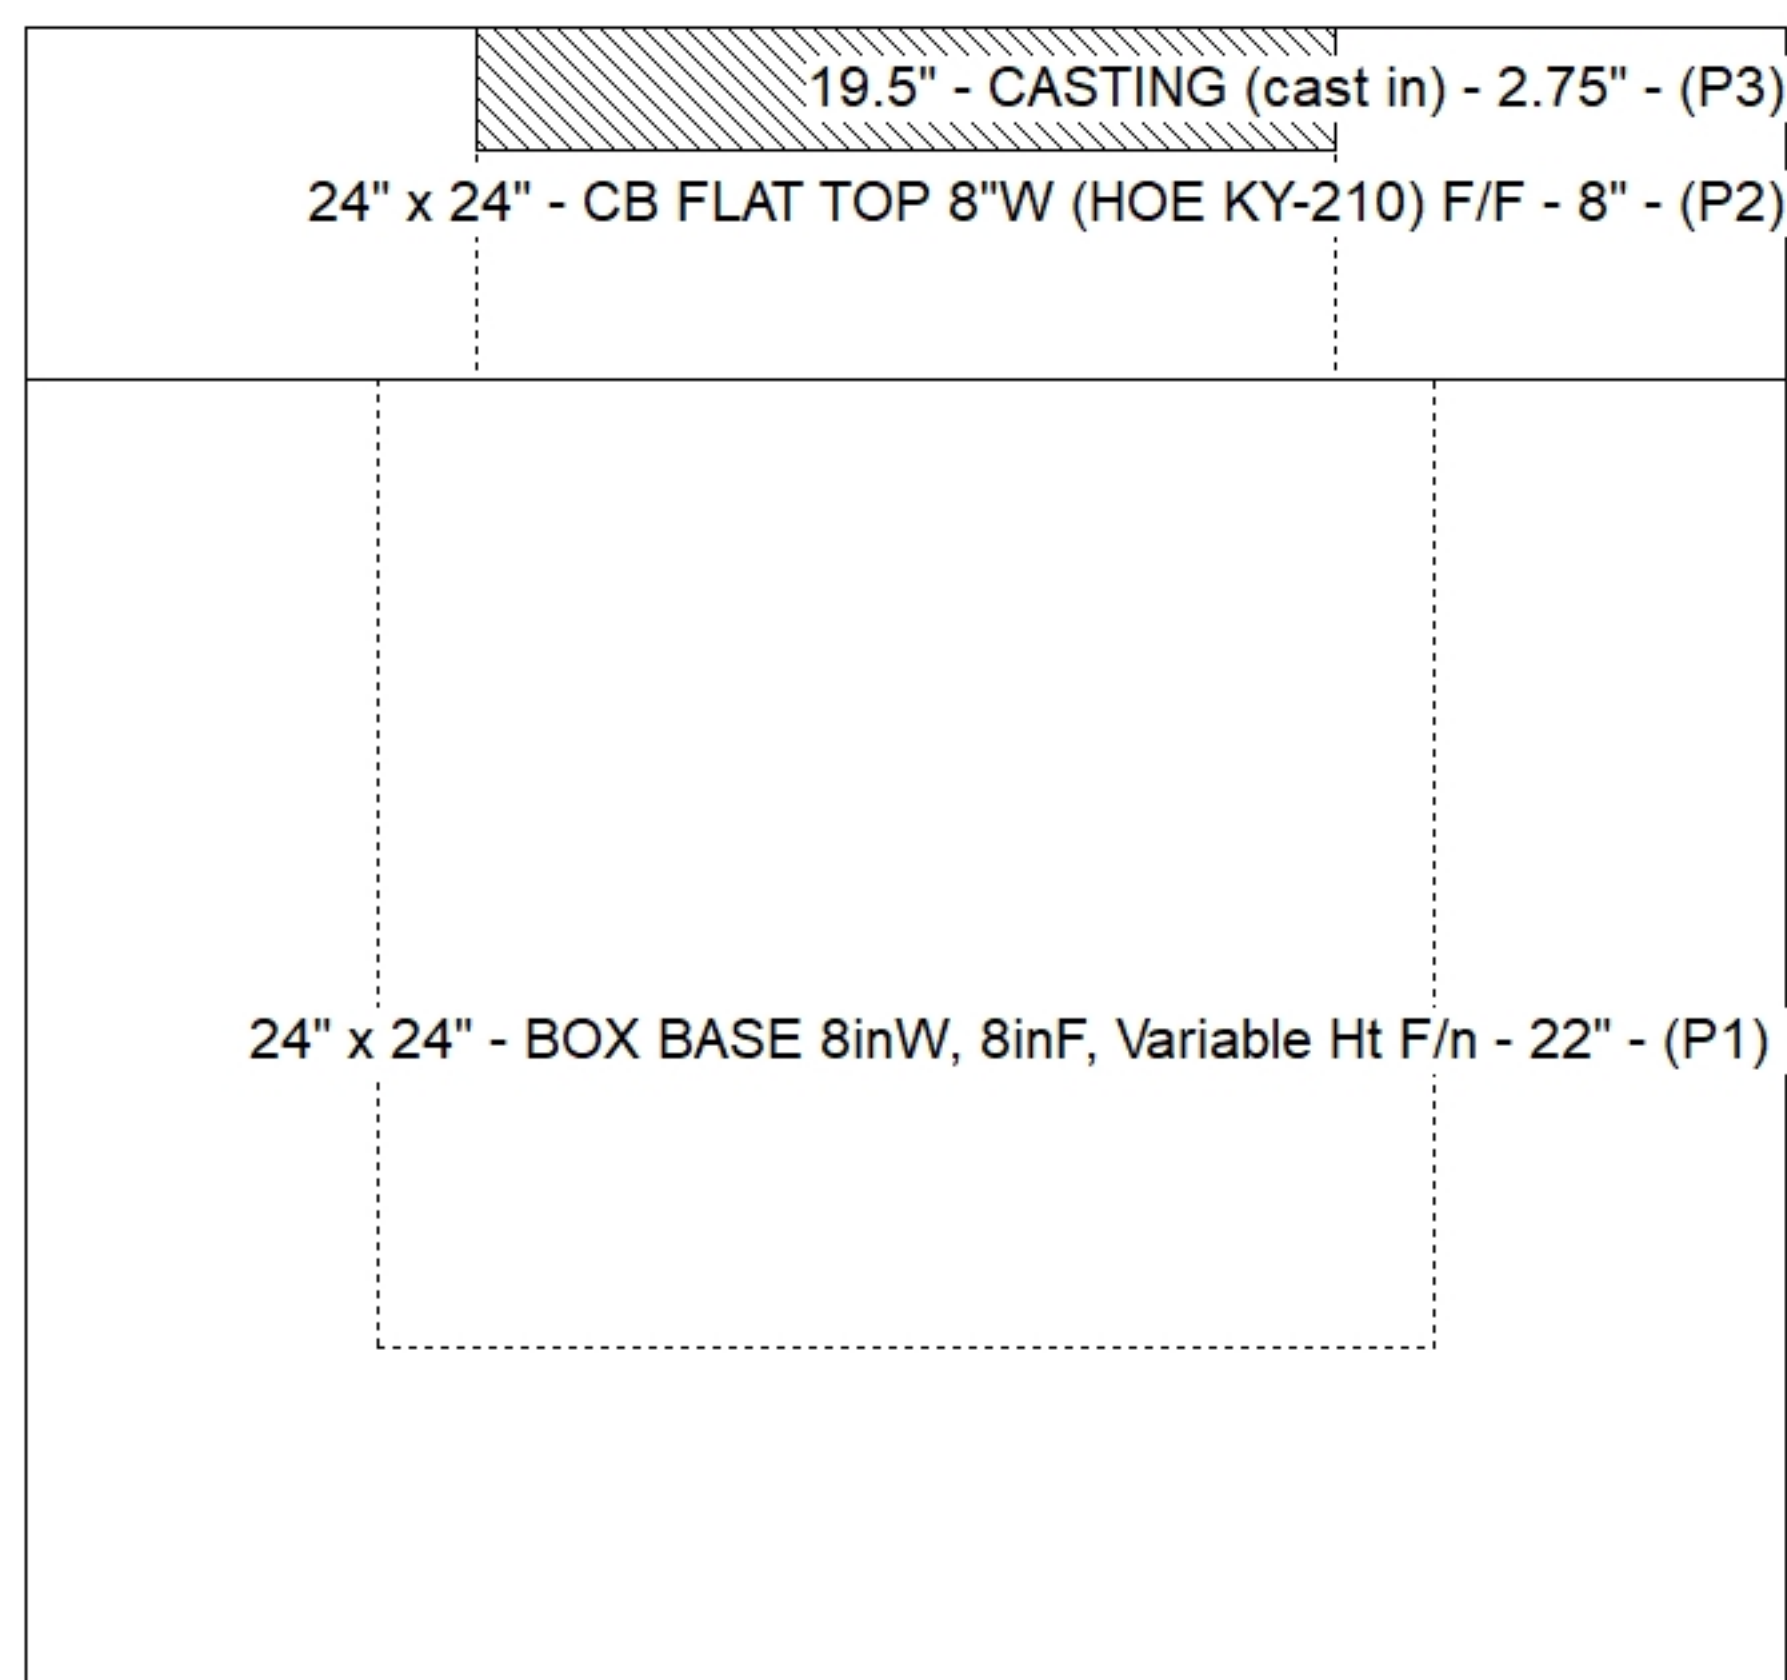

SUBMITTAL
APPROVED BY:
