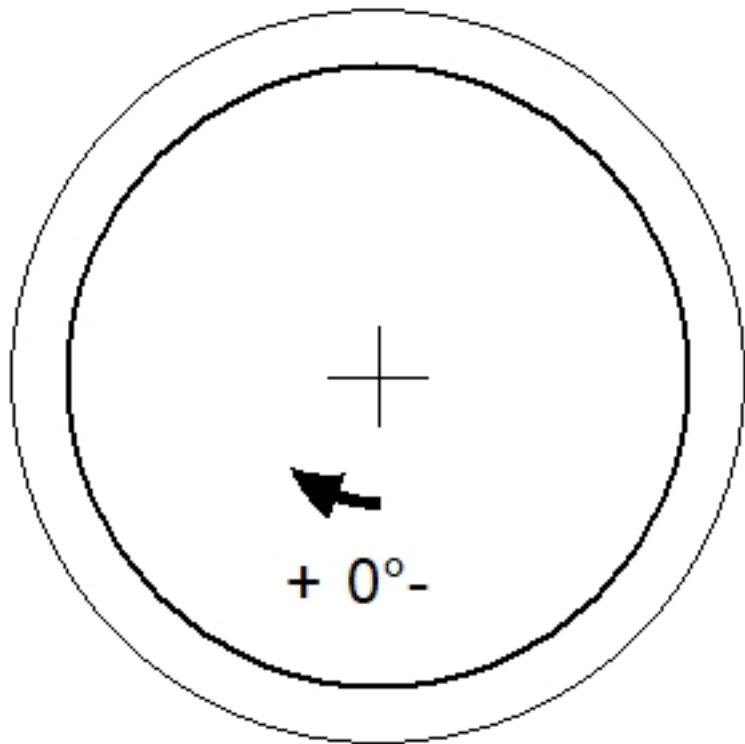
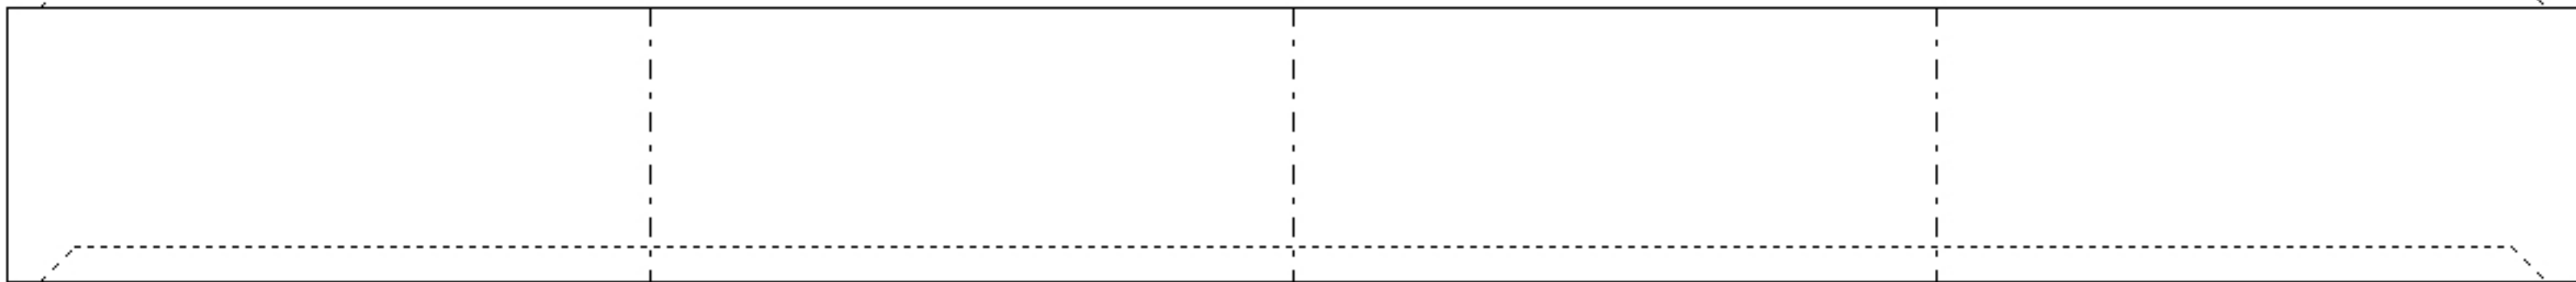


Job Name: 26-2722 863539 South Oldham High School					Plant: Beaver Dam		Tech: S. Felletter				
Job Location: Crestwood, KY					7/8/2026 9:14:25 AM		PC: C. Goff				
Contractor: Contech Engineering Solutions											
Structure ID: 30-CS-12											
P2			MH144RS48			MH RISER T/G					
P6) 24" - CASTING HEIGHT - 4" P5) 144" - MH FLAT TOP SPEC. (2 - 24"Ø HOLES) F/G - 18" P4) 144" - MH RISER Custom Ht T/G - 50" P3) 144" - MH RISER Custom Ht T/G - 69" P2) 144" - MH RISER T/G - 48" P1) 144" - MH MONOBASE 14F, Custom Ht T/n - 24" 1) ASSEMBLY REQUIRED - BRACKETS ONLY 1) CVSTENCILING 4) 144" - Conseal CS-102 1.00" 1) 24" - Conseal CS-102 1.00" 1) Hole - 36 1) Hole - 24 2) Hole - 20 1) Hole - 8					0 lb 23623 lb 25664 lb 36004 lb 25826 lb 39578 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb Structure Total: 150696 lb		Structure Notes: 4" CASTING BY OTHERS LIFTING ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE ICAST TO INSTALL BRACKETS ONLY CONTECH'S LOGO AS WELL AS THE INLET AND OUTLET MUST BE STENCILED ONTO THE STRUCTURE				
Rim: 754.15'		Rim to Invert: 9.06'		Slack: 3.756"		Sump: 108.036"		Step Position: 0°			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (⌵)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions) (P6) (P5) (P4) (P3) (P2) << (P1)  INSIDE WALL DIMENSIONS (P2) 0° 90° 180° 270° 360° 											
Coating (Int): Coating (Ext):				Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 13" Floor Height: 0"		Height (Int): 48" Height (Ext): 48"		Weight (Net): 25826 lb Volume (Net): 6.6cu.yd	
