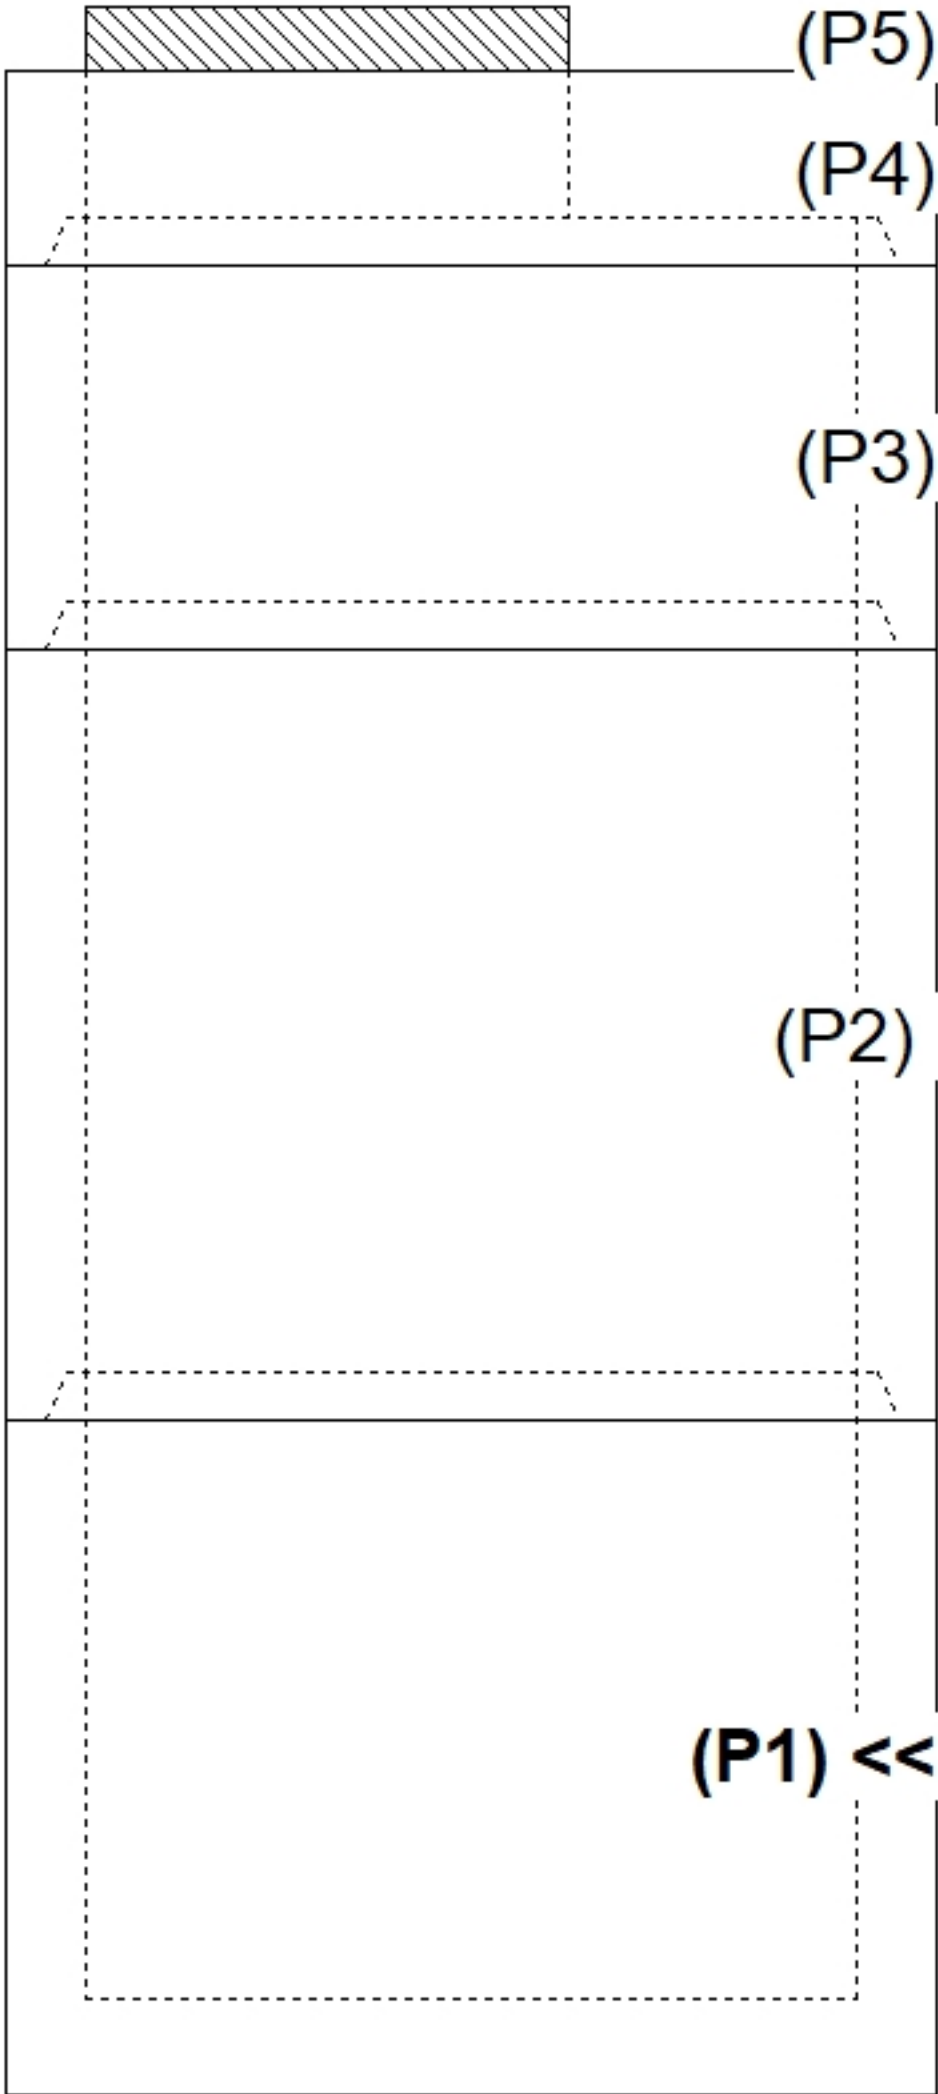
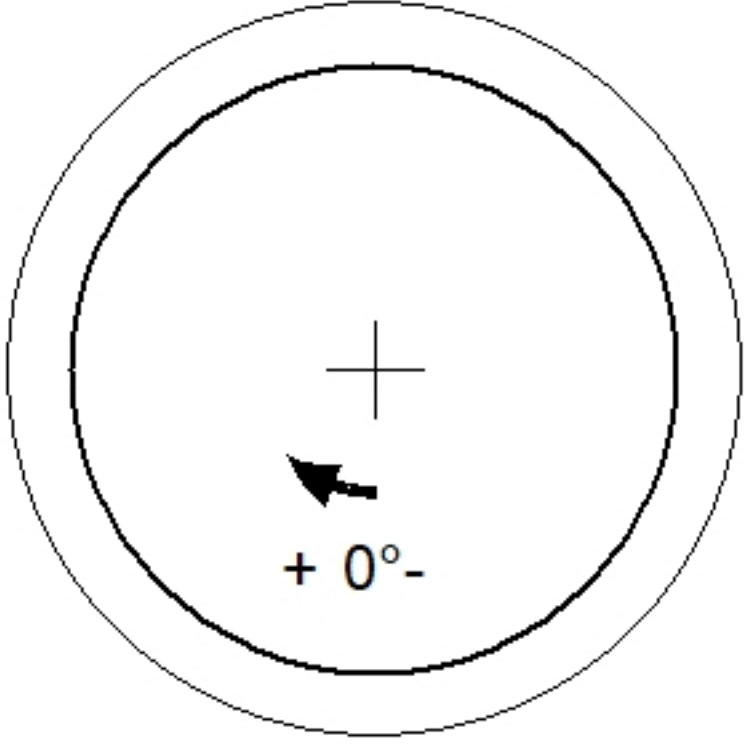
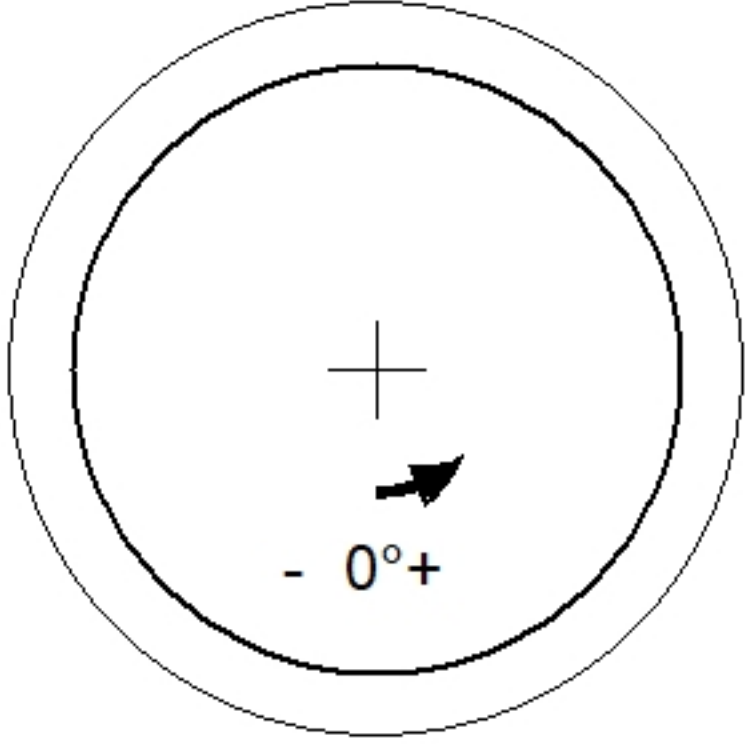
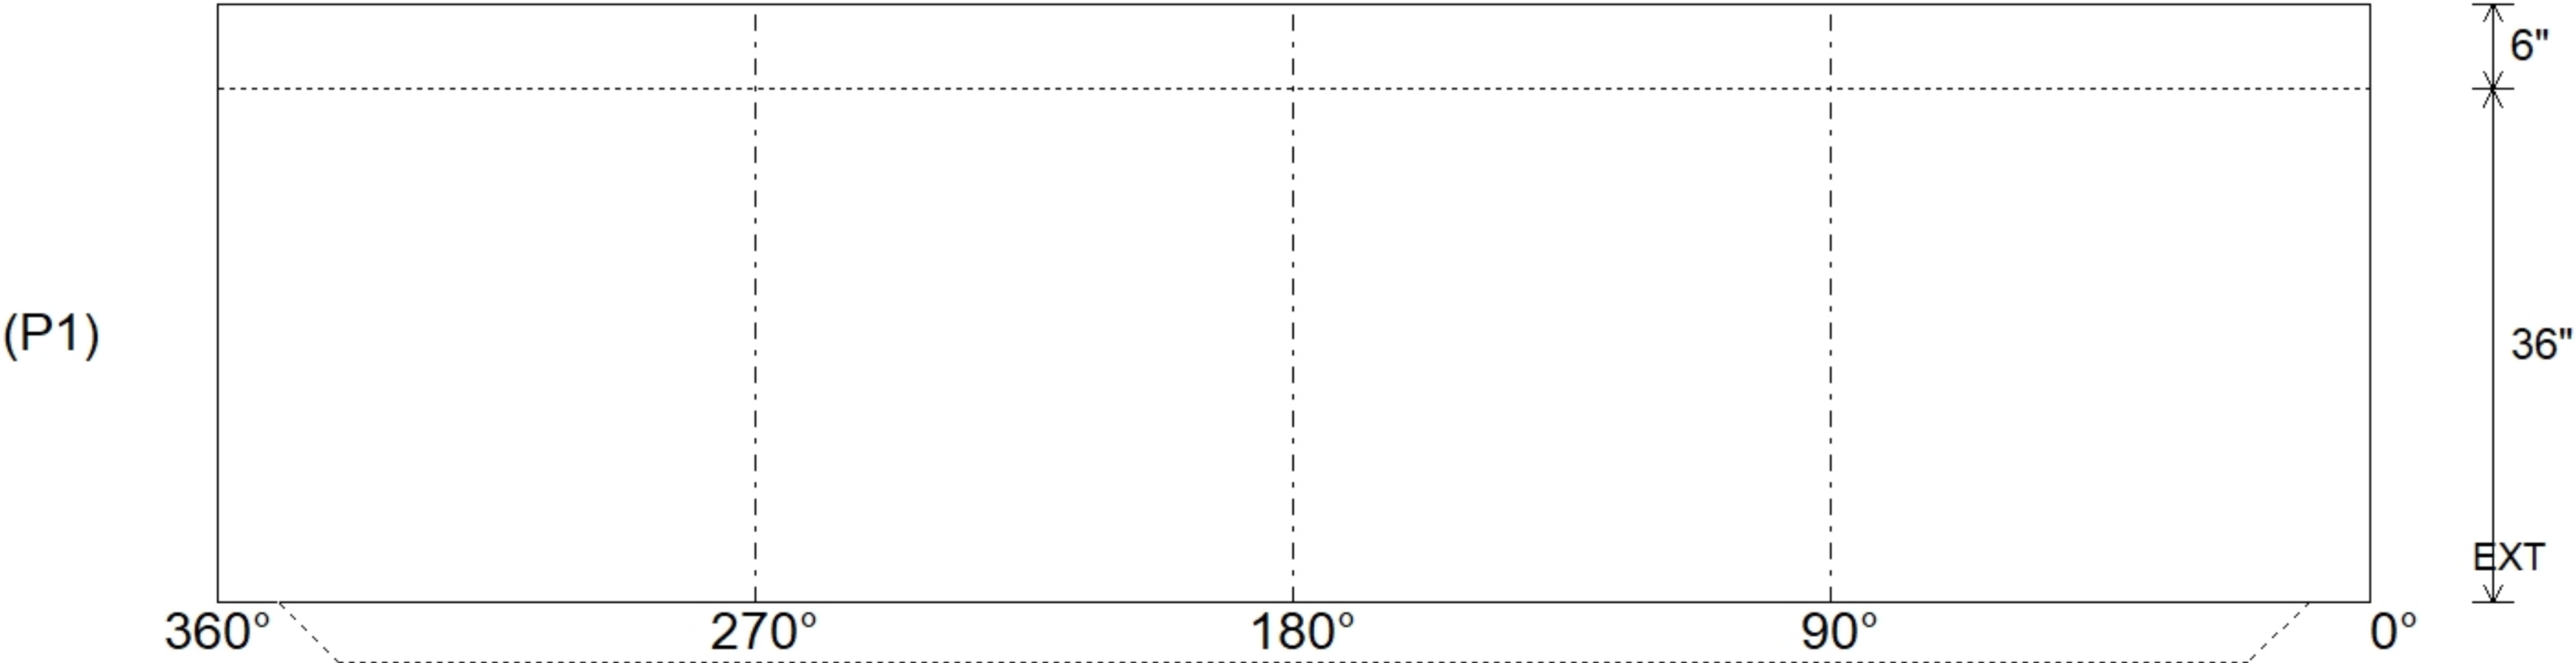


Job Name: 26-2731 870553 Hampton Inn O'Fallon Job Location: CPU Contractor: Contech Engineering Solutions					Plant: Beaver Dam 6/23/2026 1:17:06 PM		Tech: S. Felletter PC: C. Goff				
Structure ID: 10-CS-4											
P1		MH048BA36		MH BASE T/n							
P5) 30" - CASTING HEIGHT - 4" P4) 48" - MH FLAT LID w/30in ECC Hole F/G - 12" P3) 48" - MH RISER T/G - 24" P2) 48" - MH RISER T/G - 48" P1) 48" - MH BASE T/n - 36" 1) ASSEMBLY REQUIRED 1) CVSTENCILING 3) 48" - Conseal CS-102 1.00" 2) PSX - 16M NYLO						0 lb 1413 lb 1677 lb 3182 lb 3845 lb 0 lb 0 lb 0 lb 16 lb ----- Structure Total: 10133 lb		Structure Notes: 4" CASTING BY OTHERS . LIFTING ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE . ICAST TO INSTALL THE INTERNALS . BASE AND P2 RISER TO BE MECHANICALLY ATTACHED PRIOR TO INSTALLATION OF INTERNALS . CONTECH'S LOGO AS WELL AS THE INLET AND OUTLET MUST BE STENCILED ONTO THE STRUCTURE			
Rim: 570.5'		Rim to Invert: 6.91'		Slack: 6.92"		Sump: 48"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (┘)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
						RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimenions)  INSIDE WALL DIMENSIONS 					
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 5" Floor Height: 6"		Height (Int): 36" Height (Ext): 42"		Weight (Net): 3845 lb Volume (Net): 0.98cu.yd		
