

Contractor: Winwater Hartford KY Co.

Plant: 100




Slack: 0.12"

REINFORCING PER ASTM A615 (GRADE 60).
- WALLS (As .31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

P2) 24" x 48" - CASTING HEIGHT - 5"
P1) 24" x 48" - BOX BASE 8inW, 12inF, Variable Ht - 7"
1) SECONDARY POUR - WALLS
1) CASTING - HOE 818 F/G
1) 24" x 48" - Conseal CS-102 1.00"
3) DOGHOUSE INVRTD - 8"x7"



0 lb
3304 lb
0 lb
734 lb
0 lb
0 lb

Structure Total: 4038 lb

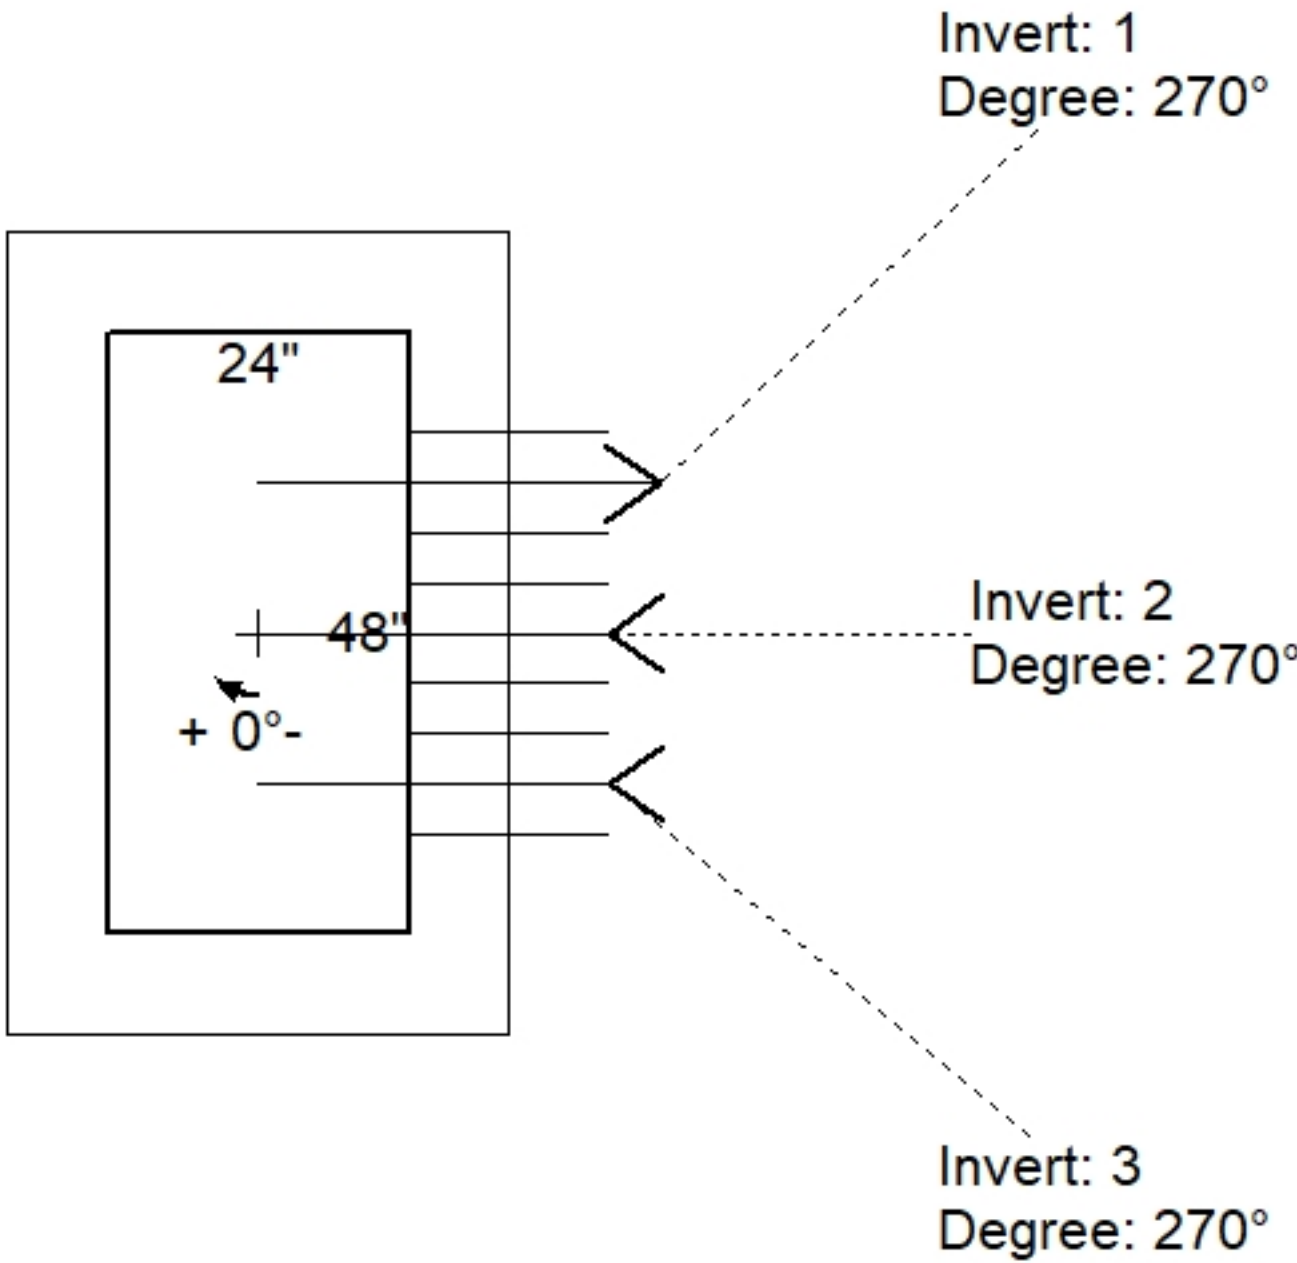

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	401.28'							
Reducer								
Invert 1	400.28'	270°	6" PVC SDR35	6.25"	8" x 7"	DOGHOUSE INVRTD 8"x7"	-0.005"	P1
Invert 2	400.28'	270°	6" PVC SDR35	6.25"	8" x 7"	DOGHOUSE INVRTD 8"x7"	-0.005"	P1
Invert 3	400.28'	270°	6" PVC SDR35	6.25"	8" x 7"	DOGHOUSE INVRTD 8"x7"	-0.005"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

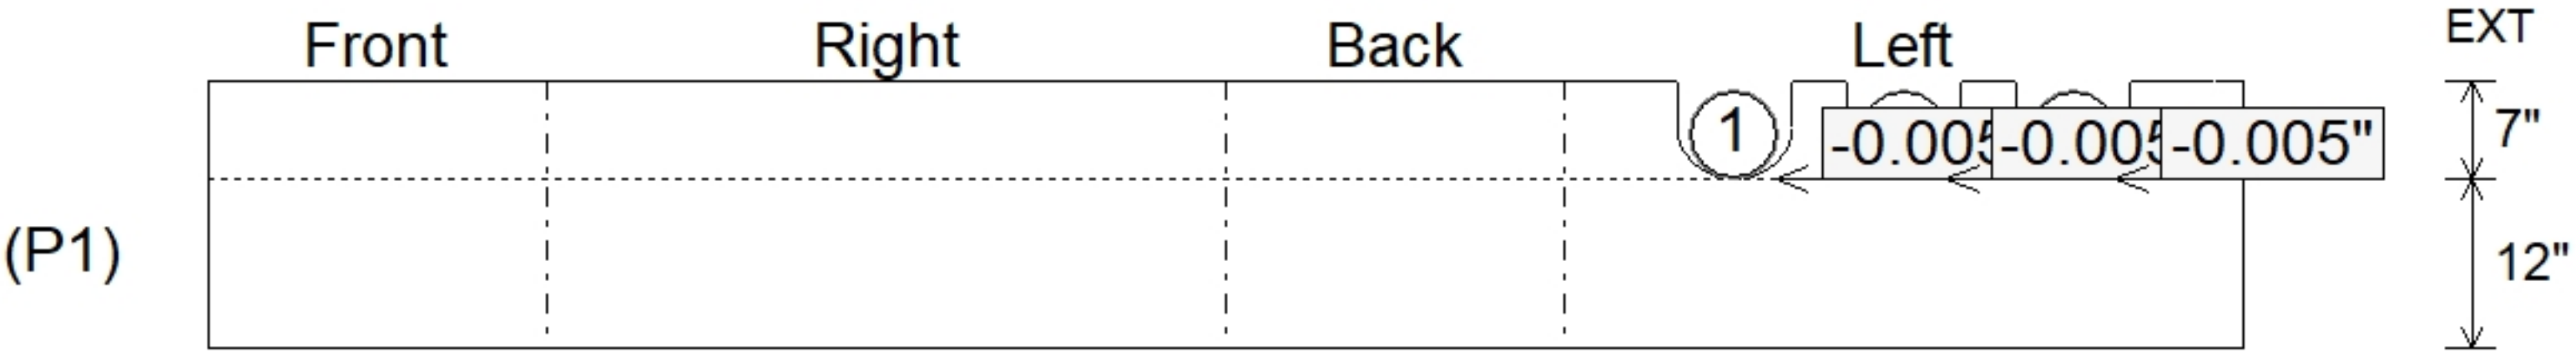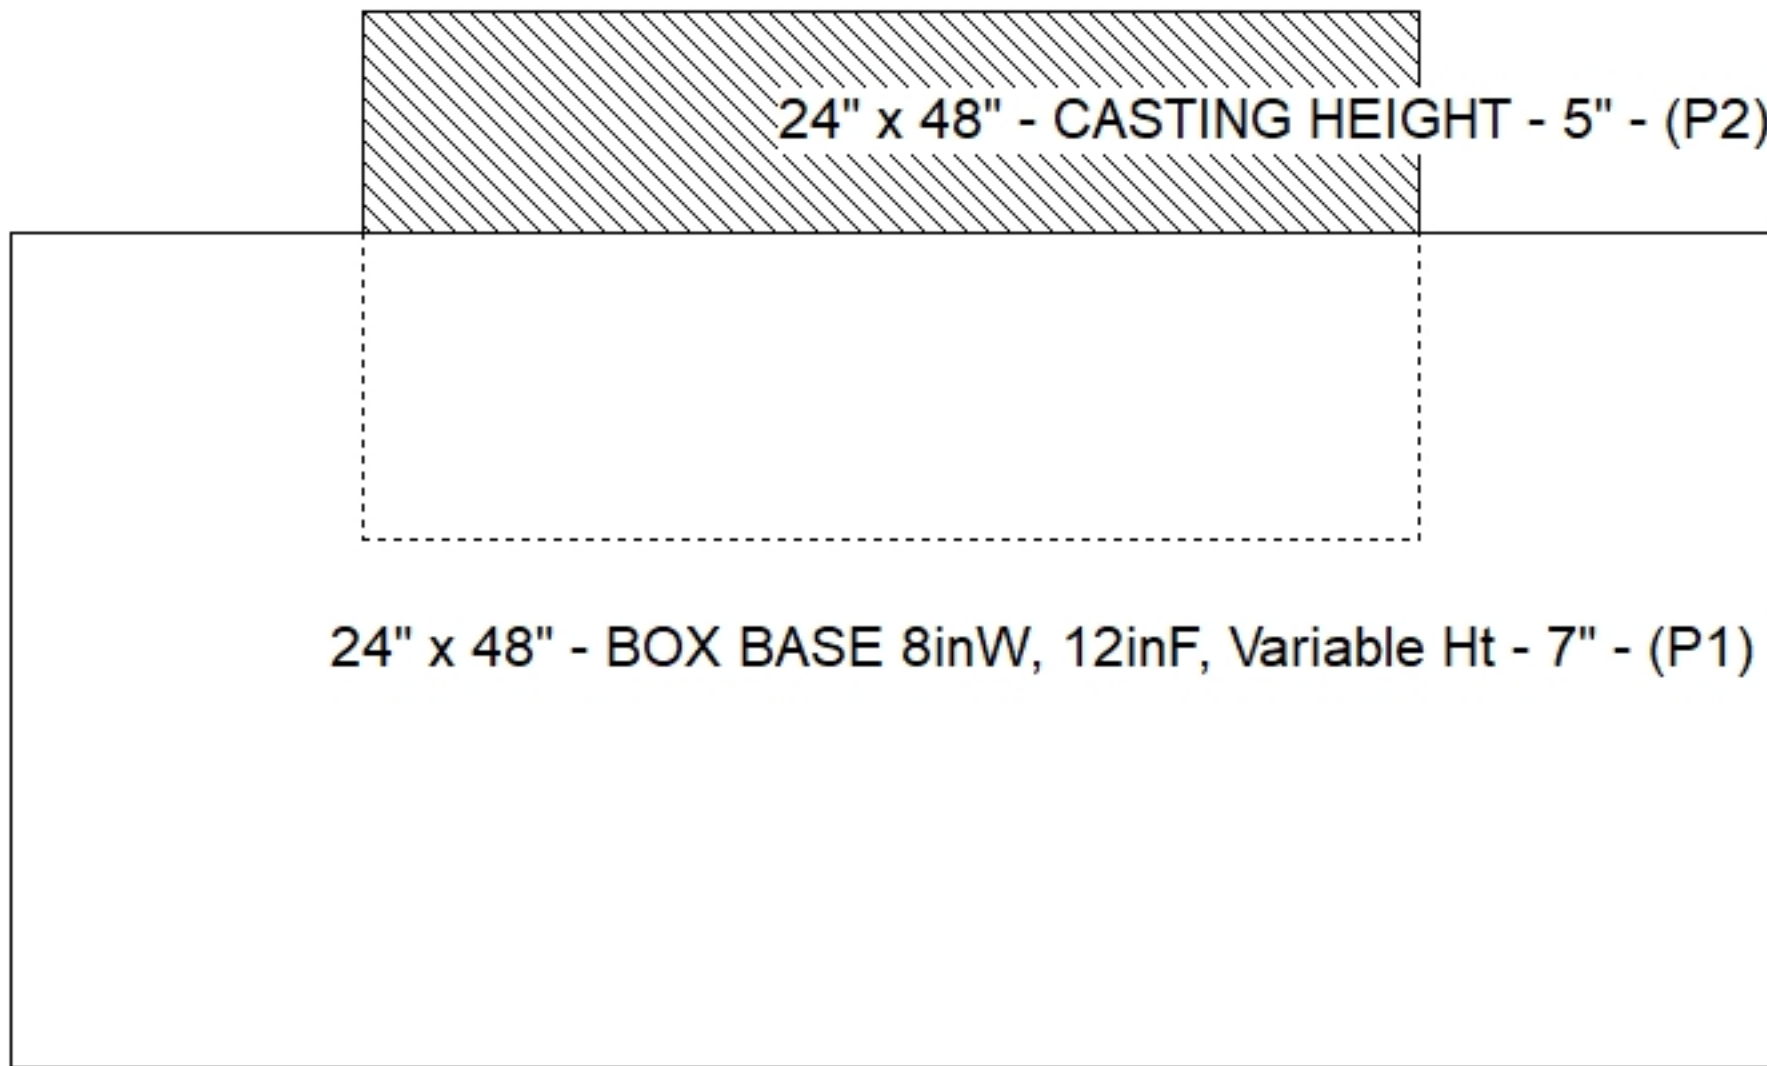

Submittal Drawing
9/29/2026 11:06:00 AM

SUBMITTAL
APPROVED BY:
