

Job Name: 26-2791 788327 2221 Bradford Dr
Job Location: Louisville, KY
Contractor: Contech Engineering Solutions

Plant: Beaver Dam

7/14/2026 1:14:14 PM

Tech: S. Felletter

PC: C. Goff



Structure ID: 10-CS-4

P3 MH048LD12-30


MH FLAT LID w/30in ECC Hole F/G

- P4) 30" - CASTING HEIGHT - 4"
P3) 48" - MH FLAT LID w/30in ECC Hole F/G - 12"
P2) 48" - MH RISER T/G - 72"
P1) 48" - MH BASE T/n - 18"
1) ASSEMBLY REQUIRED
1) CVSTENCILING
2) 48" - Conseal CS-102 1.00"
2) Hole - 16

Structure Total:


0 lb
1413 lb
4856 lb
2588 lb
0 lb
0 lb
0 lb
0 lb
8857 lb

Structure Notes:
4" CASTING BY OTHERS
LIFTING ANCHORS TO BE INSTALLED
ON THE OUTSIDE OF THE STRUCTURE
ICAST TO INSTALL THE INTERNALS
CONTECH'S LOGO AS WELL AS THE
INLET AND OUTLET MUST BE
STENCILED ONTO THE STRUCTURE

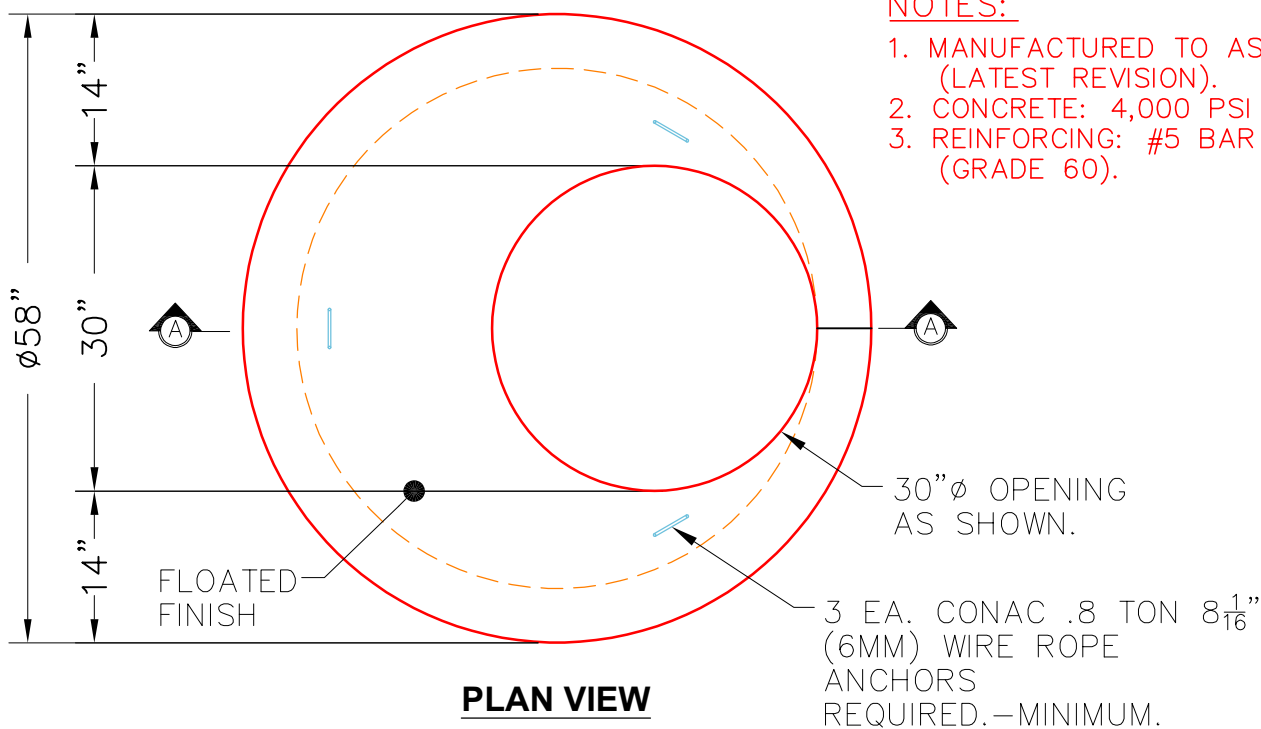

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" C.C. E.W. (GRADE 60).

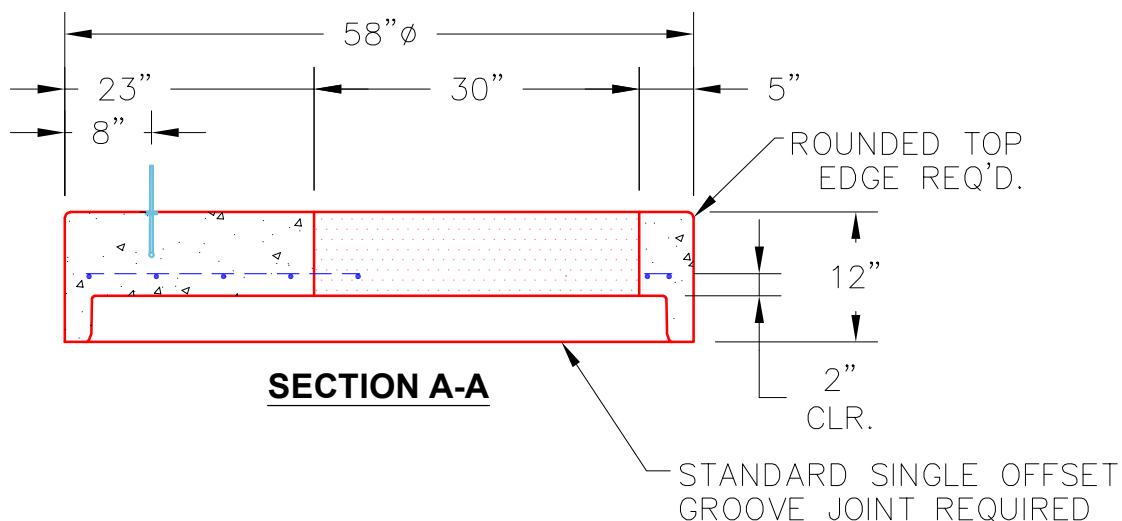

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 12"

Weight (Net): 1413 lb
Volume (Net): 0.36cu.yd
