

Job Name: 26-2800 901652 13635 Telegraph Road

Job Location: CPU

Contractor: Contech Engineering Solutions

Plant: Beaver Dam

6/30/2026 1:03:34 PM

Tech: S. Felletter

PC: C. Goff



Structure ID: 15-CS-6

P1MH072BAVF

MH BASE (09"F) Custom Ht T/n

P4) 30" - CASTING HEIGHT - 0"

P3) 72" - MH FLAT TOP w/ 30" CASTING CAST IN F/G - 15"

P2) 72" - MH RISER Custom Ht T/G - 70"

P1) 72" - MH BASE (09"F) Custom Ht T/n - 24"

1) ASSEMBLY REQUIRED

1) CVSTENCILING

2) 72" - Conseal CS-102 1.00"

2) Hole - 16

0 lb

4663 lb

9967 lb

7886 lb

0 lb

0 lb

0 lb

0 lb

Structure Total: 22515 lb

Structure Notes:

4" CASTING BY OTHERS

LIFTING ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE

ICAST TO INSTALL THE INTERNALS


CONTECH'S LOGO AS WELL AS THE INLET AND OUTLET MUST BE STENCILED ONTO THE STRUCTURE


9" Thick base slab


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)


UPSIDE-DOWN VIEW (int. dimenions)





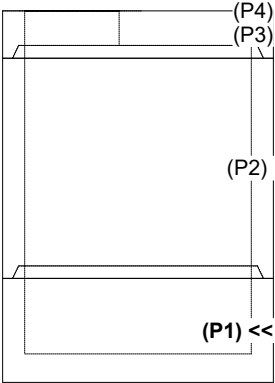

INSIDE WALL DIMENSIONS



Coating (Int):

Coating (Ext):

Seam Up: Tongue

Seam Dn: n/a

Wall Thickness: 7"

Floor Height: 9"

Height (Int): 24"

Height (Ext): 33"

Weight (Net): 7886 lb

Volume (Net): 2.01cu.yd
