

Job Name: 26-2800 901652 13635 Telegraph Road
Job Location: CPU
Contractor: Contech Engineering Solutions

Plant: Beaver Dam
6/30/2026 1:03:46 PM

Tech: S. Felletter
PC: C. Goff



Structure ID: 15-CS-6

P3 MH072LD15SP

MH FLAT TOP w/ 30" CASTING CAST IN F/G



- P4) 30" - CASTING HEIGHT - 0"
P3) 72" - MH FLAT TOP w/ 30" CASTING CAST IN F/G - 15"
P2) 72" - MH RISER Custom Ht T/G - 70"
P1) 72" - MH BASE (09"F) Custom Ht T/n - 24"
1) ASSEMBLY REQUIRED
1) CVSTENCILING
2) 72" - Conseal CS-102 1.00"
2) Hole - 16

0 lb
4663 lb
9967 lb
7886 lb
0 lb
0 lb
0 lb
0 lb
Structure Total: 22515 lb

Structure Notes:
4" CASTING BY OTHERS
LIFTING ANCHORS TO BE INSTALLED
ON THE OUTSIDE OF THE STRUCTURE
ICAST TO INSTALL THE INTERNALS
CONTECH'S LOGO AS WELL AS THE
INLET AND OUTLET MUST BE
STENCILED ONTO THE STRUCTURE

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" C.C. E.W. (GRADE 60).

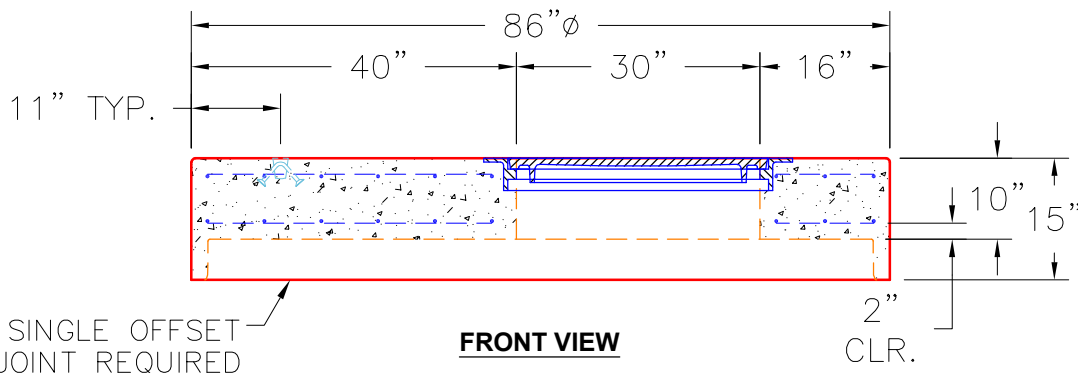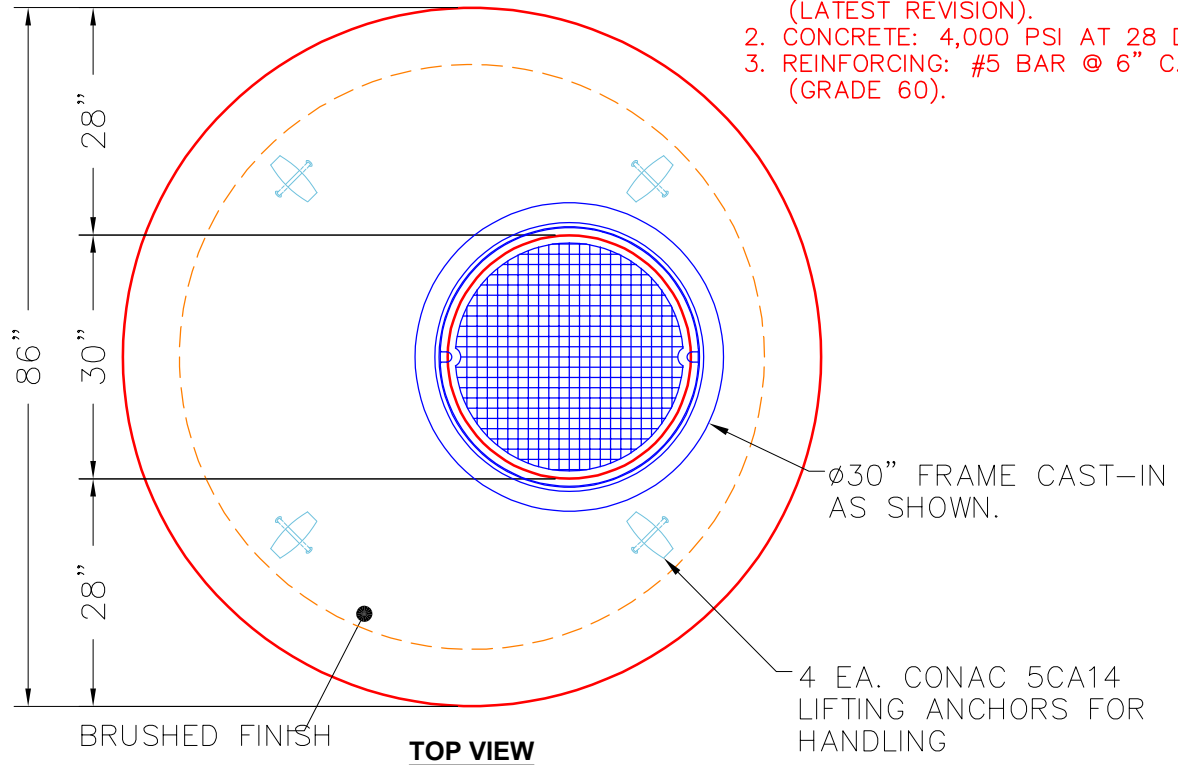

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 7"

Height (Ext): 15"

Weight (Net): 4663 lb
Volume (Net): 1.19cu.yd
