

Contractor: Stemaly Excavating Inc.

TECH: Jared - F

Plant: 100



Size: 72" x 144"

Rim to Invert: 2.42'

Floor Height: 6"


Slack: 0"

1. PER ASTM C-890-13 SPECIFICATIONS.
2. CONCRETE = 5,000 PSI AT 28 DAYS.
3. NO STEPS AND NO FLOW CHANNEL.
4. CASTING BY ICAST (2EA. HOE MC-375 F/C GREASE)
5. SECONDARY POUR REQ'D - BAFFLE WALL.

- FLOOR (As .47) #5 BARS AT 8" C.C.E.W.



07200 lb

Structure Total: 27322 lb

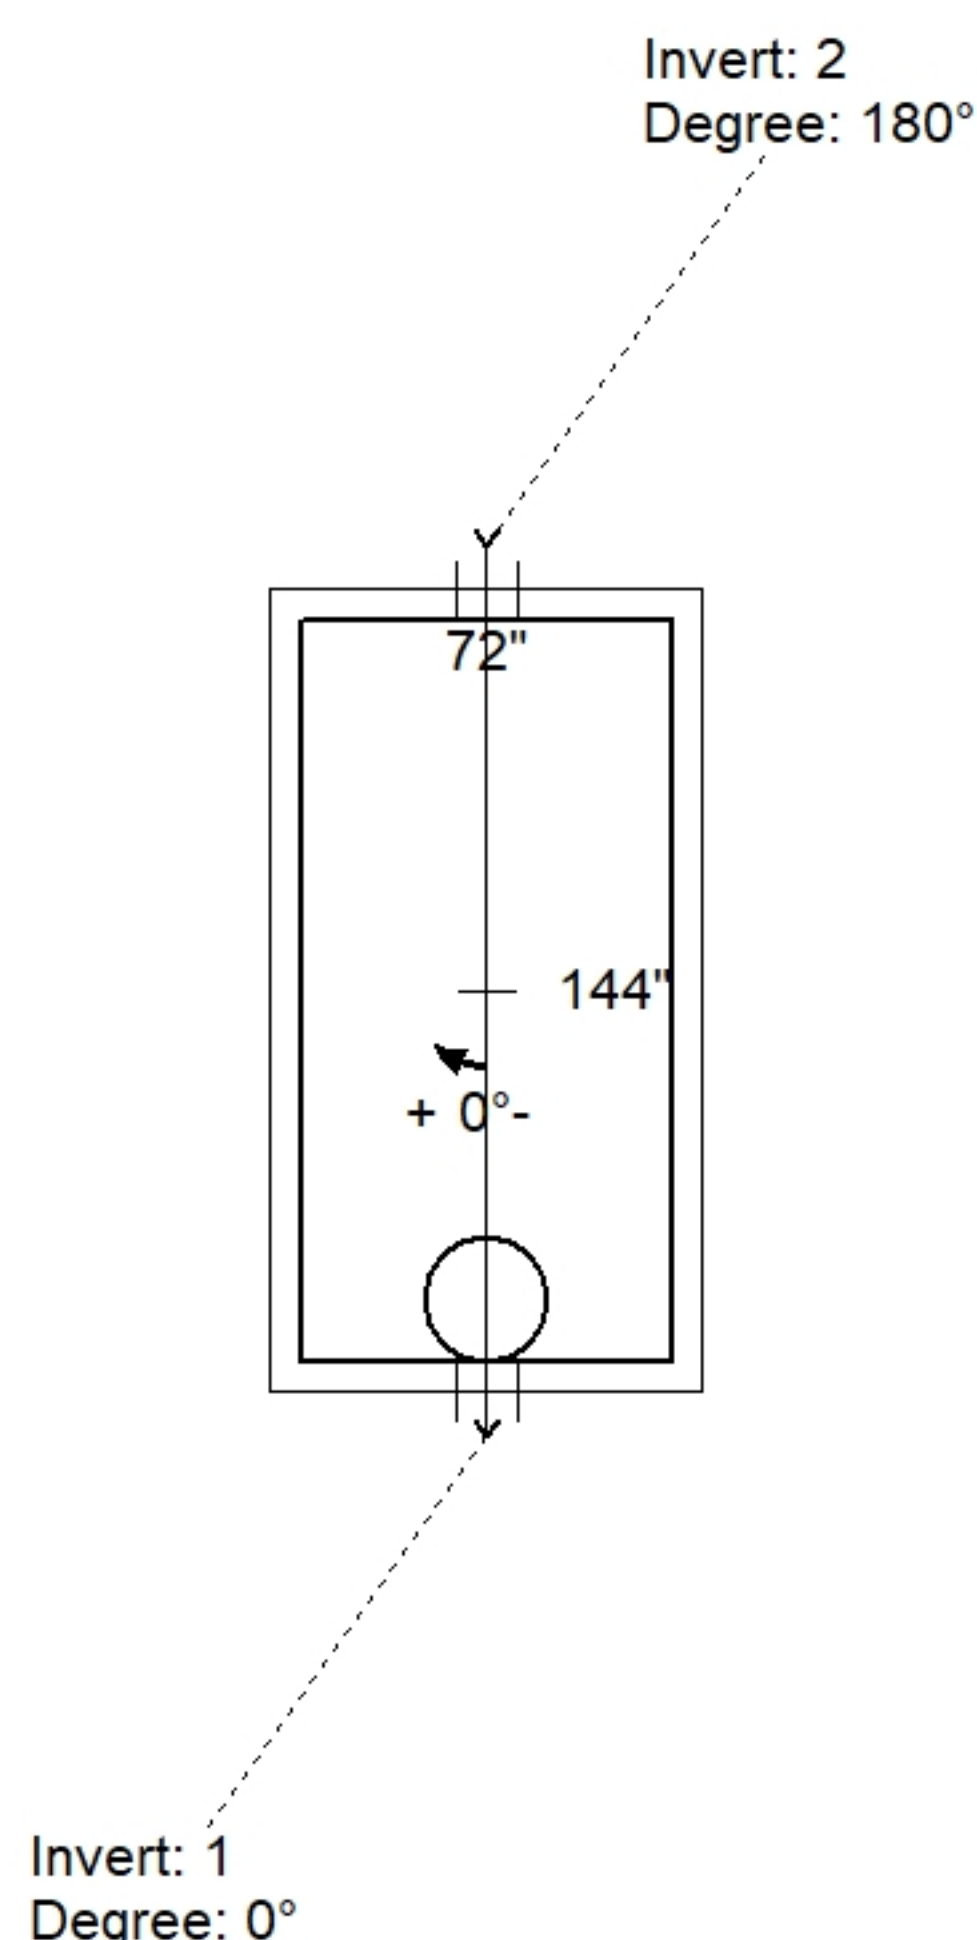

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	5.25'							
Reducer								
Invert 1	2.83'	0°	6" PVC SDR35	6.25"	12"	Kor-N-Seal1 S106-12M	30.96"	P1
Invert 2	3'	180°	6" PVC SDR35	6.25"	12"	Kor-N-Seal1 S106-12M	33"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

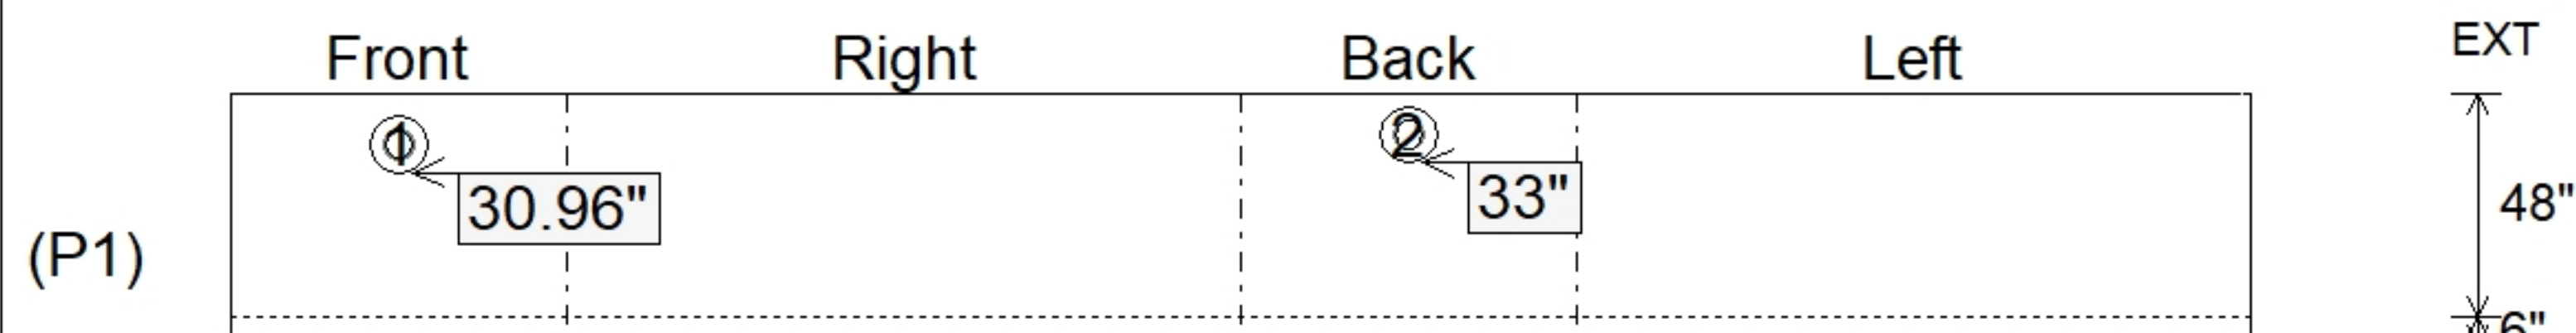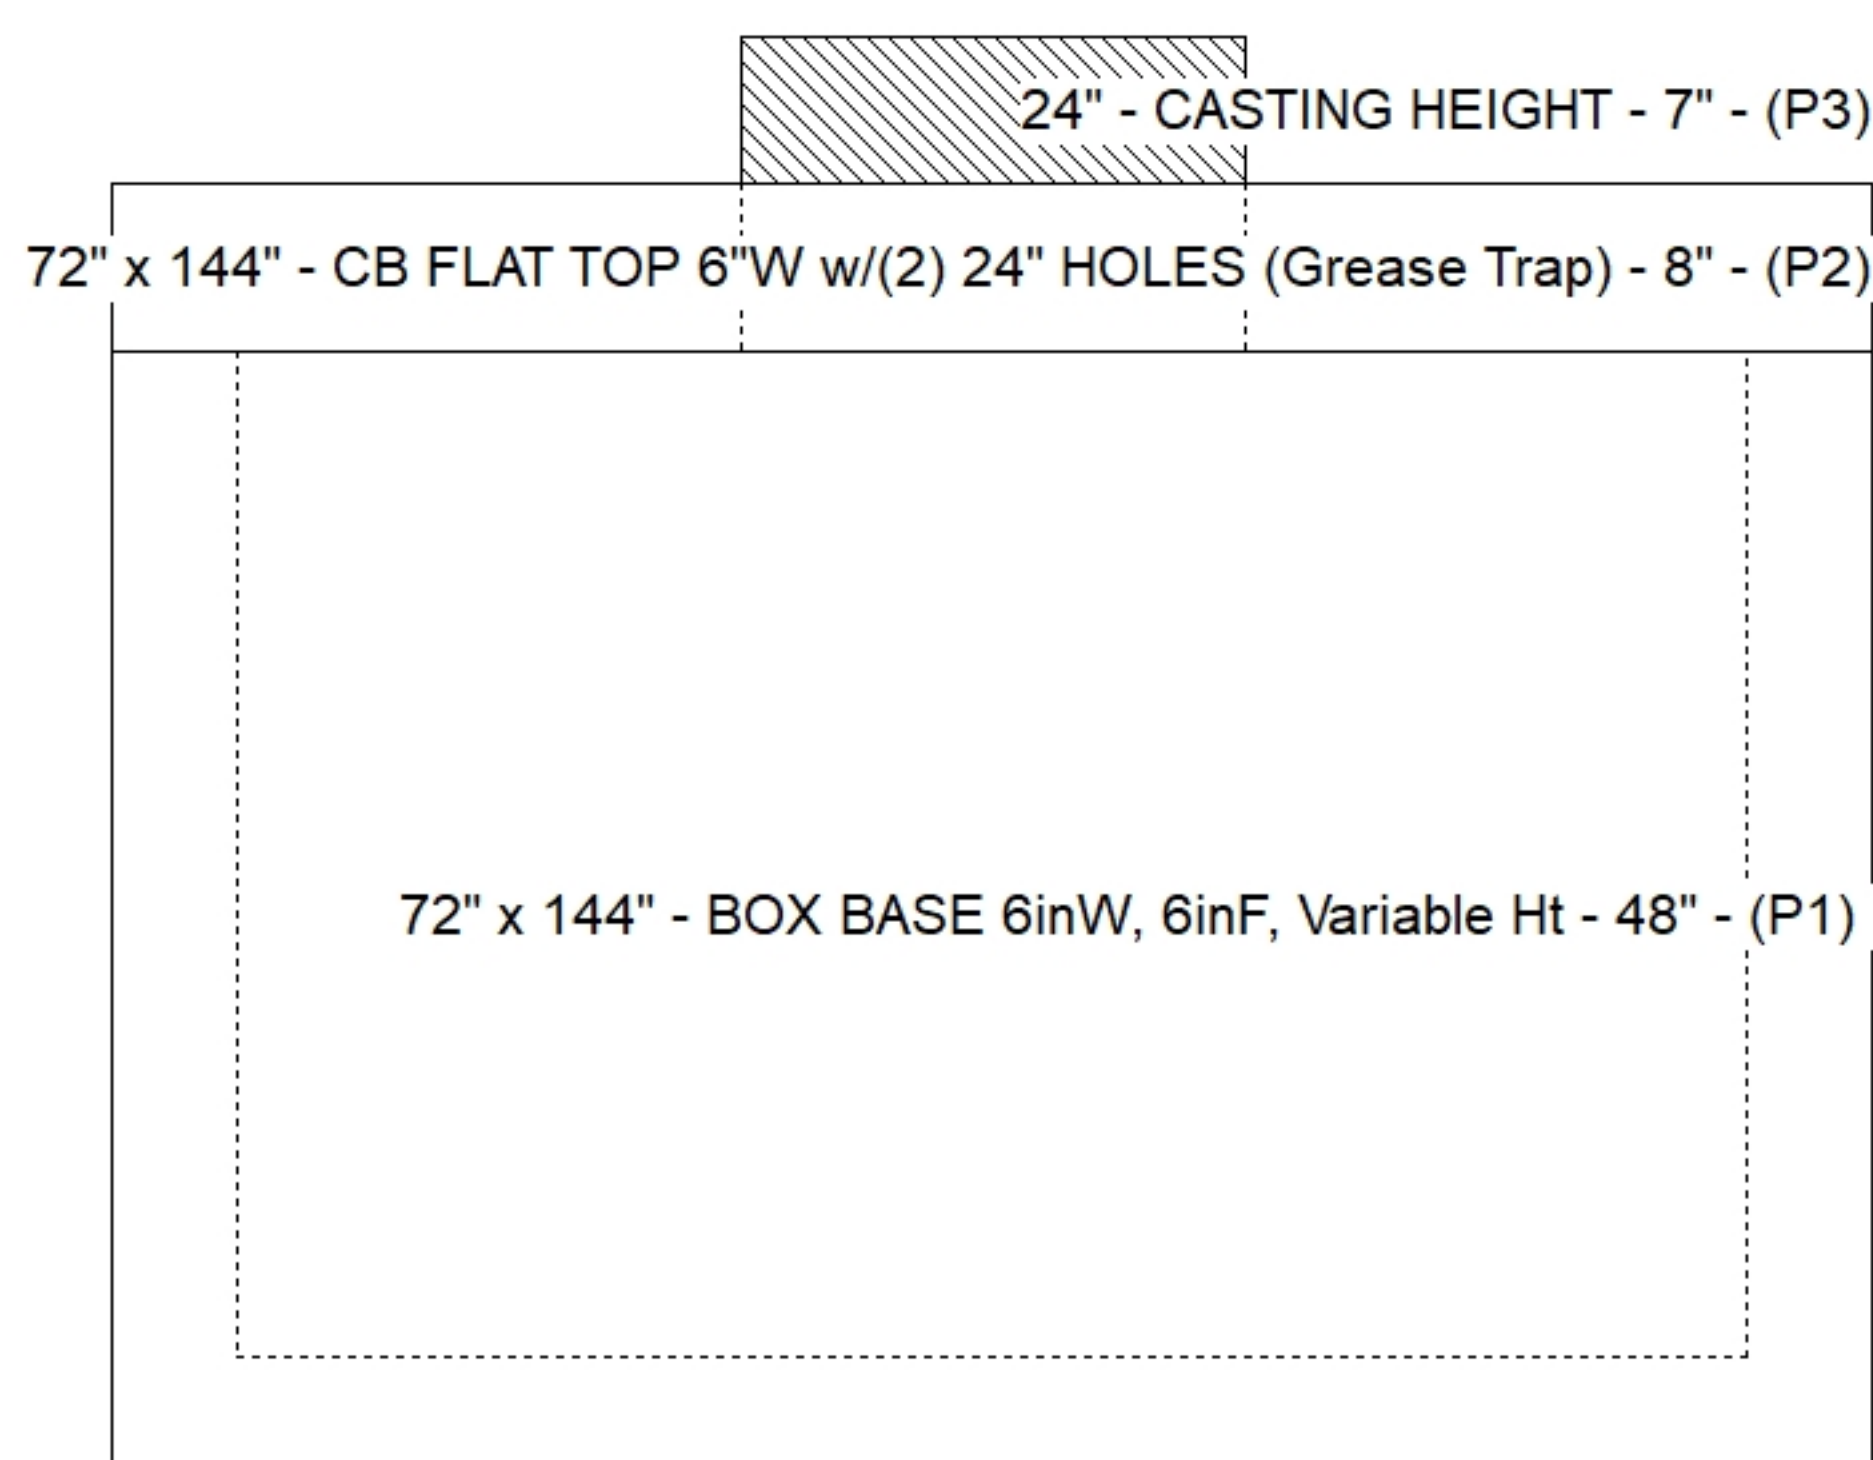

Submittal Drawing
10/2/2026 7:42:45 AM

SUBMITTAL
APPROVED BY:
