

Contractor: Winwater Hartford KY Co.

Plant: 100



Slack: 1.56"


REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


P4) 30" x 30" - CASTING HEIGHT - 4"
P3) 30" x 30" - GRADE RING - 3"
P2) 48" - MH FLAT TOP w/30"x30" Hole - 12"
P1) 48" - MH BASE - 36"
1) CASTING - HOE 468 F/G
1) 48" - Conseal CS-102 1.00"
1) 30" x 30" - Conseal CS-102 1.00"
1) Hole - 24

0 lb
218 lb
1350 lb
3648 lb
489 lb
0 lb
0 lb
0 lb


Structure Total: 5704 lb

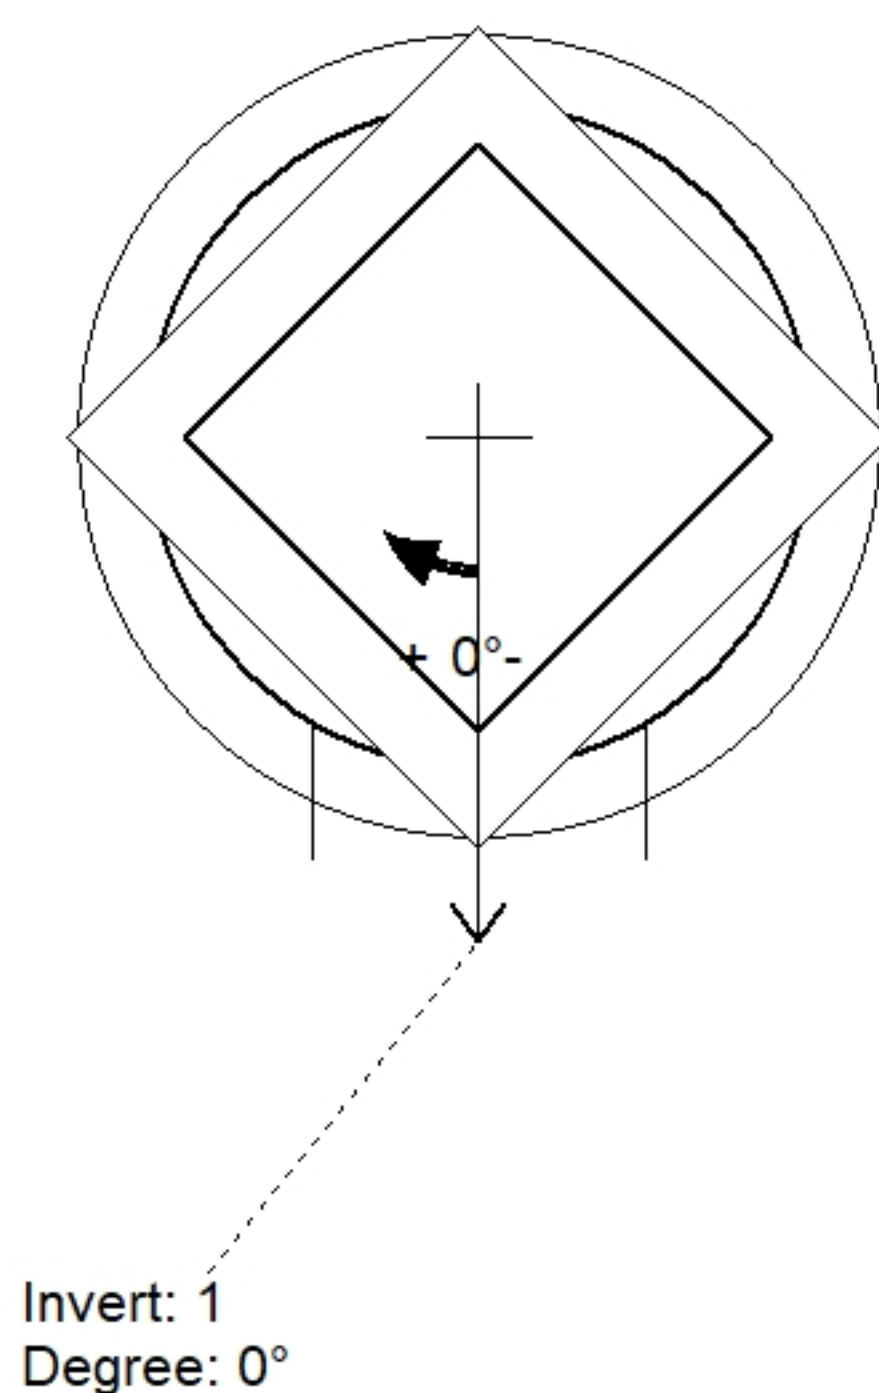

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	435.66'							
Reducer								
Invert 1	431.08'	0°	18" HDPE	21.2"	24"	Hole 24	0"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

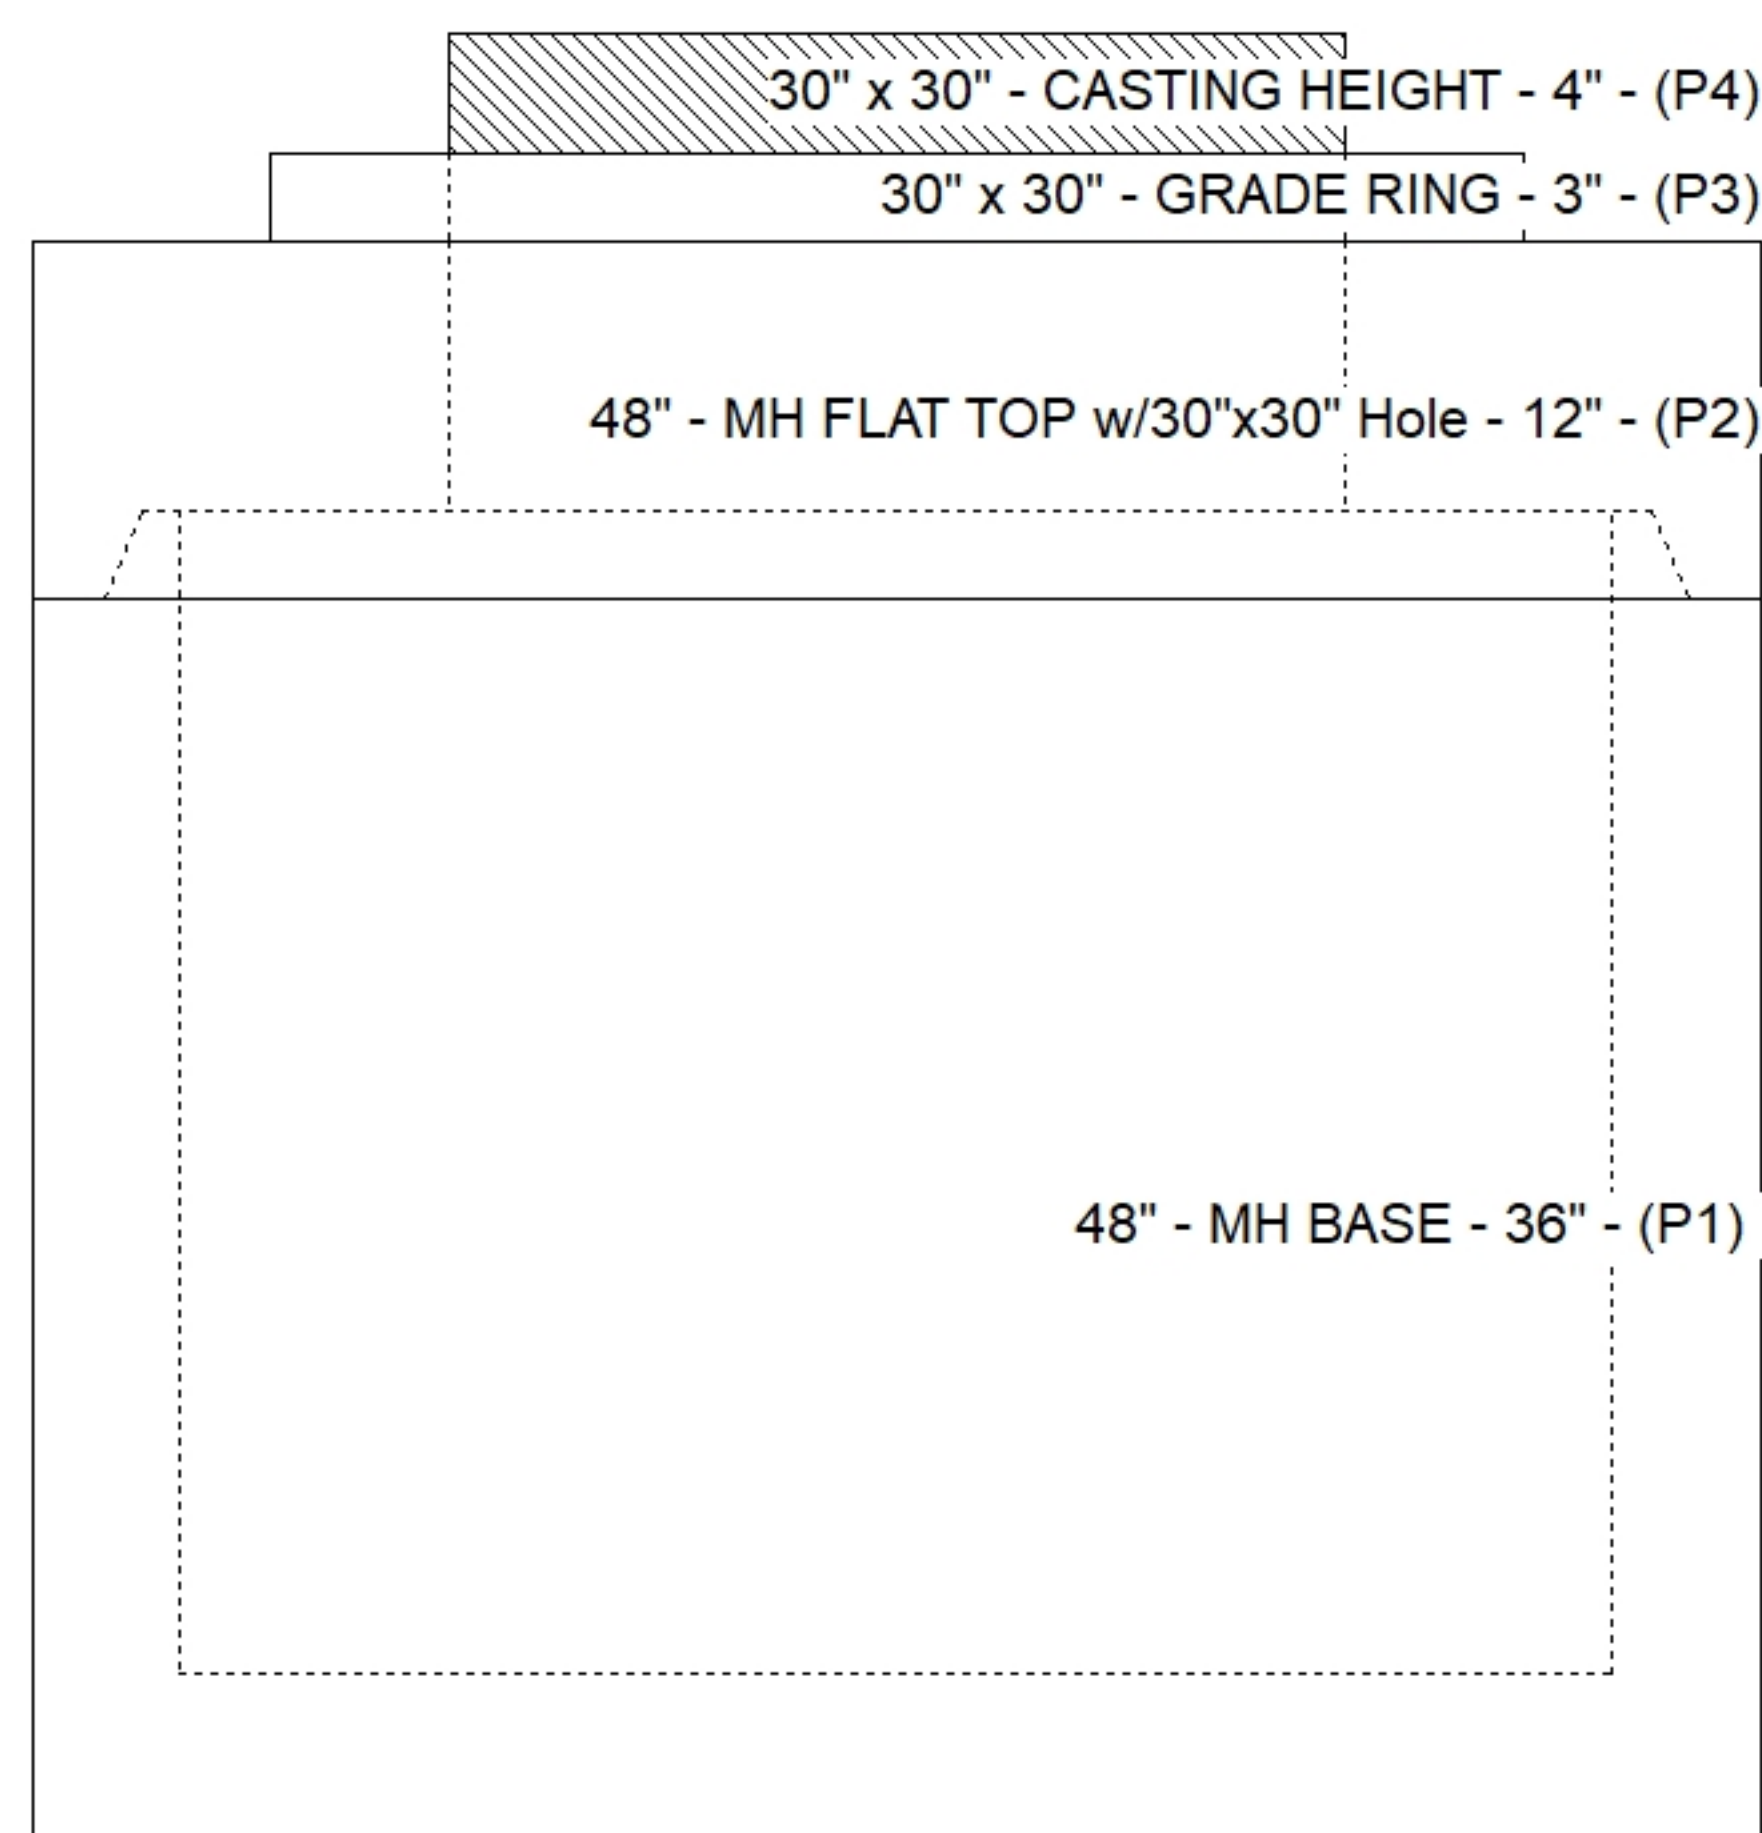

Default - Interior Dimensions

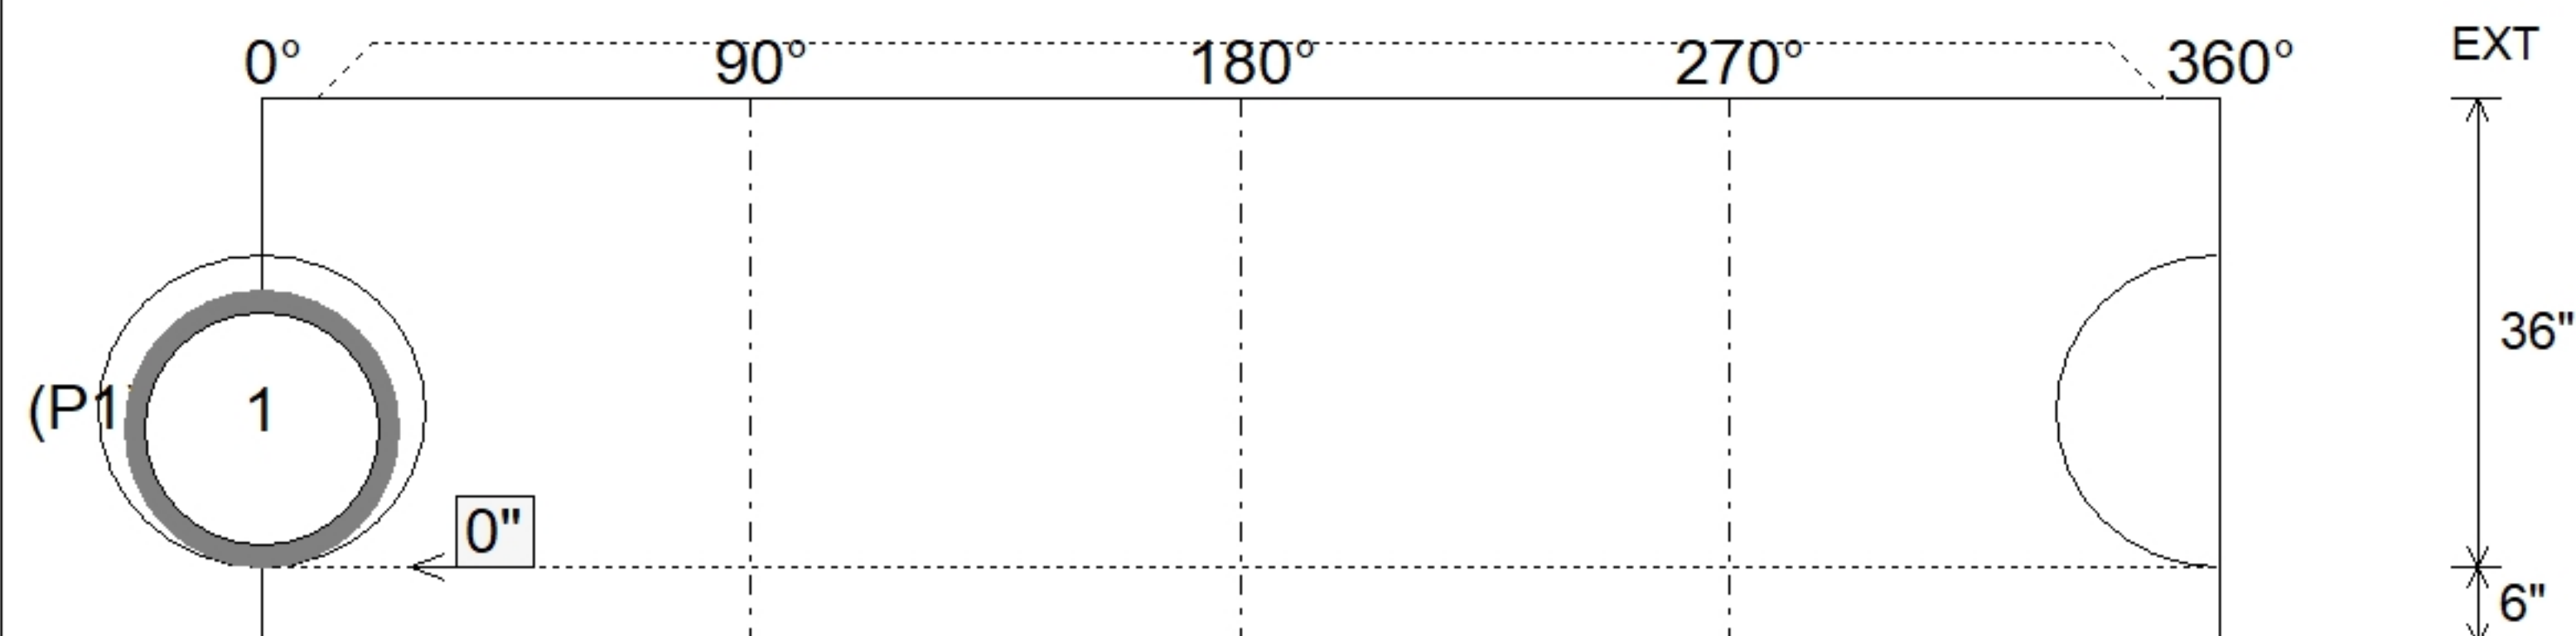

SUBMITTAL
APPROVED BY:
