

Contractor: Byard Construction, LLC

TECH: Jared - F

Plant: 100



Size: 48"

Rim to Invert: 12.88'

Floor Height: 6"


Slack: 0.56"

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

13) MH Step ML-10-TDS-NCR - 10"


0 lb

Structure Total: 13562 lb

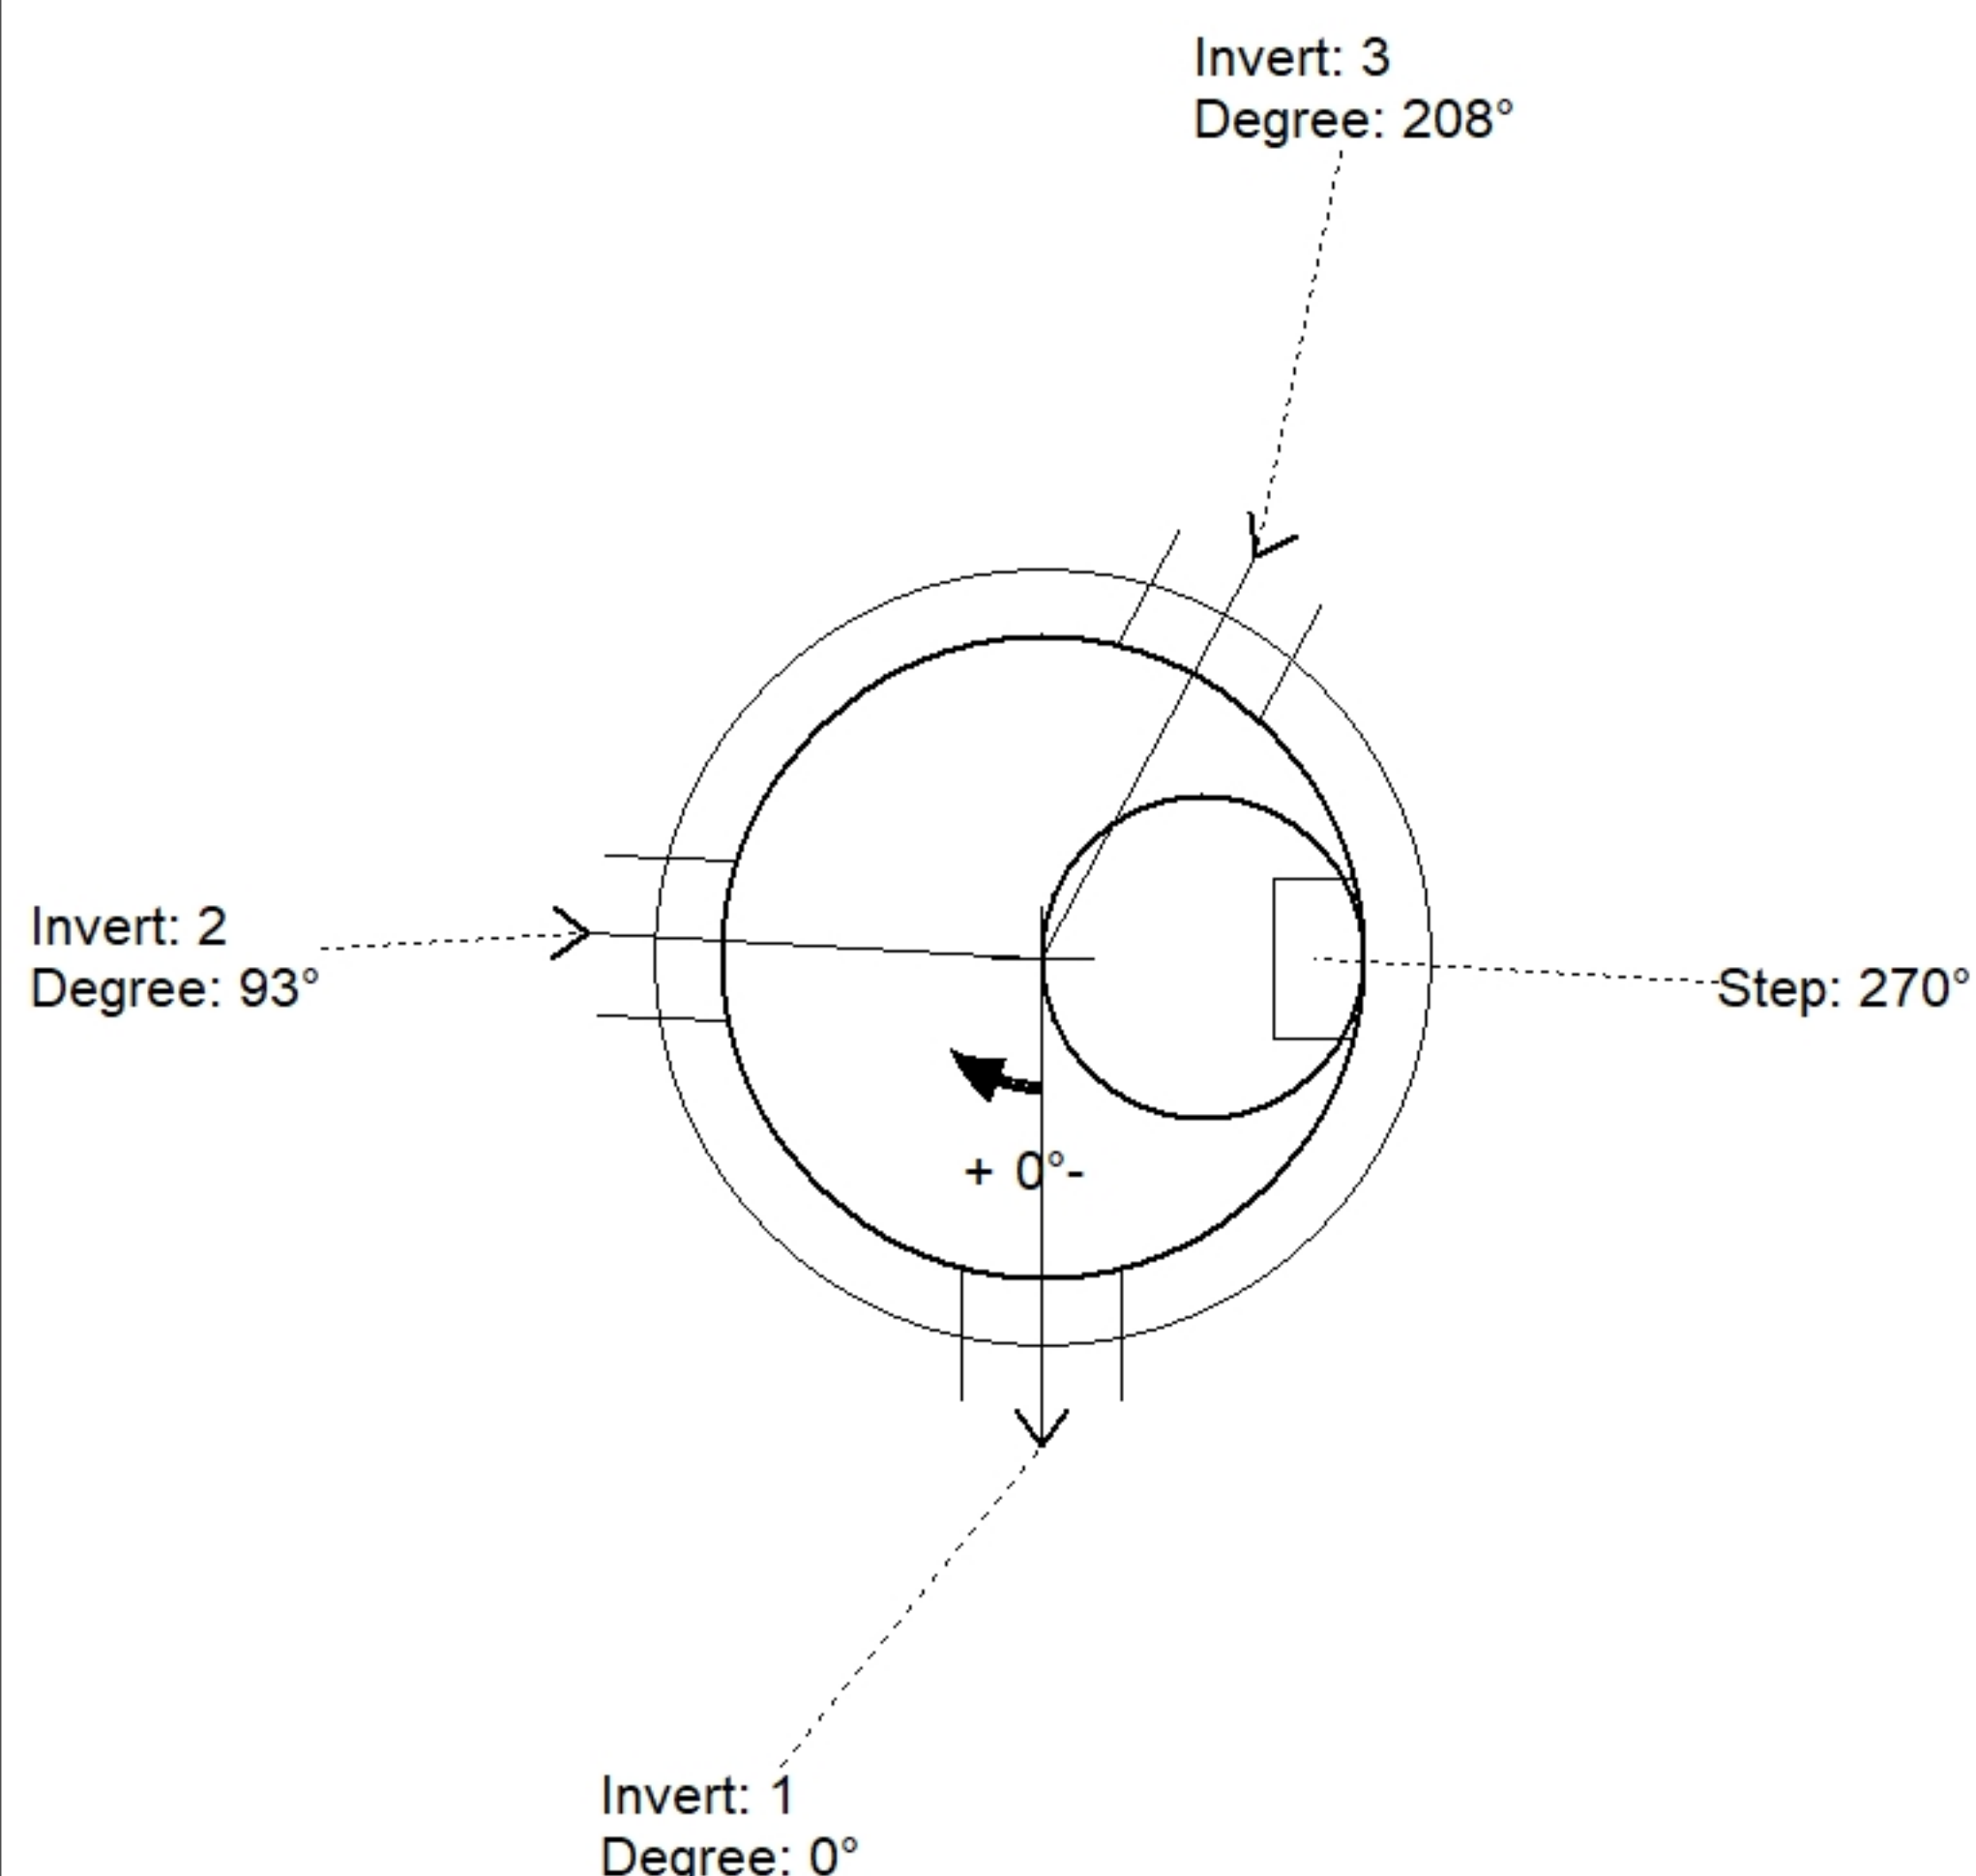

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')_	Ref
Rim	516.84'							
Reducer								
Invert 1	503.96'	0°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	0"	P1
Invert 2	504.06'	93°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	1.2"	P1
Invert 3	504.06'	208°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	1.2"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

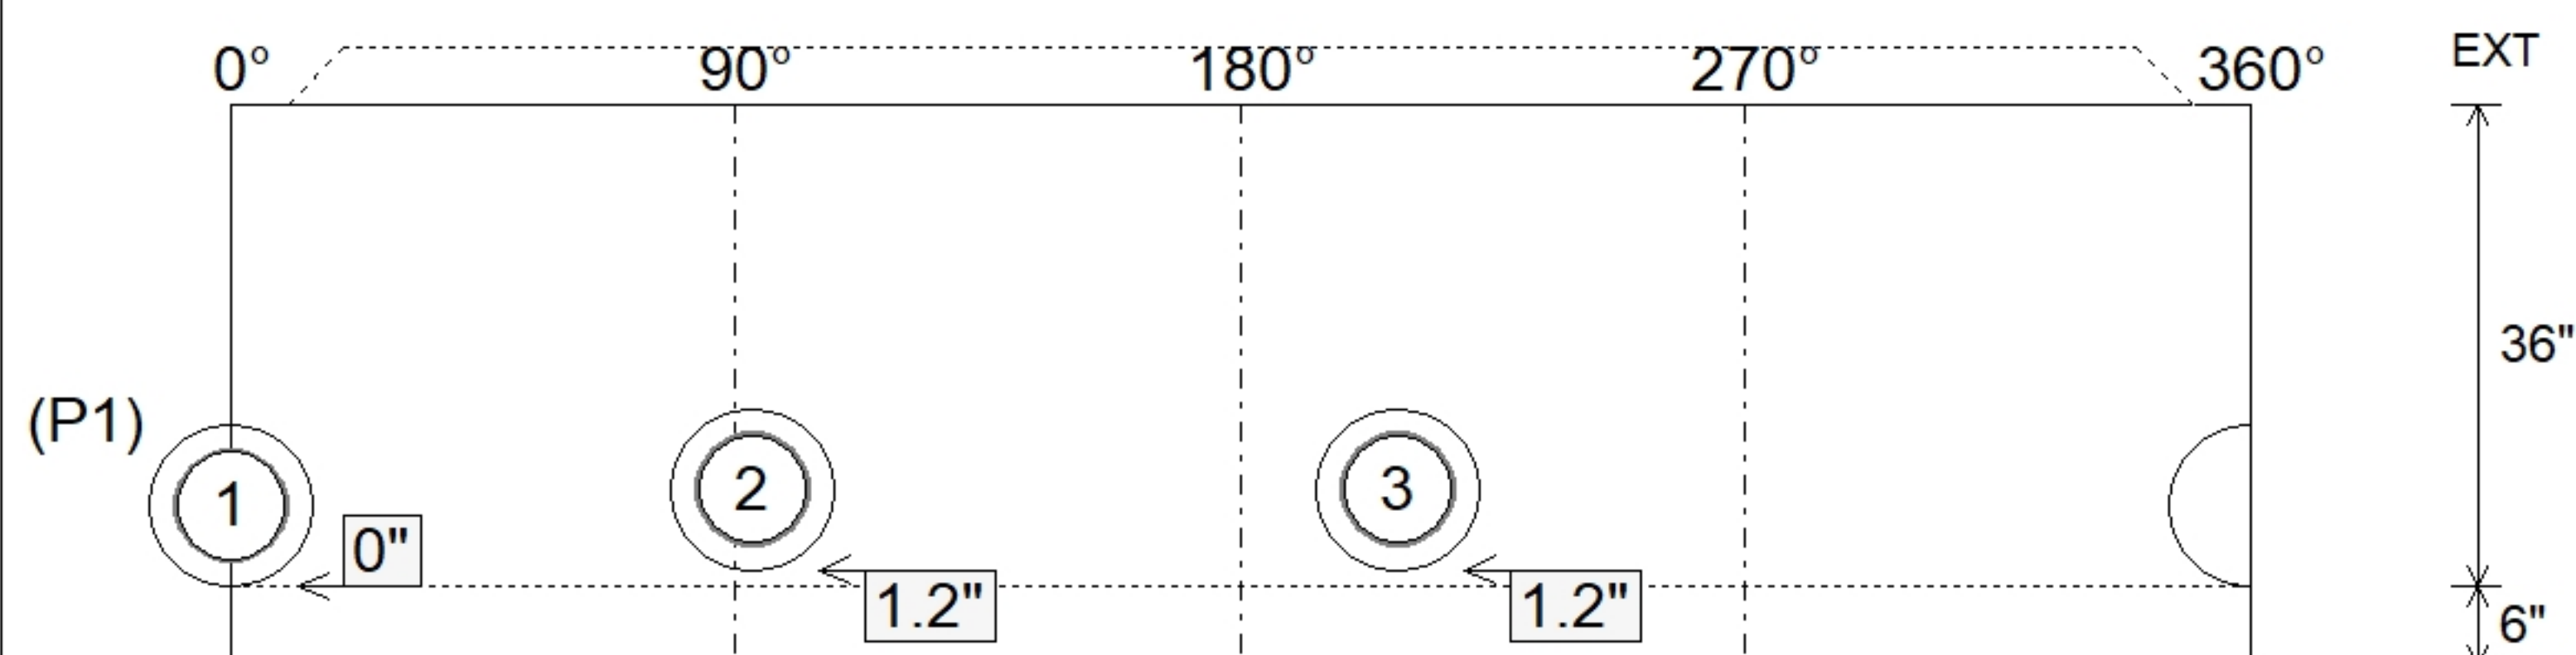

Submittal Drawing
9/24/2026 2:15:45 PM

SUBMITTAL
APPROVED BY:
