


Job Name: 26-3000 - Whispering Cedars at Black Oaks Job Location: Clarksville, TN 37042 Contractor: Byard Construction, LLC					Plant: 100 9/24/2026 11:25:43 AM		Tech: Jared - F PC: A. Chambers				
Structure ID: B2 SS-MH											
P2 MH048RS60CDARED			MH RISER w/ConBlock-CDA Red T/G								
P4) 24" - CASTING HEIGHT - 6" P3) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 42" P2) 48" - MH RISER w/ConBlock-CDA Red T/G - 60" P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 30" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) ADMIXTURE CONBLOCK CDA RED 1) CASTING - JBS 1155 F/C SANITARY 2) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 1) PSX - 8QRS-S NYLO 11) MH Step ML-10-TDS-NCR - 10"					0 lb 3116 lb 4192 lb 3309 lb 0 lb 0 lb 1440 lb 0 lb 250 lb 0 lb 0 lb 16 lb 6 lb 0 lb ----- Structure Total: 12329 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIXTURE = CONBLOCK CDA RED. 4. CASTING BY ICAST (JBS 1155 F/C SANITARY). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 516.26' Rim to Invert: 11.36' Slack: 0.32" Sump: 2" Step Position: 65											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

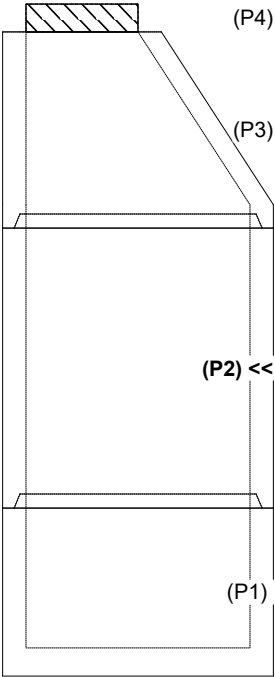


(P4)

(P3)

(P2) <<

(P1)


RIGHT-SIDE UP VIEW (int. dimensions)

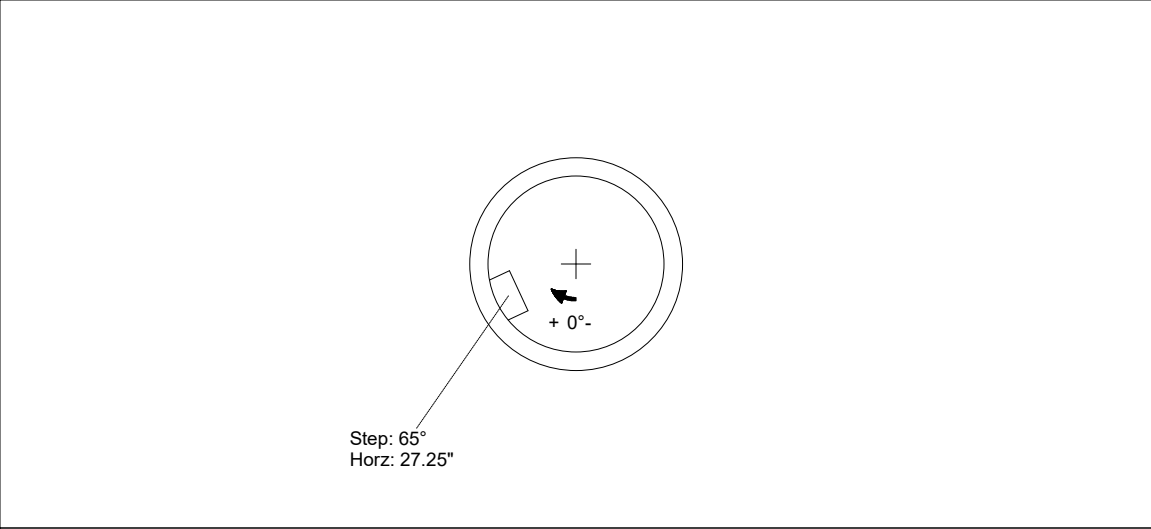

Step: 65°
Horz: 27.25"

+ 0°-

INSIDE WALL DIMENSIONS

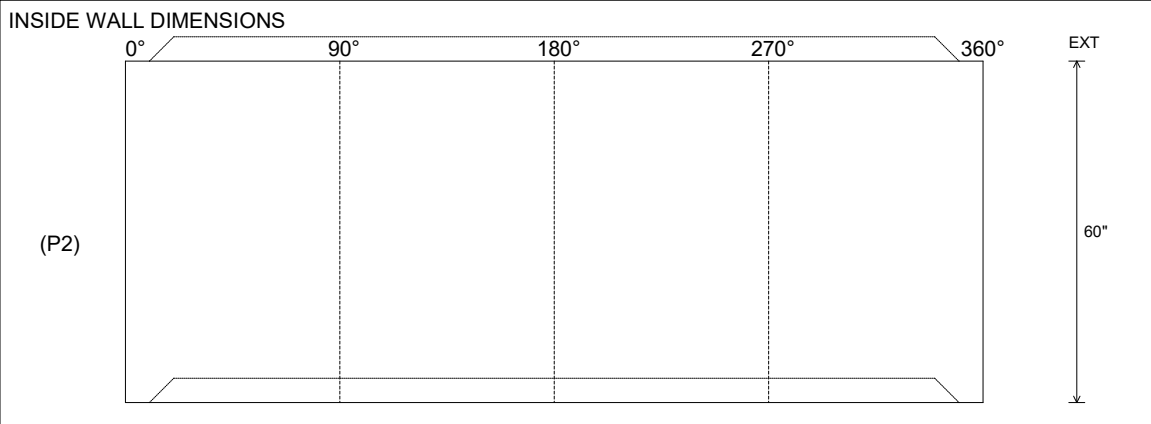

(P2)

0° 90° 180° 270° 360°

EXT

60"

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 5" Floor Height: 0"	Height (Int): 60" Height (Ext): 60"	Weight (Net): 4192 lb Volume (Net): 1.07cu.yd
----------------------------------	------------------------------------	--	--	--
