

Contractor: Byard Construction, LLC

TECH: Jared - F

Plant: 100



Size: 48"

Rim to Invert: 8.02'

Floor Height: 6"


Slack: 2.24"

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

8) MH Step ML-10-TDS-NCR - 10"



0 lb

Structure Total: 9104 lb

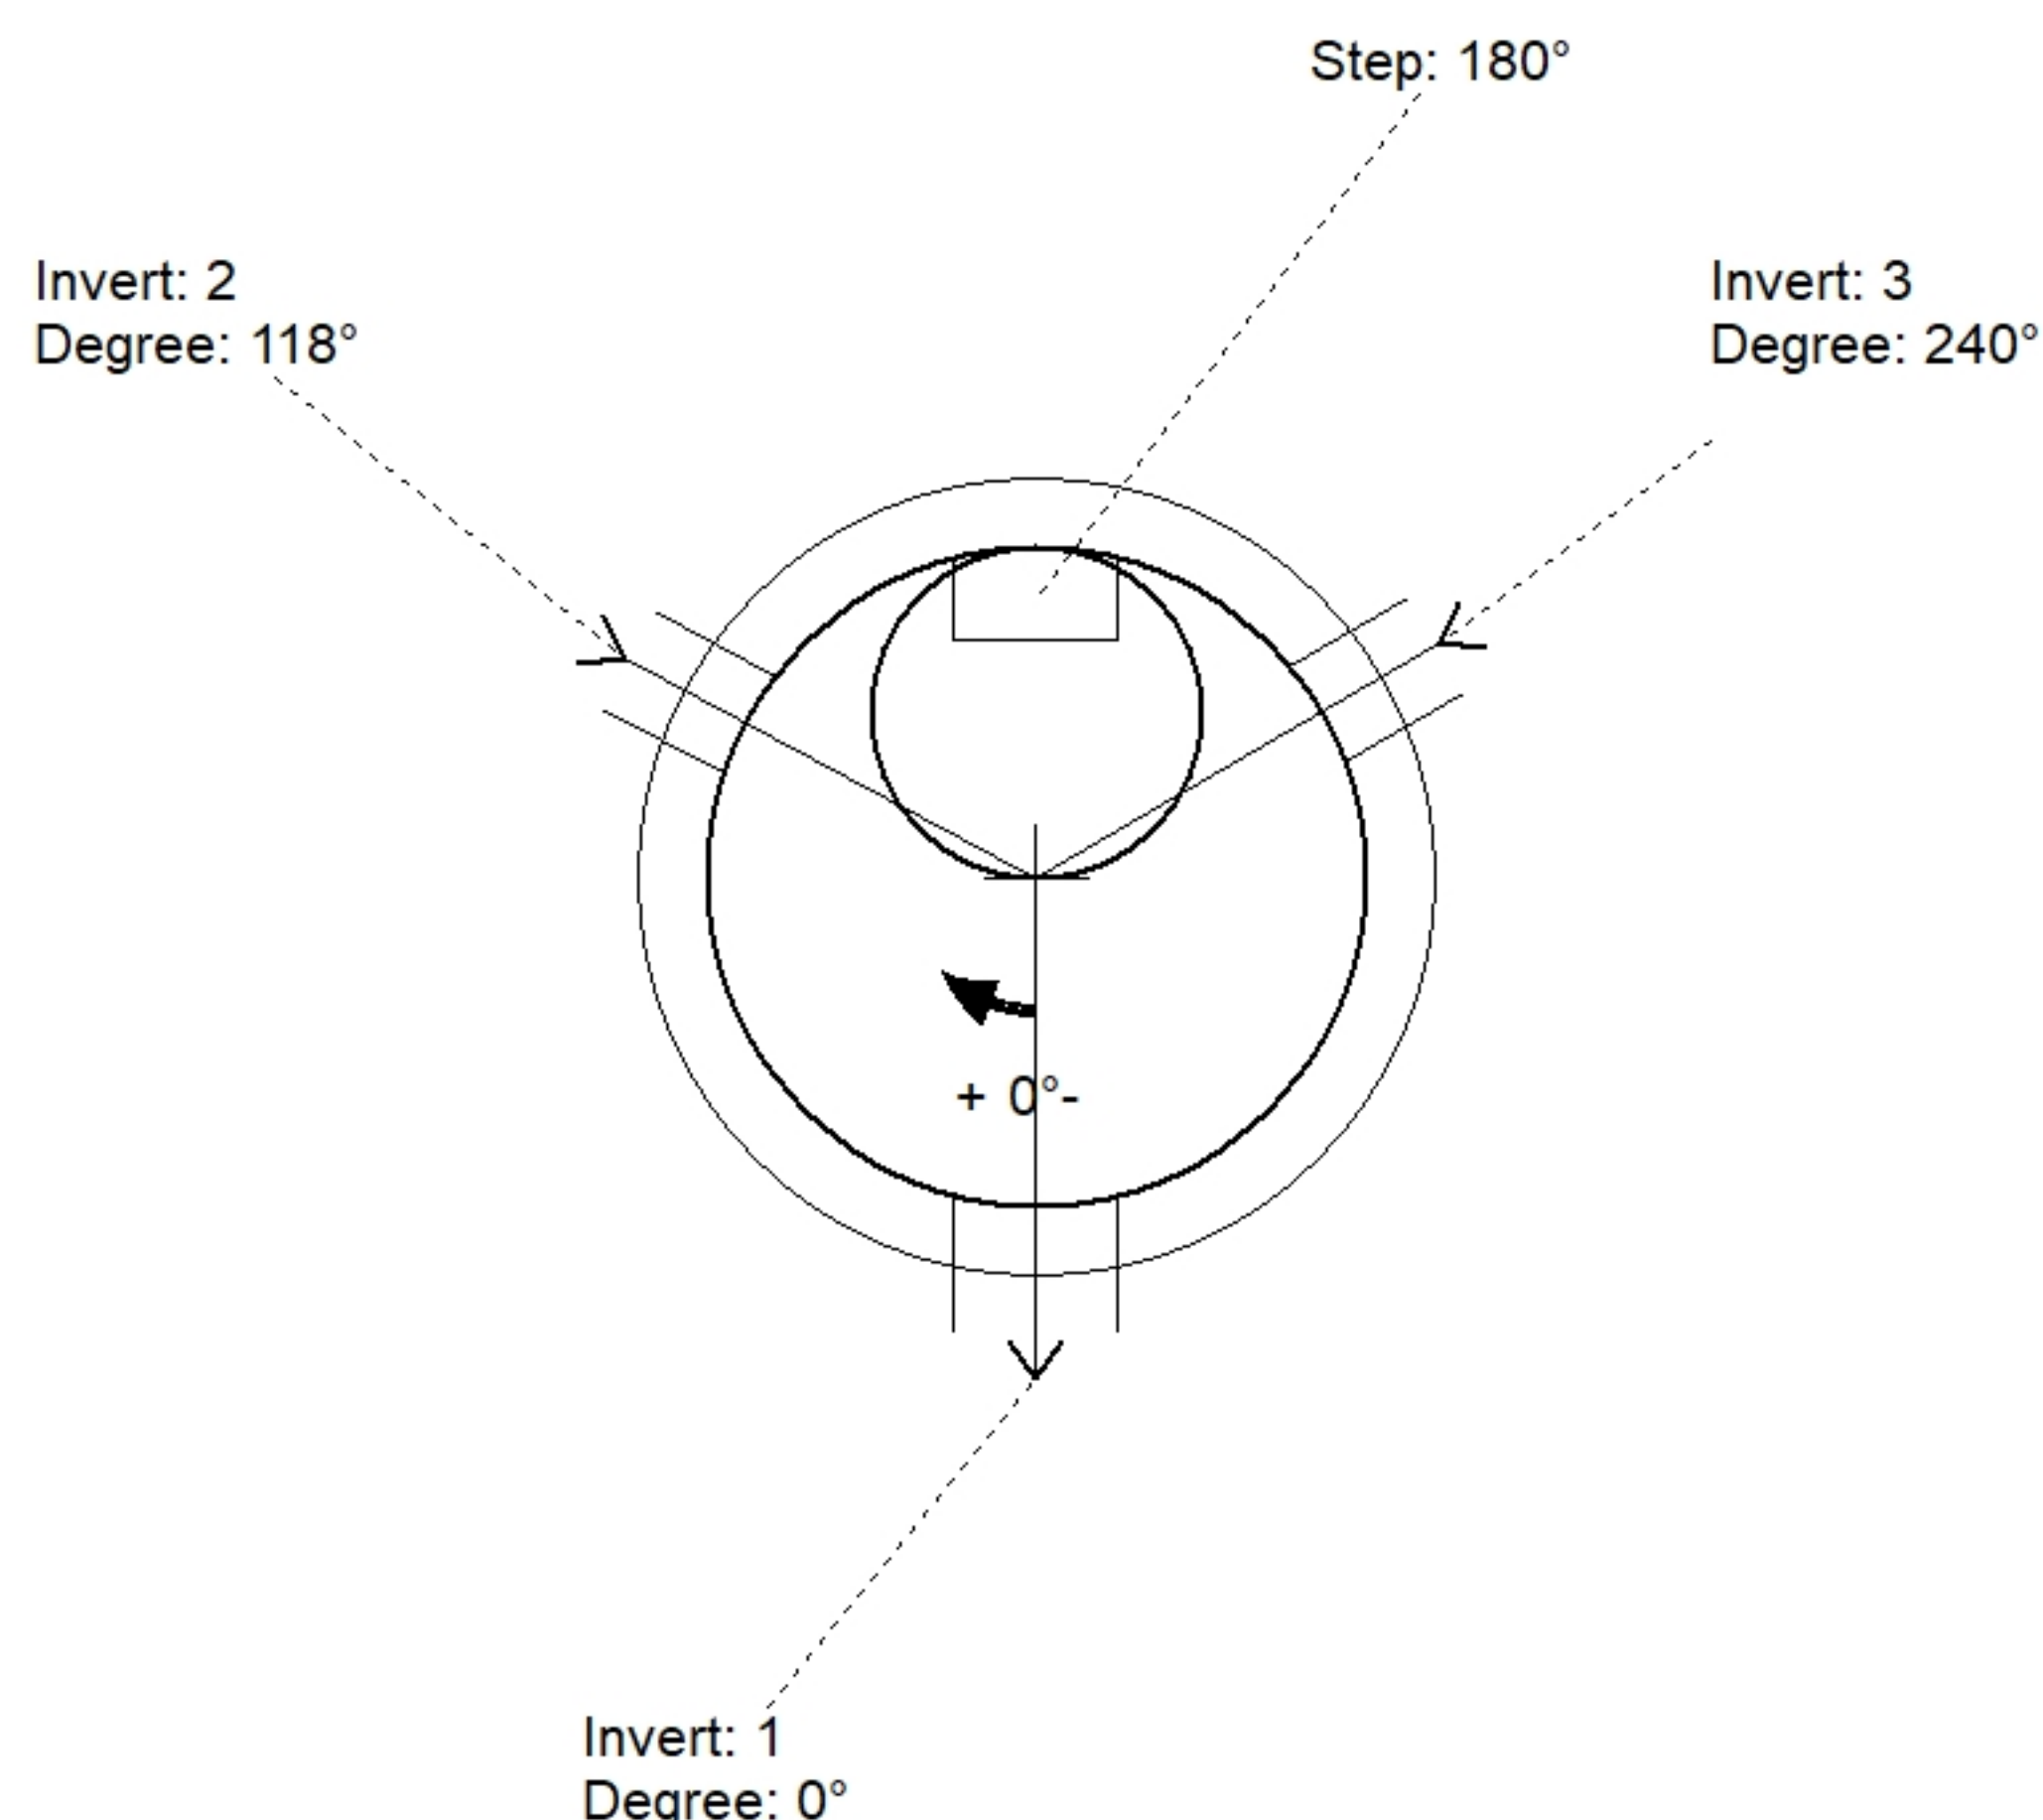

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	514.46'							
Reducer								
Invert 1	506.44'	0°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	0"	P1
Invert 2	506.64'	118°	4" PVC SDR35	4.25"	8"	PSX 8QRS-S NYLO	2.4"	P1
Invert 3	506.64'	240°	4" PVC SDR35	4.25"	8"	PSX 8QRS-S NYLO	2.4"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

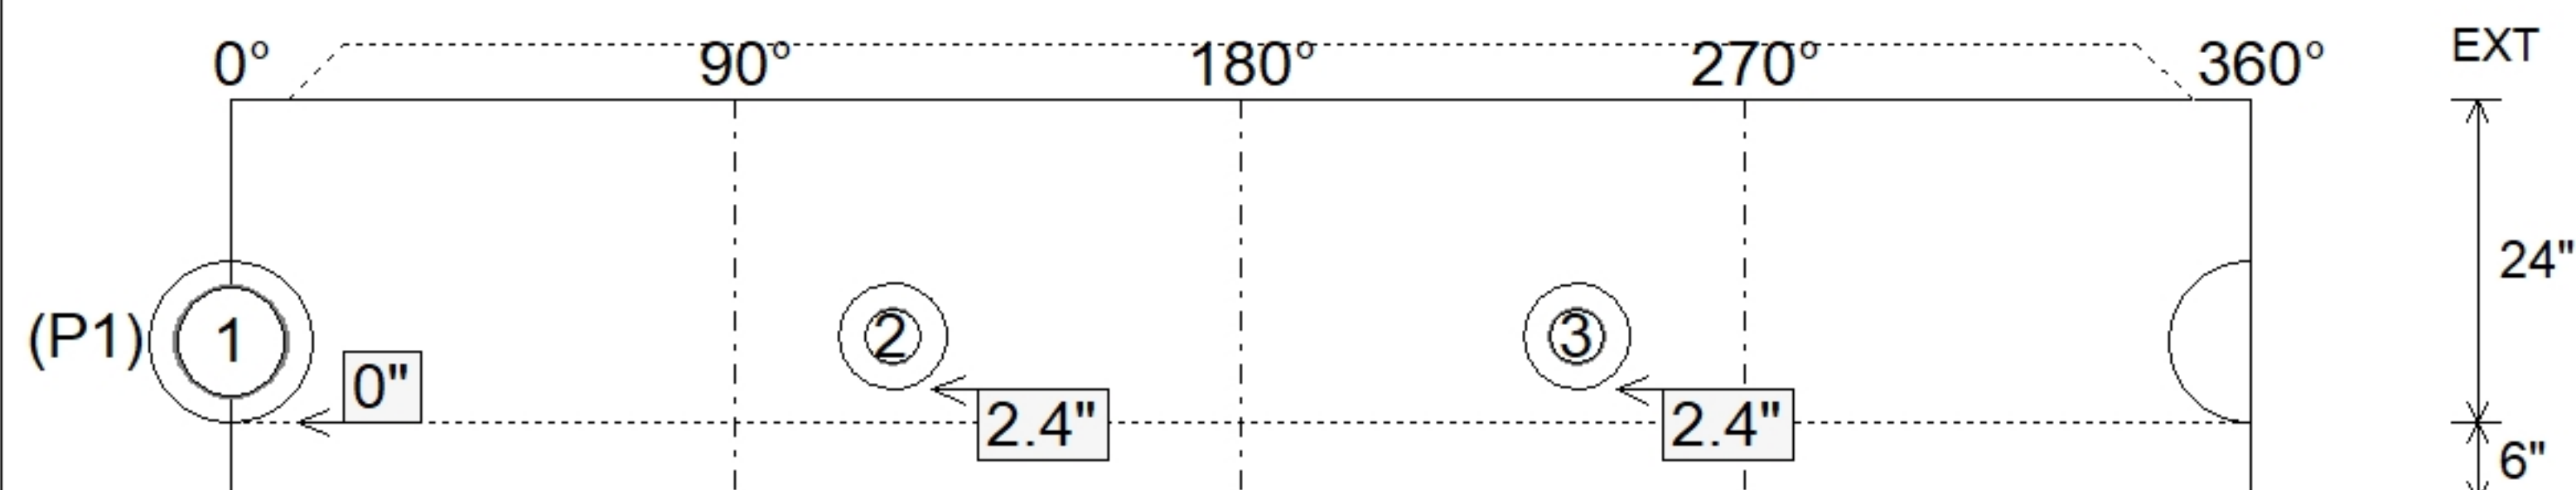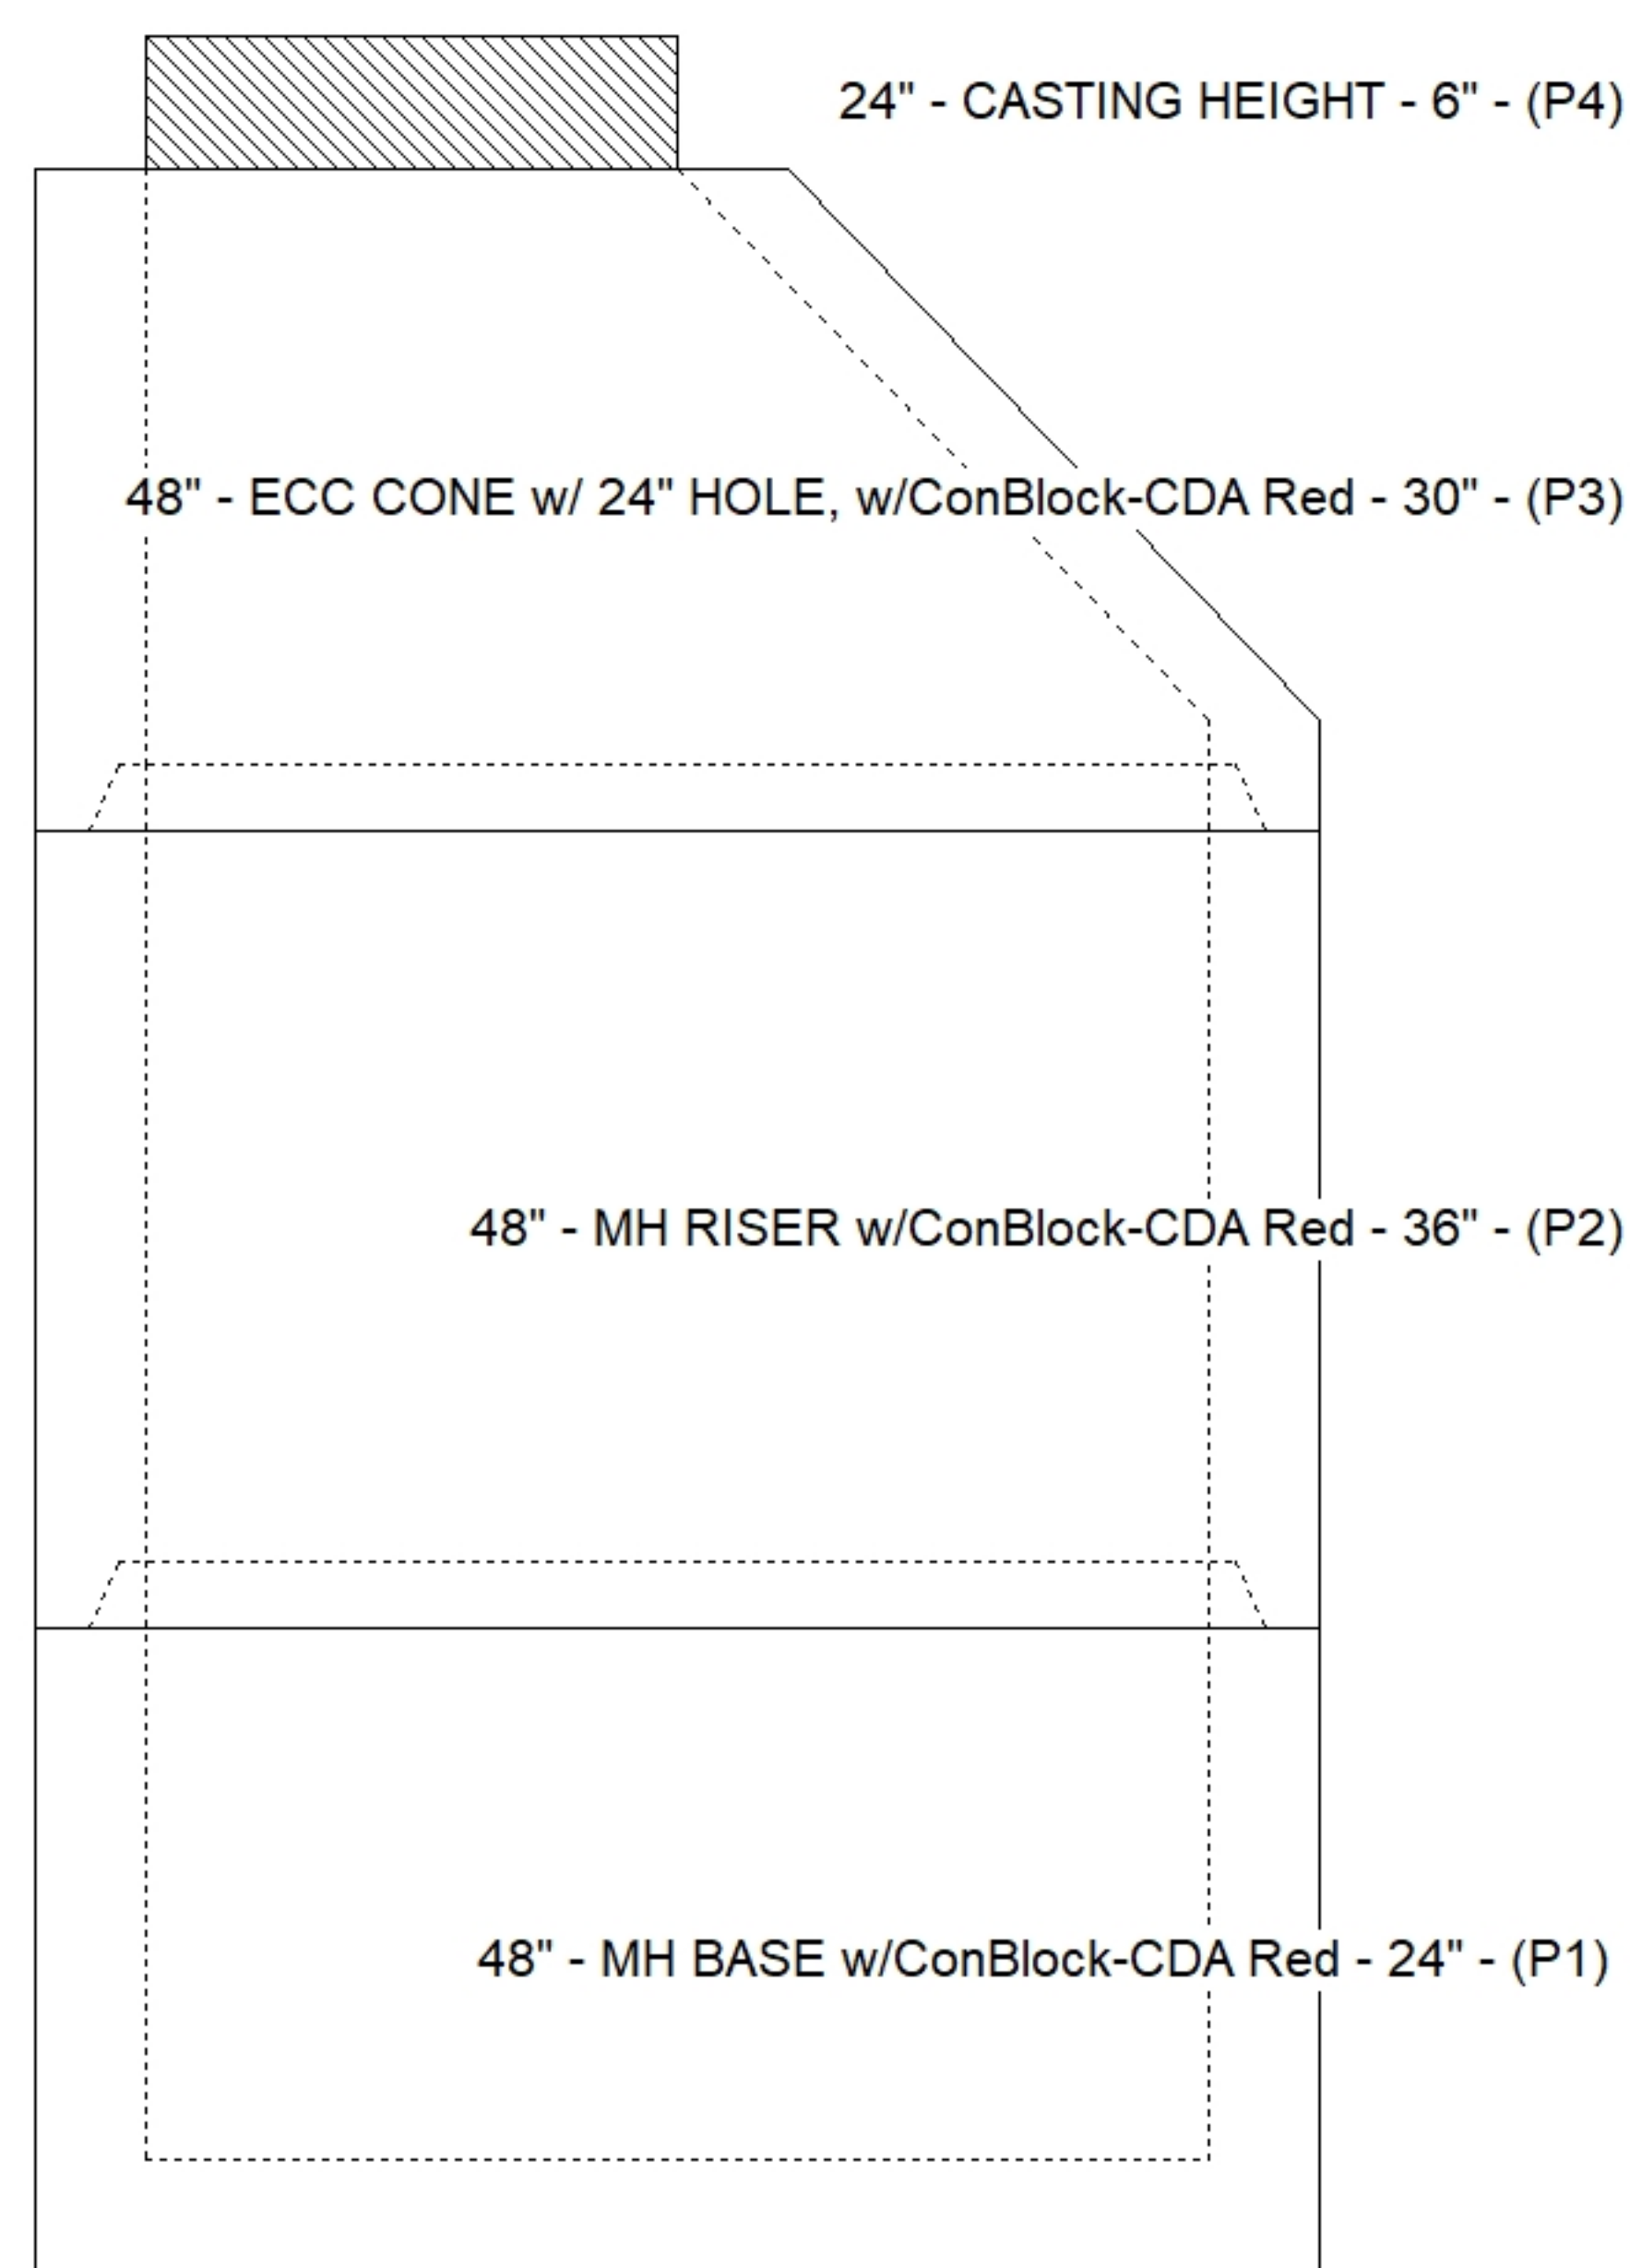

Submittal Drawing
9/24/2026 2:15:47 PM

SUBMITTAL
APPROVED BY:
