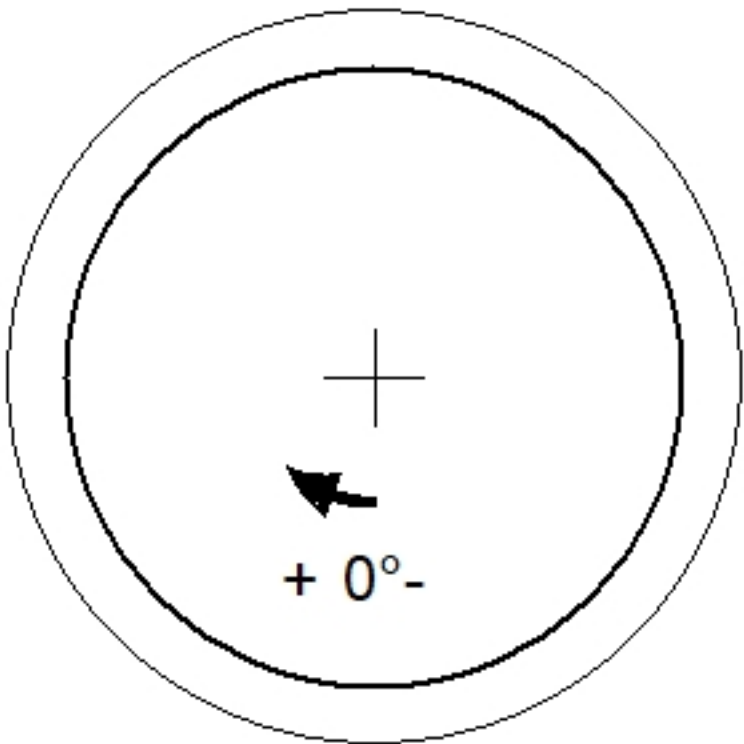
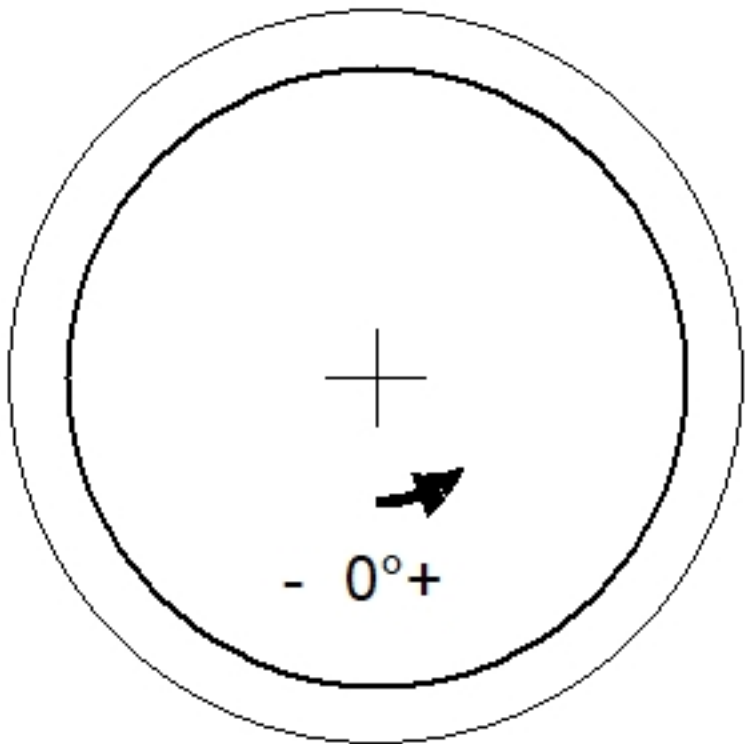
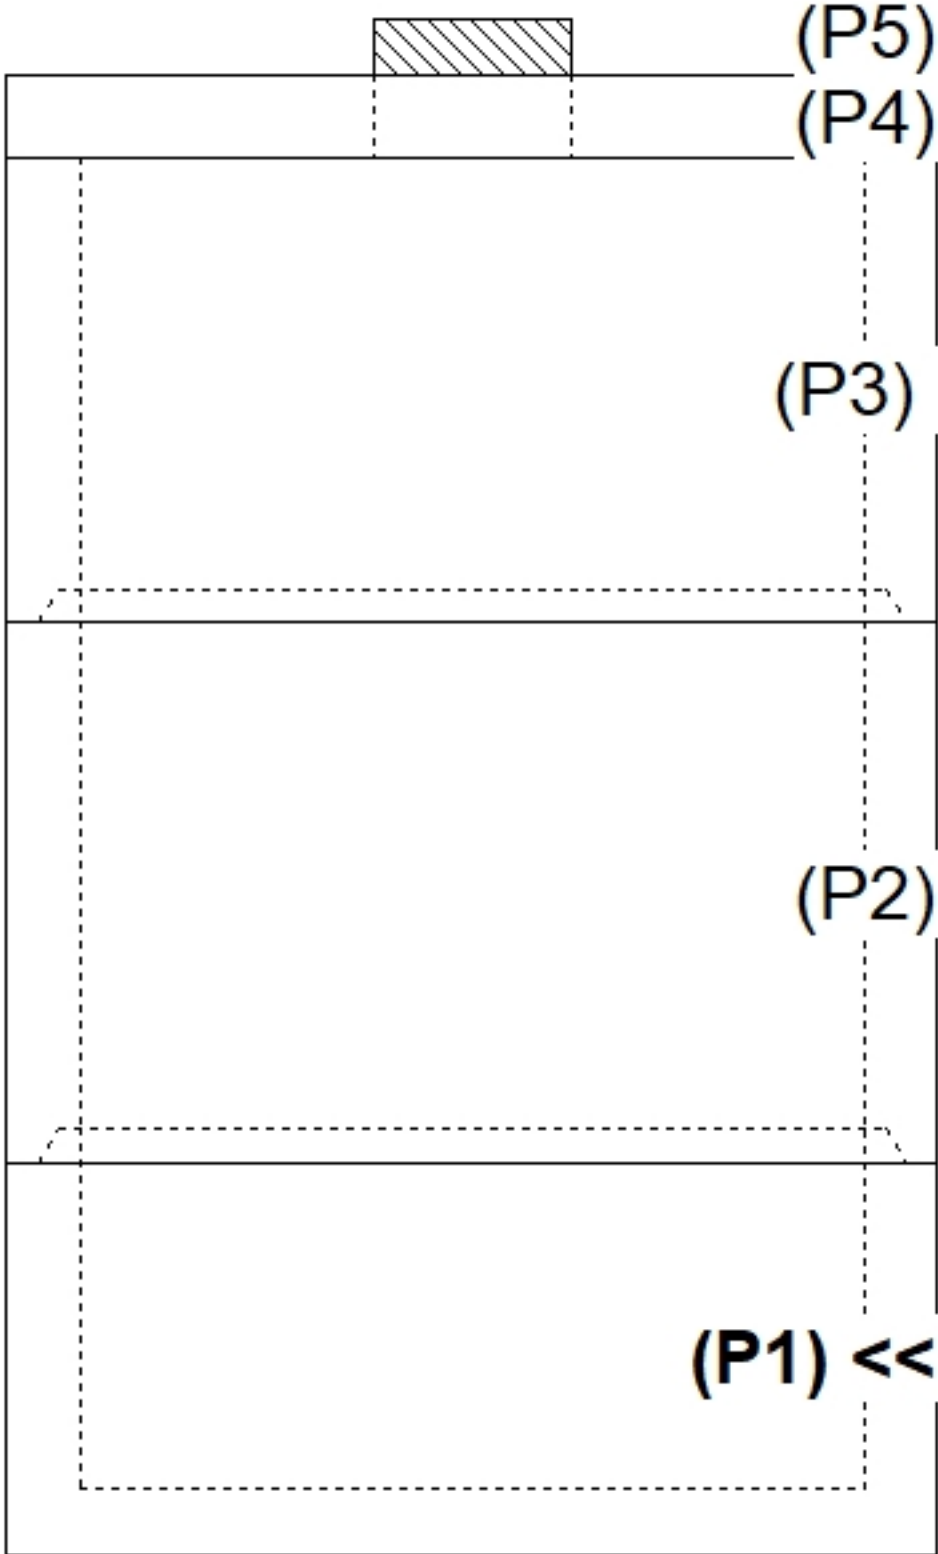
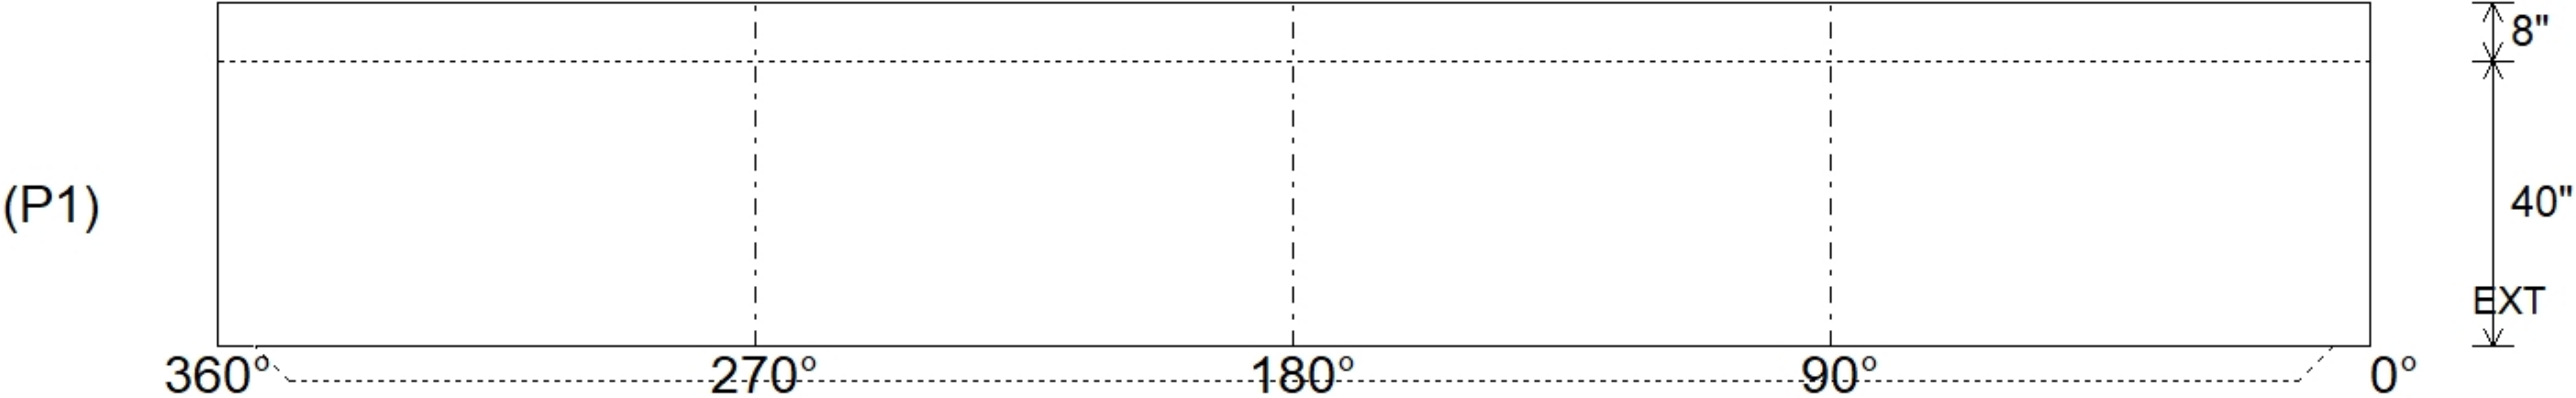


Job Name: 26-3009 ADS FedEx Mt. Juliet Job Location: Mt. Juliet, TN Contractor: ADS Advanced Drainage Systems, Inc.					Plant: Beaver Dam 7/23/2026 8:34:24 AM		Tech: S. Felletter PC: T. Ryan														
Structure ID: S07																					
P1		MH096BAVF										MH BASE Custom Ht T/n									
P5) 24" - CASTING HEIGHT - 7" P4) 96" - MH FLAT TOP w/ 24" Conc. Hole F/F - 10" P3) 96" - MH RISER Custom Ht F/G - 57" P2) 96" - MH RISER T/G - 66" P1) 96" - MH BASE Custom Ht T/n - 40" 1) ASSEMBLY REQUIRED - BRACKETS ONLY 1) CASTING - HOE MC-375 F/C Storm 3) 96" - Conseal CS-102 1.00" 1) 24" - Conseal CS-102 1.00" 2) Hole - 30						0 lb 8185 lb 13117 lb 16442 lb 16817 lb 0 lb 271 lb 0 lb 0 lb 0 lb ----- 54831 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-375 F/C "STORM"). 4. LIFTING ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE. 5. ASSEMBLY REQUIRED - BRACKETS ONLY. 6. P2 & P3 RISERS TO BE MECHANICALLY ATTACHED PRIOR TO INTERNAL INSTALLATION/DELIVERY . REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - RISER/WALLS (As .24) - FLOOR (As .47) #5 BARS AT 8" C.C.E.W.													
Rim: 556'		Rim to Invert: 4'		Slack: 0"		Sump: 132"		Step Position:													
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset											
Invert 1																					
Invert 2																					
Invert 3																					
Invert 4																					
Invert 5																					
Invert 6																					
Invert 7																					
Invert 8																					
RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimenions) 																					
 INSIDE WALL DIMENSIONS 																					
Coating (Int): Coating (Ext):				Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 9" Floor Height: 8"		Height (Int): 40" Height (Ext): 48"		Weight (Net): 16817 lb Volume (Net): 4.3cu.yd											
