

Job Name: 26-3040 Shun Pike Storm
Job Location: Nicholasville, KY
Contractor: PECCO Eng

Plant: Beaver Dam

Tech: S. Felletter

7/20/2026 10:32:31 AM

PC: E. Bradley



Structure ID: 1

P3 GR24x36x6x3

GRADE RING 6"W F/F

P5) 24" x 36" - CASTING HEIGHT - 4"
P4) 24" x 36" - GRADE RING 6"W F/F - 3"
P3) 24" x 36" - GRADE RING 6"W F/F - 3"
P2) 24" x 36" - GRADE RING 6"W F/F - 3"
P1) 24" x 36" - KNOCKOUT BASE 6"W/F - STOCK F/n - 42"
1) CASTING - HOE 518 F/G
4) 24" x 36" - Con Seal CS-102 1.00"

Structure Total:


0 lb
218 lb
218 lb
218 lb
2466 lb
354 lb
0 lb

3473 lb

Structure Notes: 1. PER ASTM C913 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO INVERT CHANNEL.
4. REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
- WALLS (As .12) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .12) #5 BARS AT 12" C.C.E.W.

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE = 4,000 PSI @ 28 DAYS.
3. REINFORCING: #4 BAR AS SHOWN (GRADE 60 KSI).
4. LIFTS: 2 EA. CONAC .8 TON WIRE ROPE ANCHORS REQUIRED.

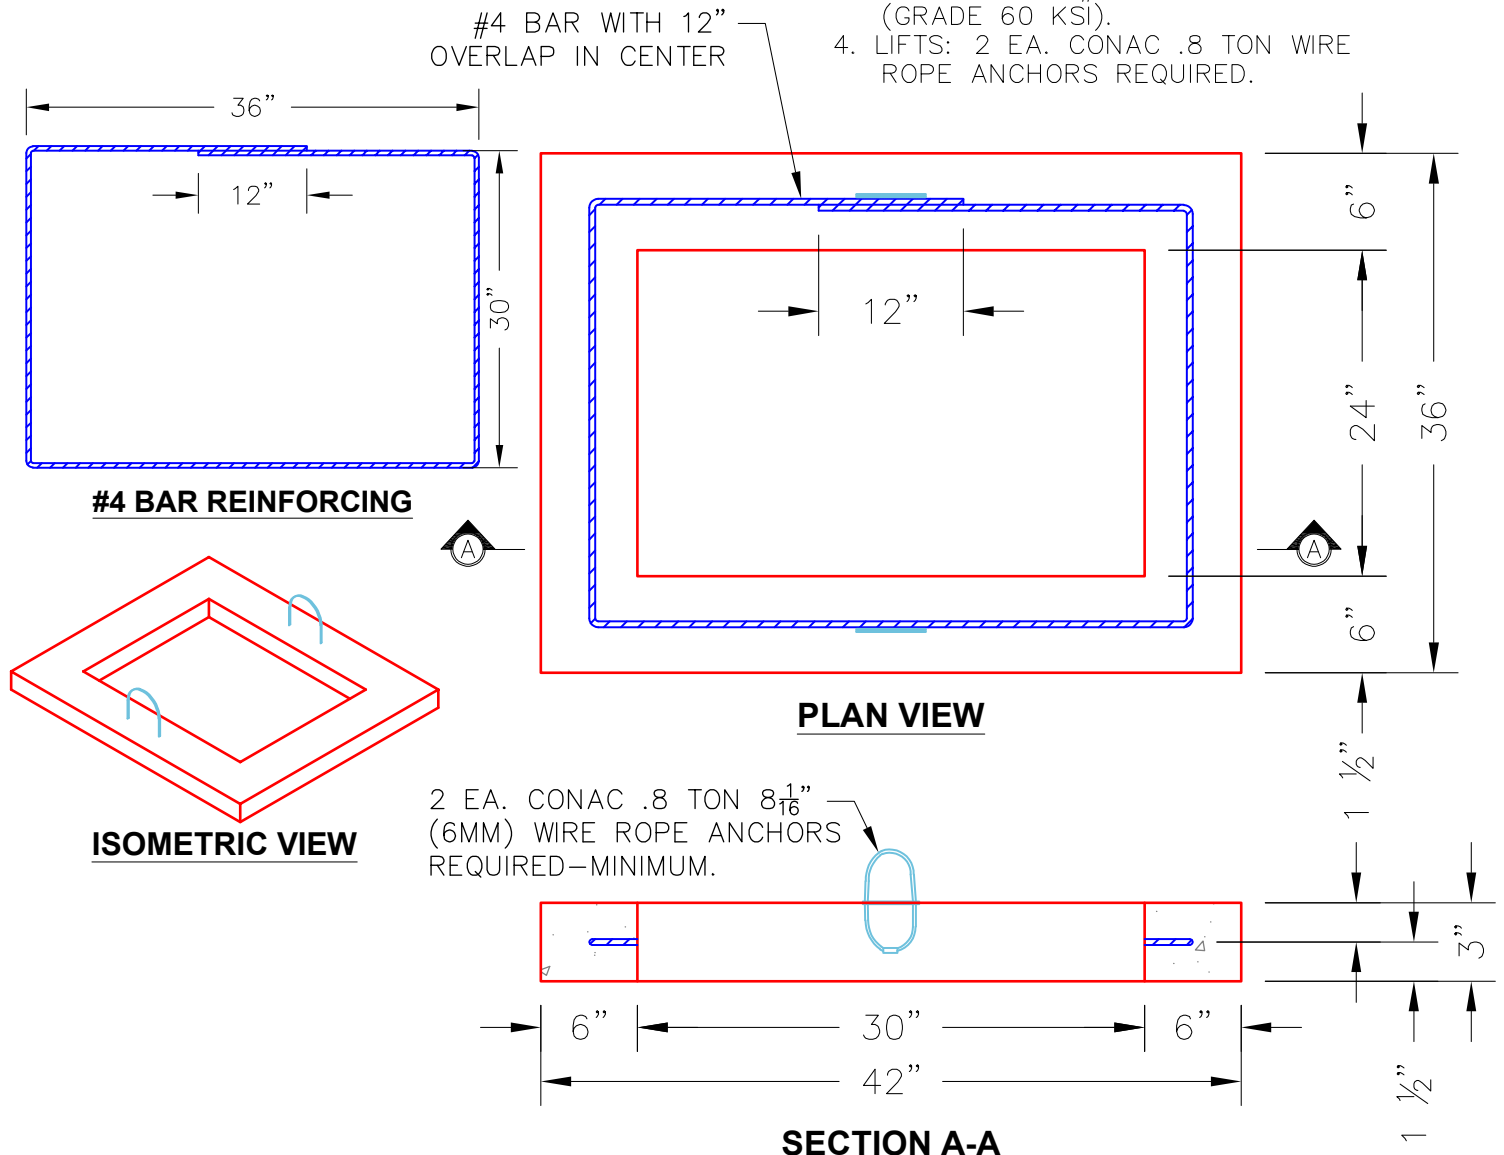

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 6"

Height (Ext): 3"

Weight (Net): 217 lb
Volume (Net): 0.06cu.yd
