

Contractor: Cleary Construction, Inc.

Plant: 100





Slack: 0"

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

2) Hole - 4


0 lb

Structure Total: 6146 lb

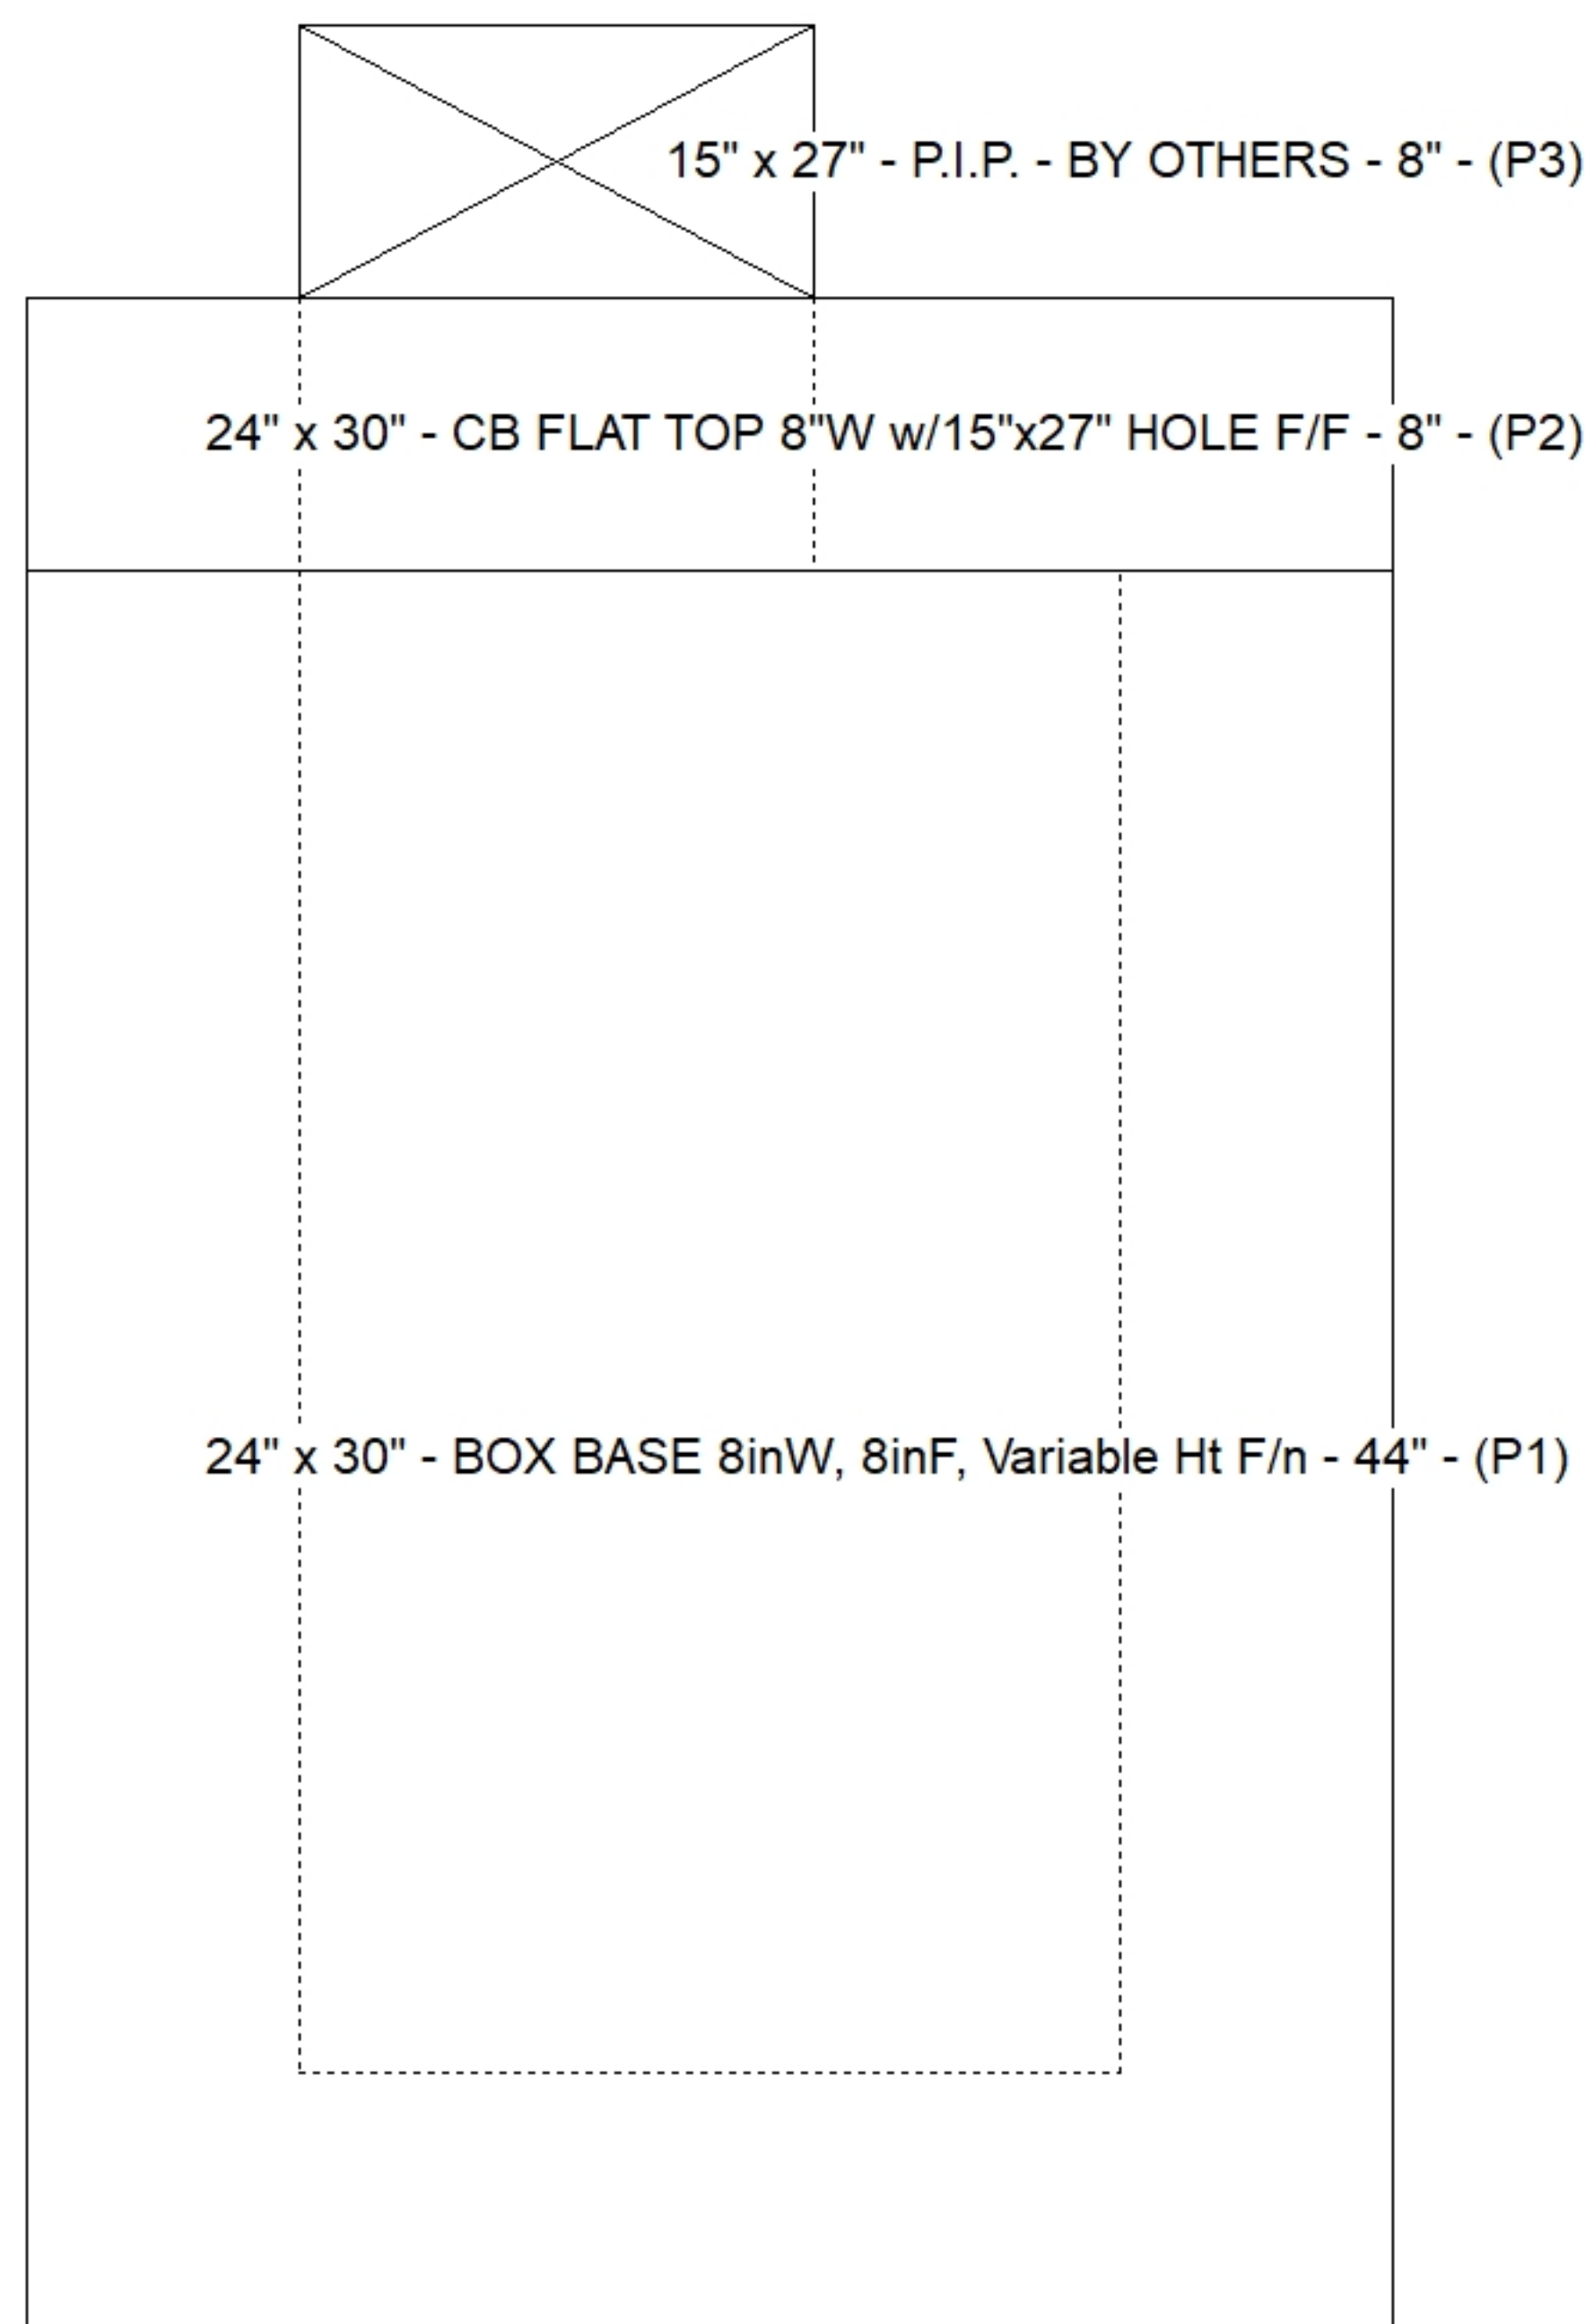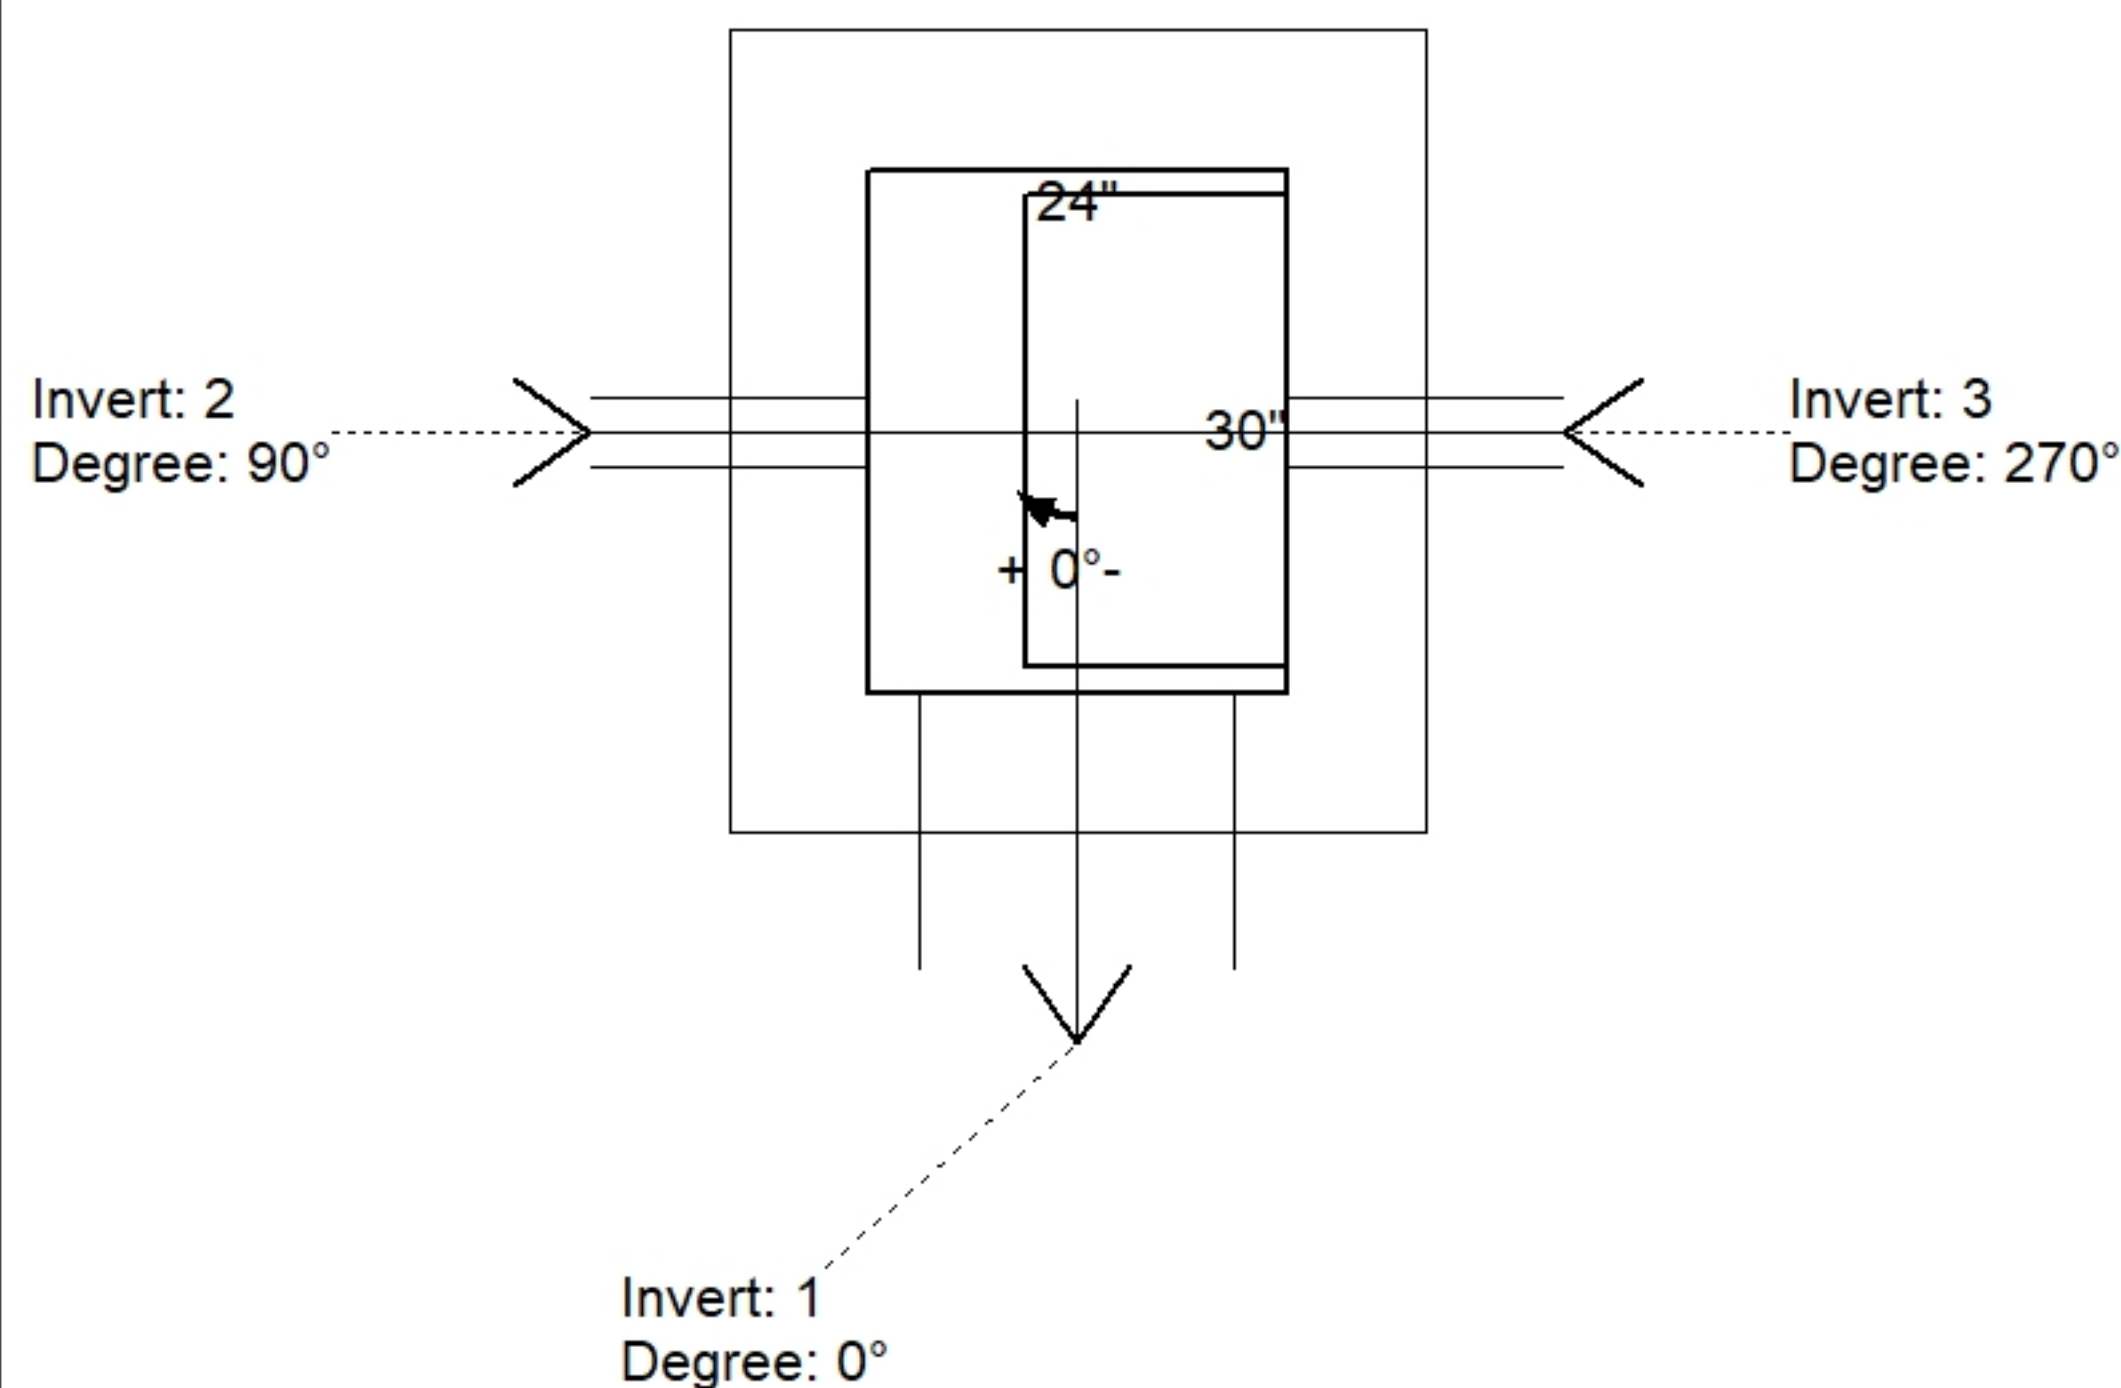

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	709.79'							
Reducer								
Invert 1	704.79'	0°	15" CMP	16"	18"	Hole 18	-1.5"	P1
Invert 2	707.79'	90°	4" WEEP HOLE	4"	4"	Hole 4	36"	P1
Invert 3	707.79'	270°	4" WEEP HOLE	4"	4"	Hole 4	36"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Cast (Int. Dim.) - Interior Dimensions

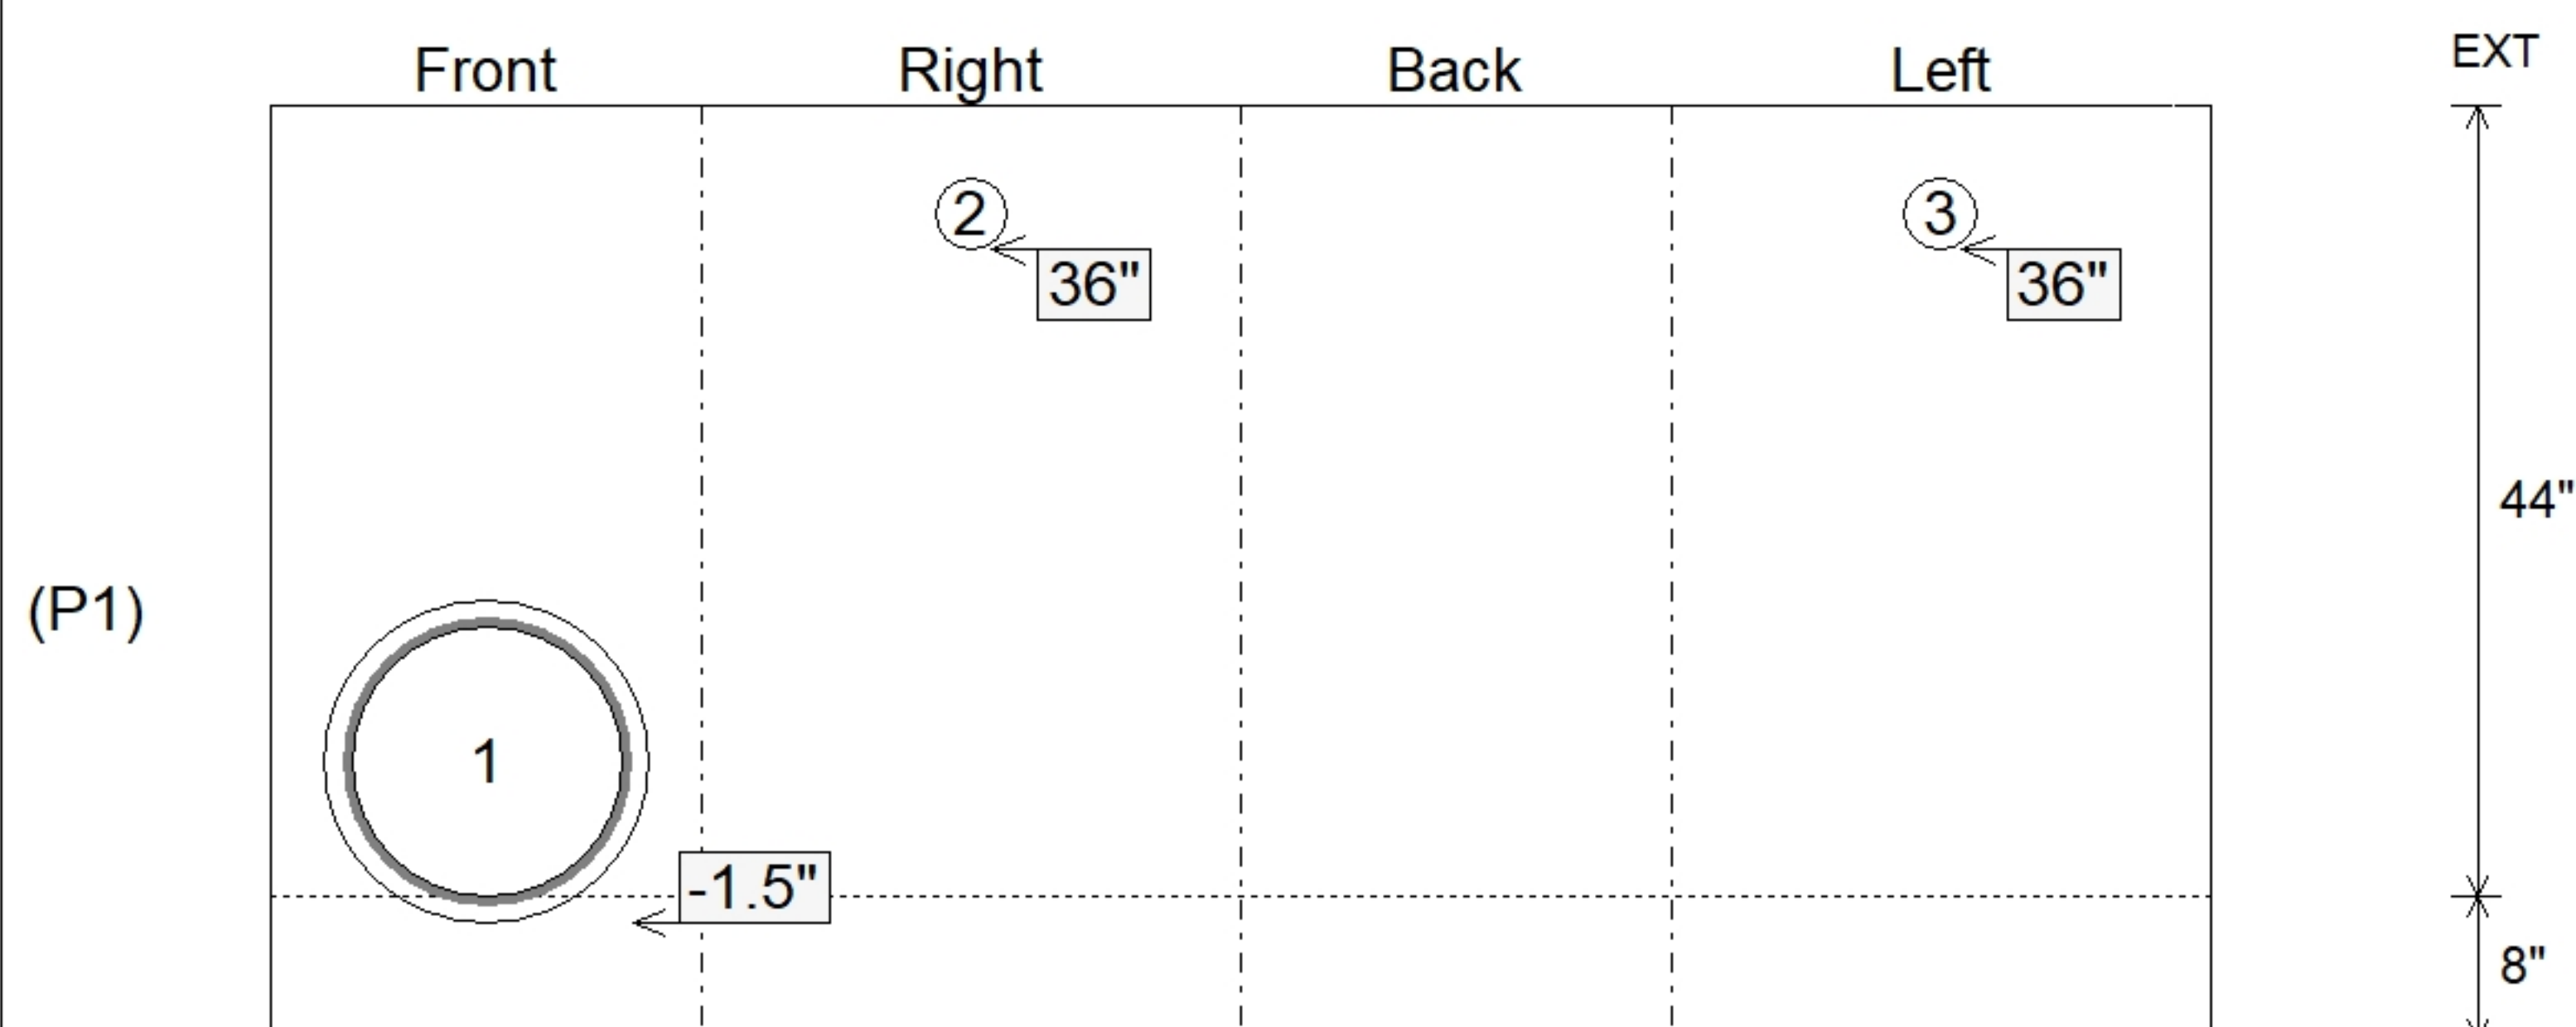

SUBMITTAL
APPROVED BY:
