
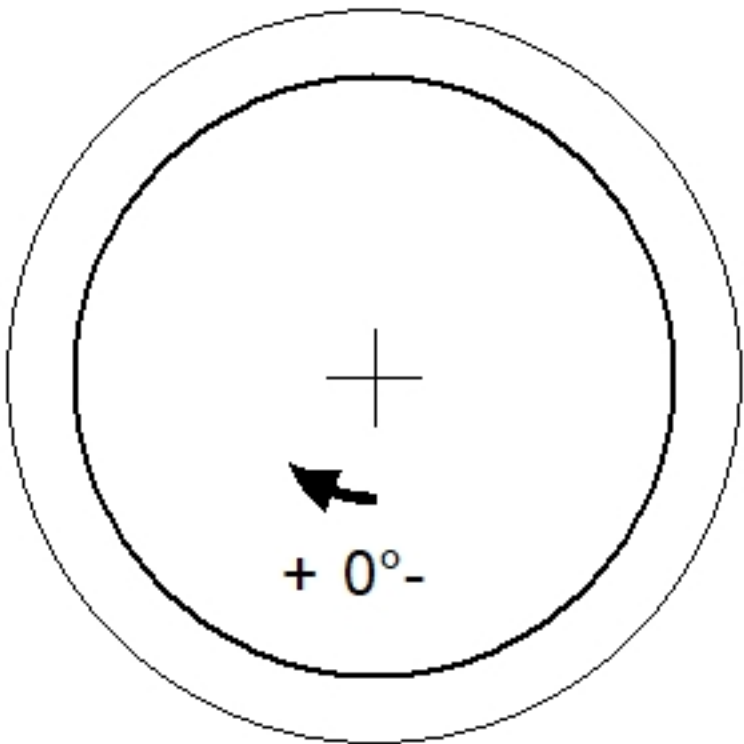


Job Name: 26-3091 907597 Ives Field Rec Enhance Job Location: Shelby Twp, MI Contractor: Contech Engineering Solutions					Plant: Beaver Dam 7/20/2026 9:17:25 AM		Tech: S. Felletter PC: C. Goff				
Structure ID: 10-CS-3											
P1		MH036BA12		MH BASE T/n							
P4) 30" - CASTING HEIGHT - 4" P3) 36" - MH FLAT LID w/30in ECC Hole F/G - 10" P2) 36" - MH RISER T/G - 72" P1) 36" - MH BASE T/n - 12" 1) ASSEMBLY REQUIRED 1) CVSTENCILING 2) 36" - Conseal CS-102 1.00" 2) Hole - 16						0 lb 683 lb 2898 lb 1272 lb 0 lb 0 lb 0 lb 0 lb ----- 4852 lb Structure Total:		Structure Notes: 4" CASTING BY OTHERS LIFTING ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE ICAST TO INSTALL THE INTERNALS CONTECH'S LOGO AS WELL AS THE INLET AND OUTLET MUST BE STENCILED ONTO THE STRUCTURE			
Rim: 639.8'		Rim to Invert: 5.98'		Slack: 11.8"		Sump: 38.04"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (┘)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
(P4) (P3) (P2) (P1) << RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimenions) 											

INSIDE WALL DIMENSIONS

(P1)

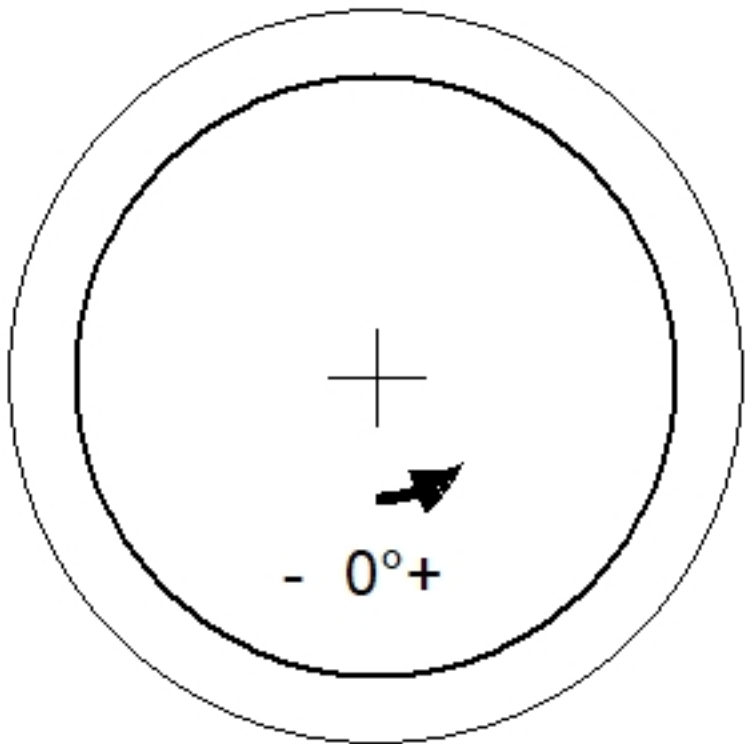
