

Job Name: 26-3112 Gunn Hill Subdivision
Job Location: CPU
Contractor: Greg Gunn

Plant: Beaver Dam

7/27/2026 10:24:29 AM

Tech: S. Felletter

PC: E. Bradley



Structure ID: MH-A1 SS-MH

P2 MH048LD12XS

MH FLAT TOP w/27" Hole ECC F/G


- P3) 27" - CASTING HEIGHT - 7"
P2) 48" - MH FLAT TOP w/27" Hole ECC F/G - 12"
P1) 48" - MH BASE w/XYPEX T/n - 36"
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) 48" - MH INVERT CHANNEL w/XYPEX - FULL HEIGHT
1) 48" - Conseal CS-102 1.00" (Double)
2) PSX - 12-08 NYLO
3) MH Step ML-10-TDS-NCR - 10"

Structure Total:

0 lb
1499 lb
3749 lb
0 lb
0 lb
1440 lb
0 lb
16 lb
0 lb


6705 lb

Structure Notes:
1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING BY OTHERS.
REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
- RISER (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

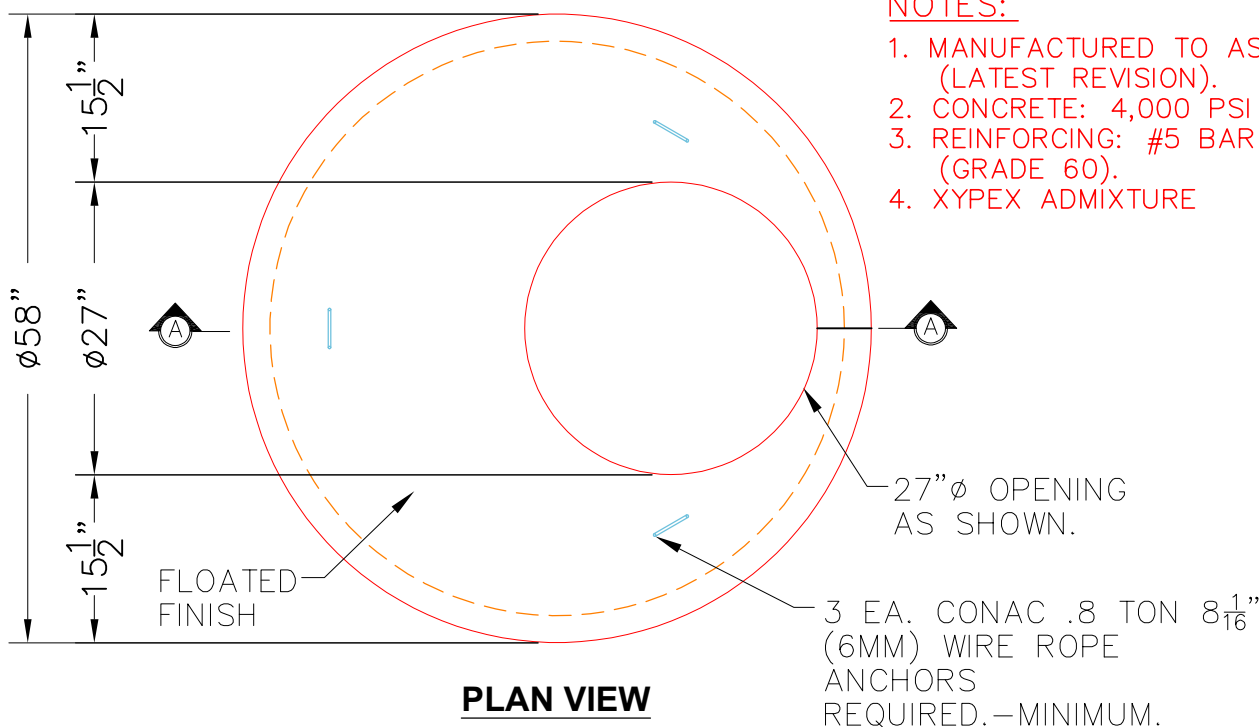

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" C.C. E.W. (GRADE 60).
4. XYPEX ADMIXTURE

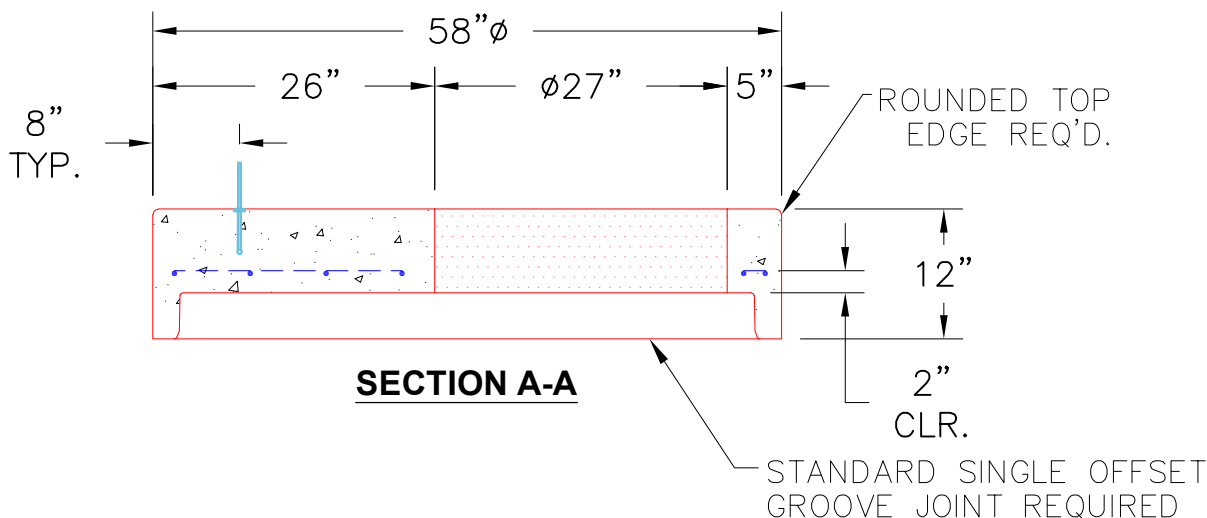

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 12"

Weight (Net): 1499 lb
Volume (Net): 0.38cu.yd
