

Contractor: Walker Building Group

Plant: Beaver Dam



Size: 36" x 48"

Rim to Invert: 4.44'



Floor Height: 8"

Slack: 0.78"

- FLOOR (As .47) #5 BARS AT 8" C.C.E.W.


0.412 H-

Structure Total: 8413 lb

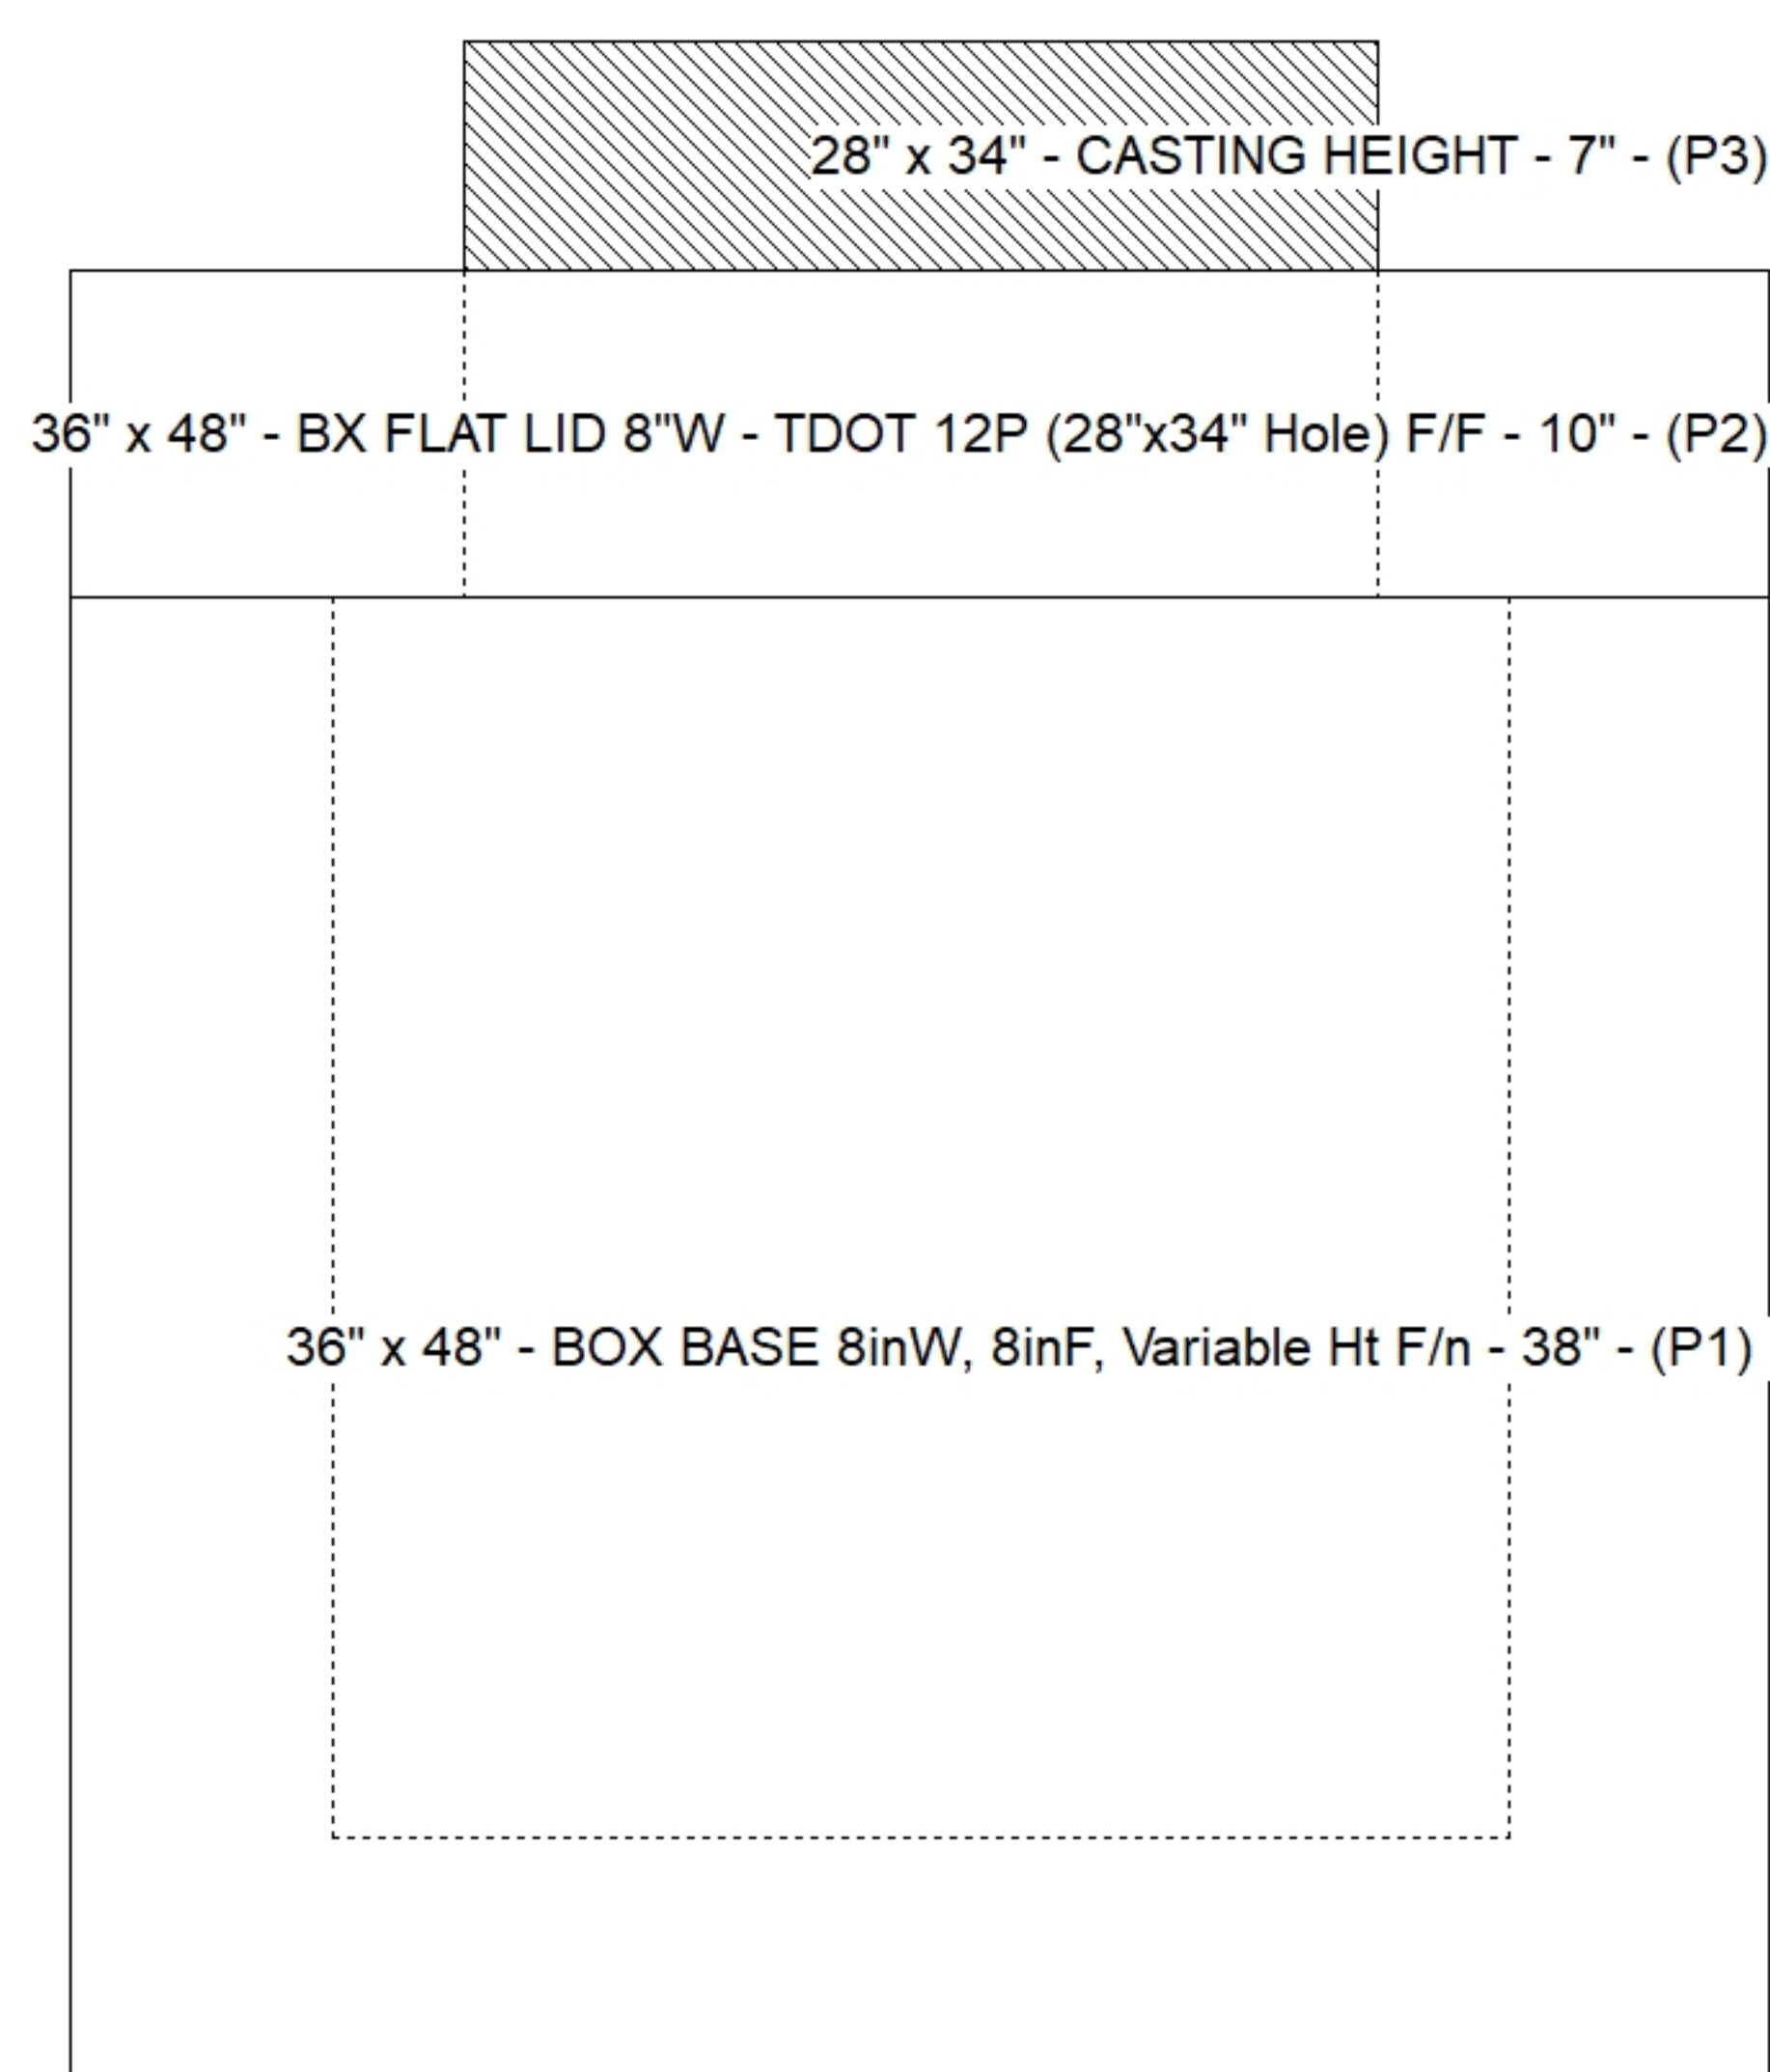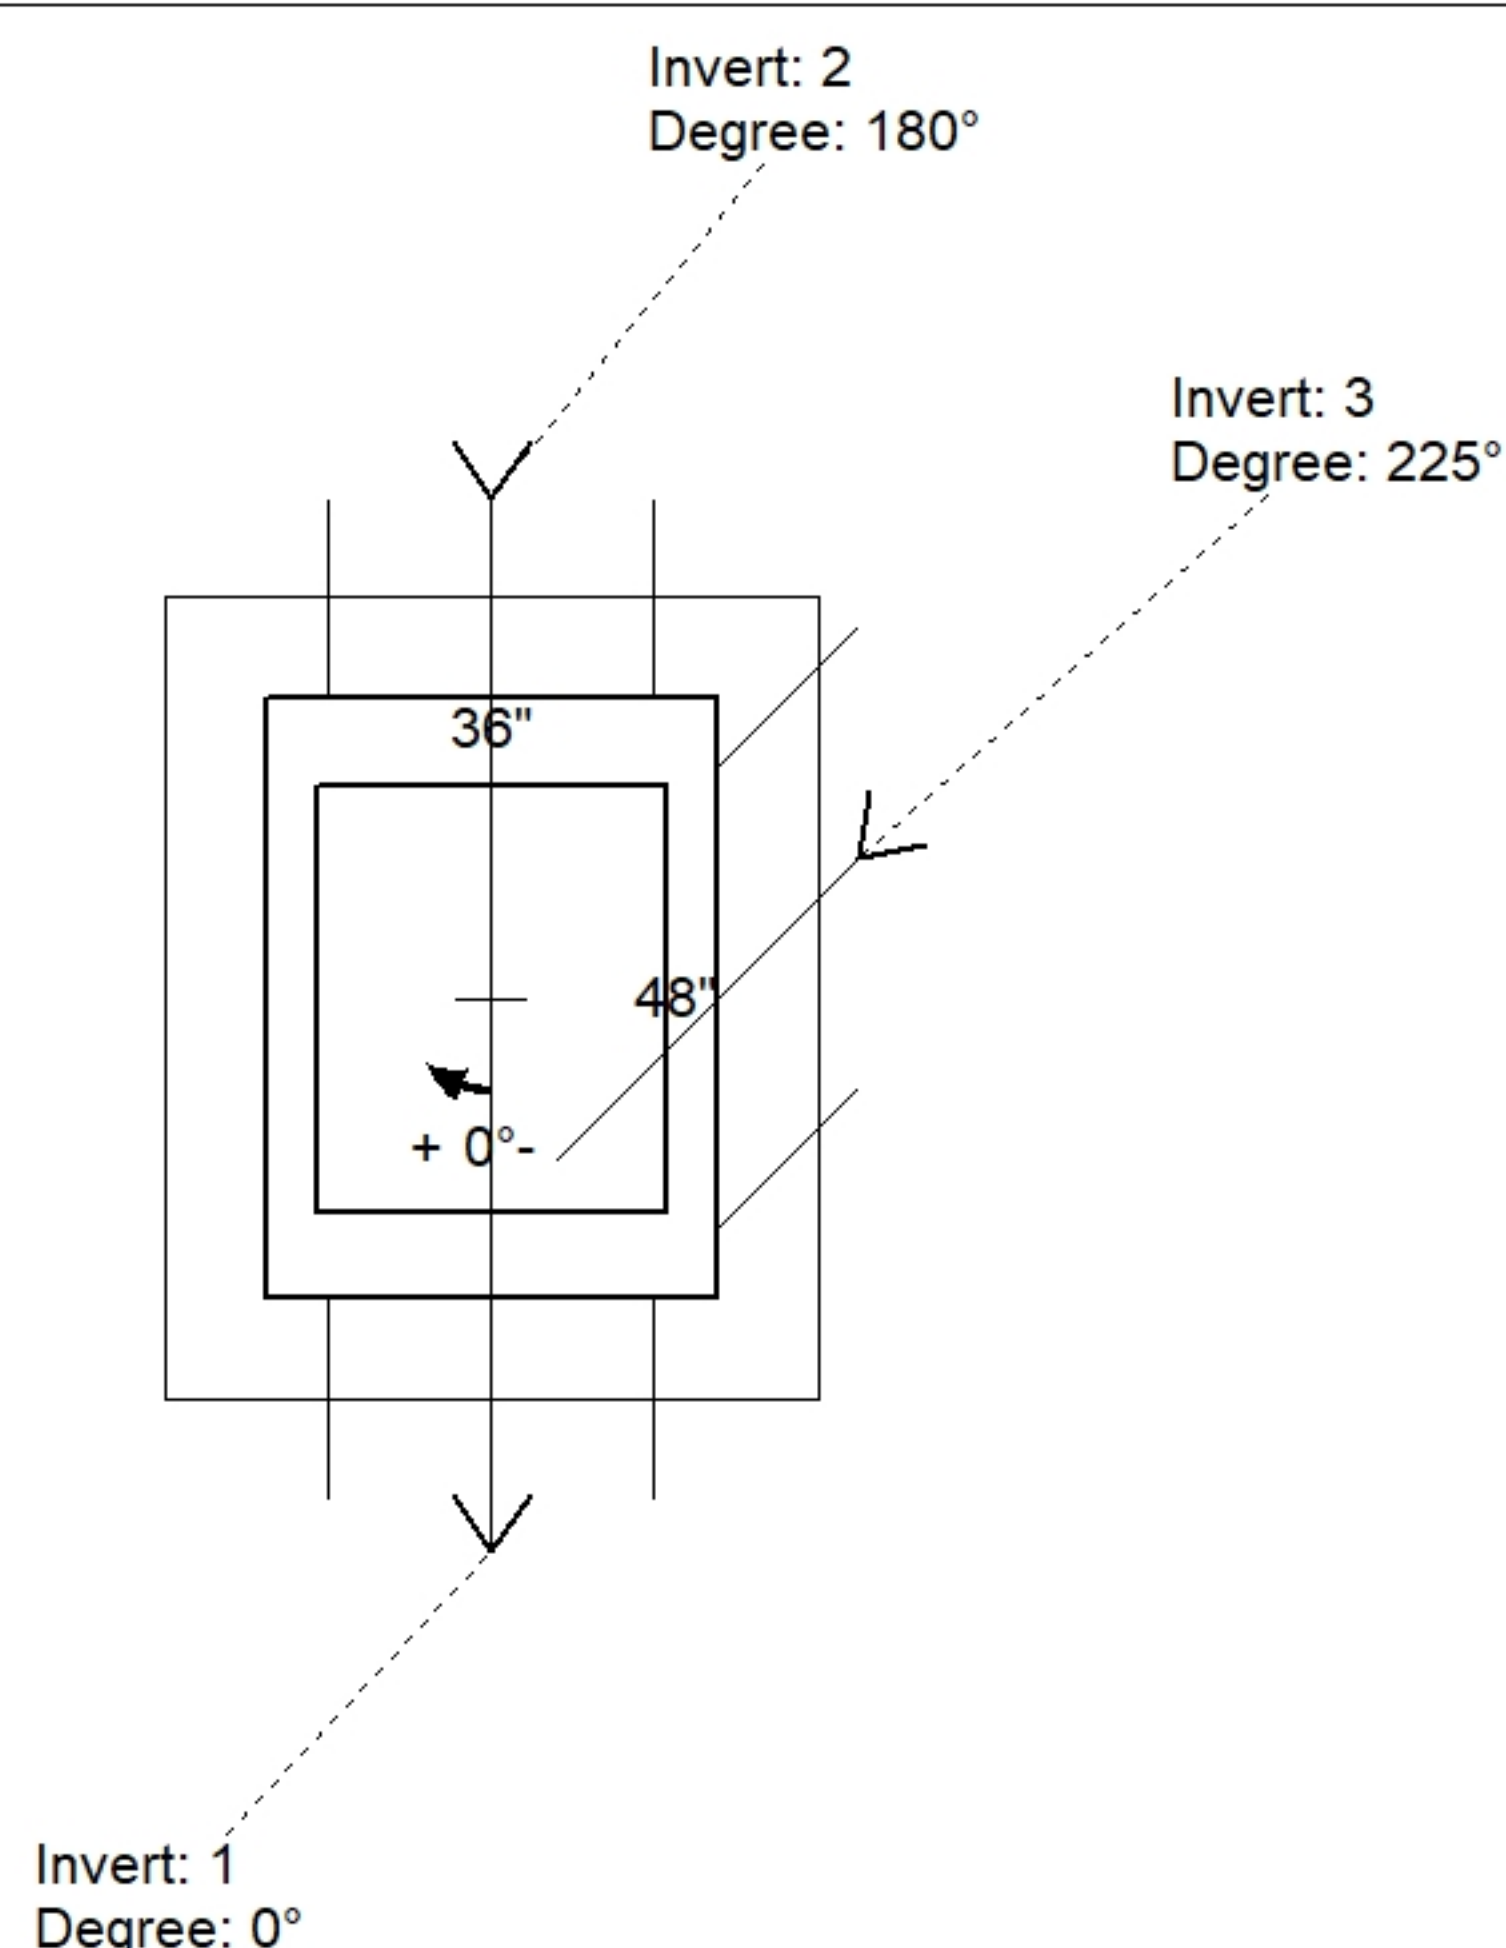

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	565.24'							
Reducer								
Invert 1	560.8'	0°	18" RCP B WALL	23"	26"	Hole 26	0"	P1
Invert 2	561'	180°	18" RCP B WALL	23"	26"	Hole 26	2.4"	P1
Invert 3	561'	225°	18" RCP B WALL	23"	26"	Hole 26	2.4"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

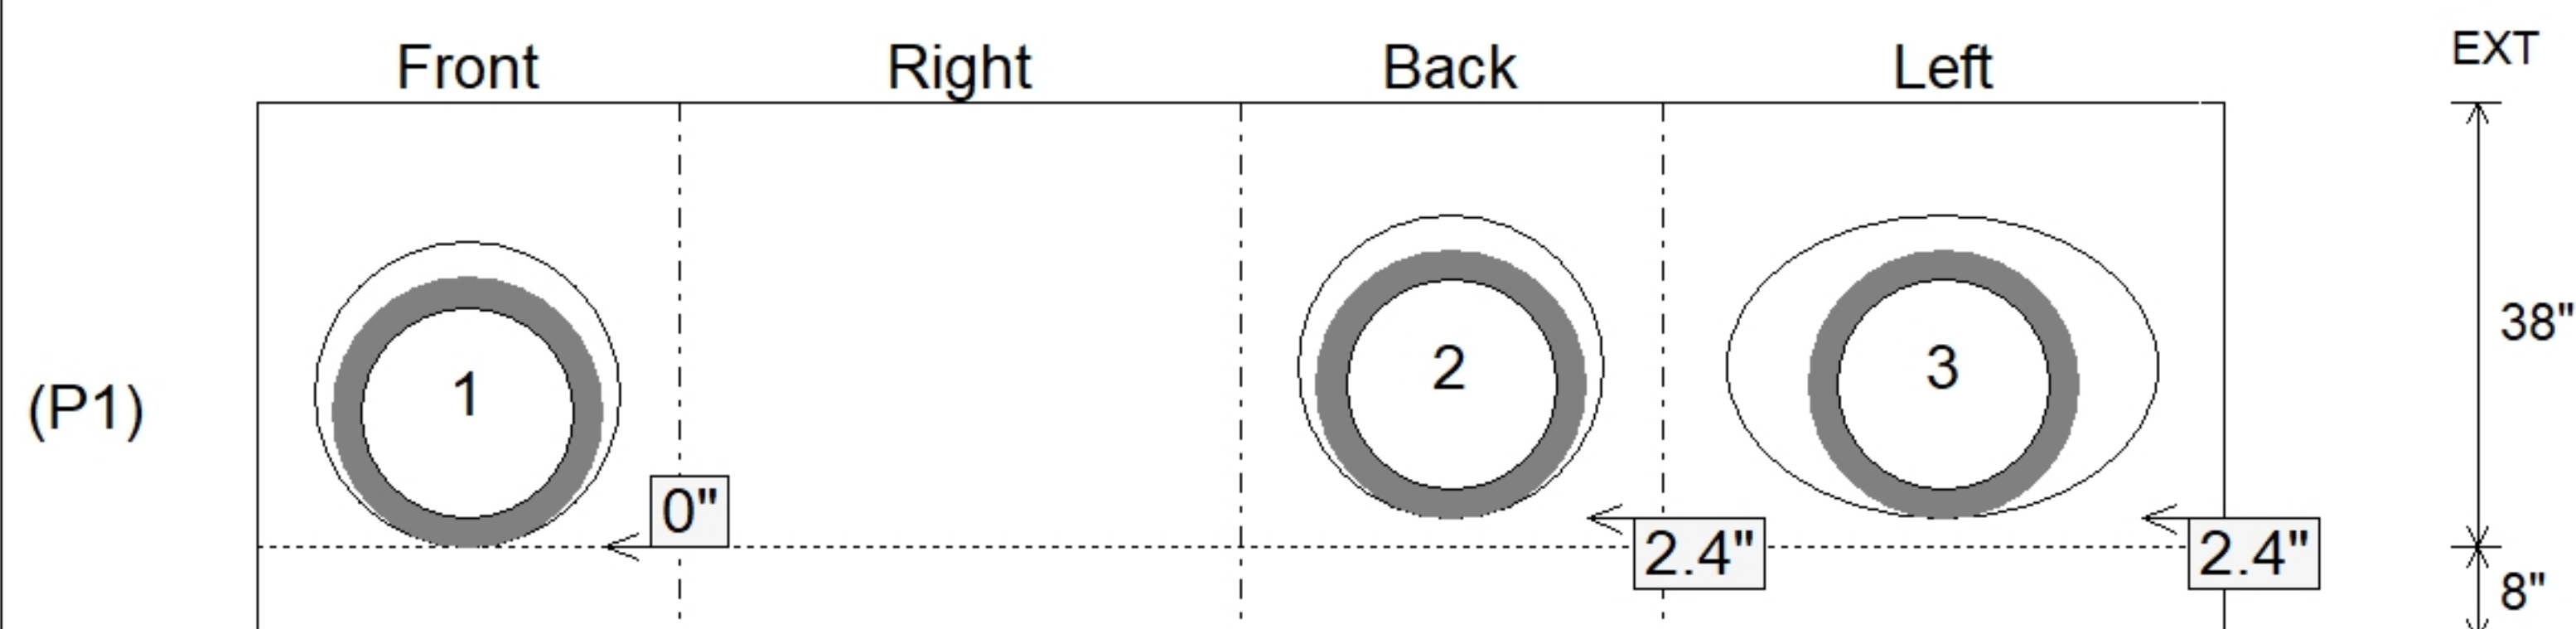

SUBMITTAL
APPROVED BY:
