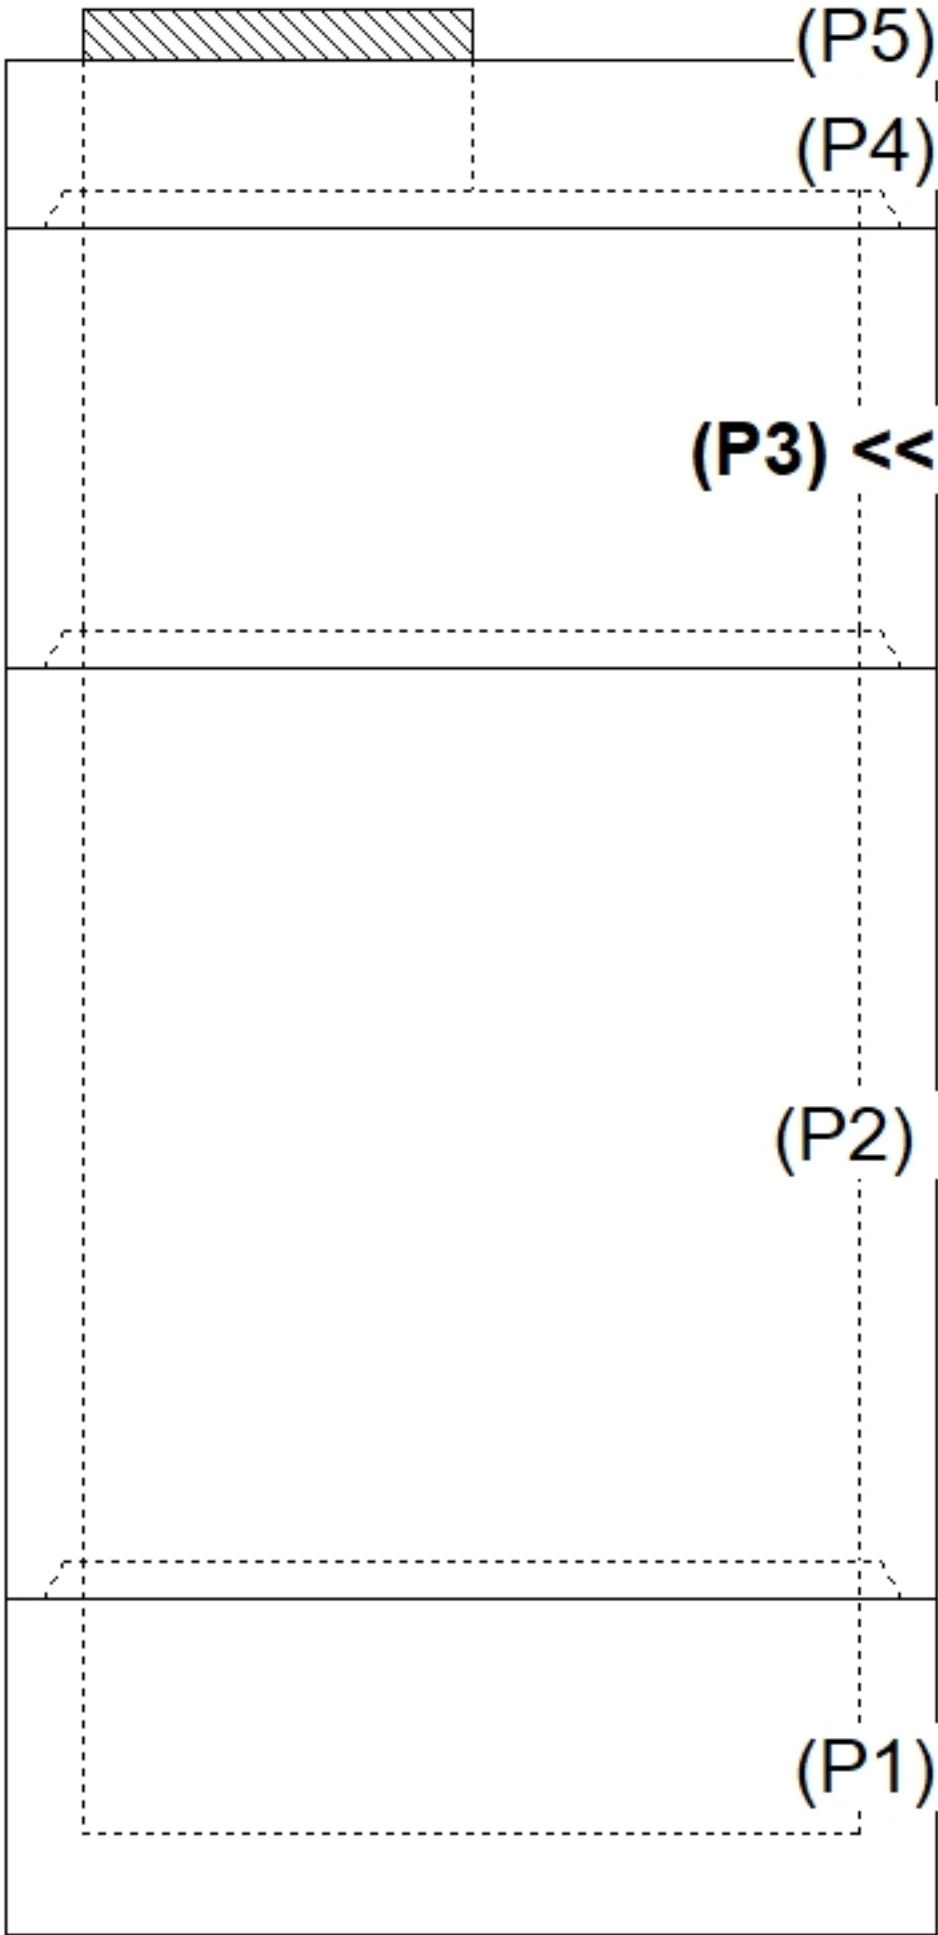
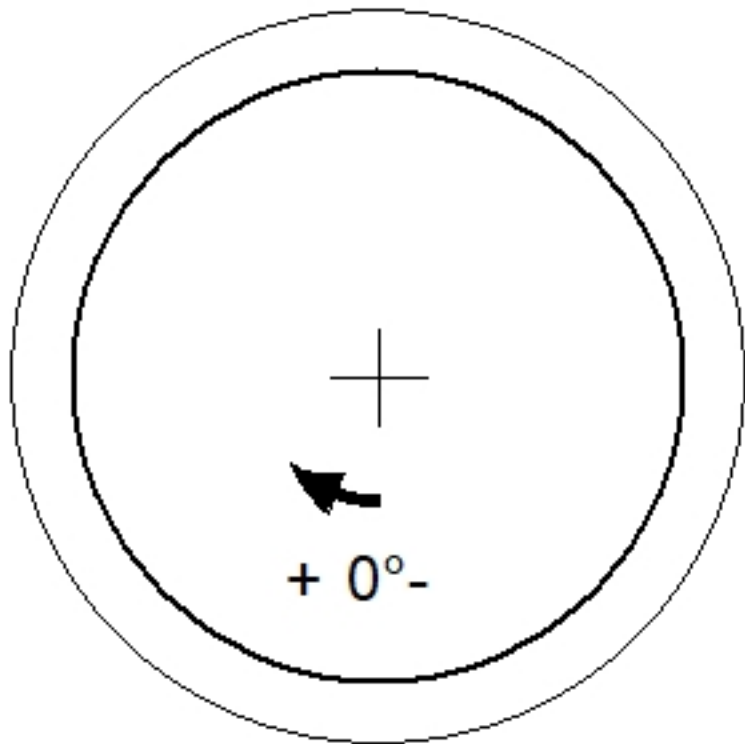
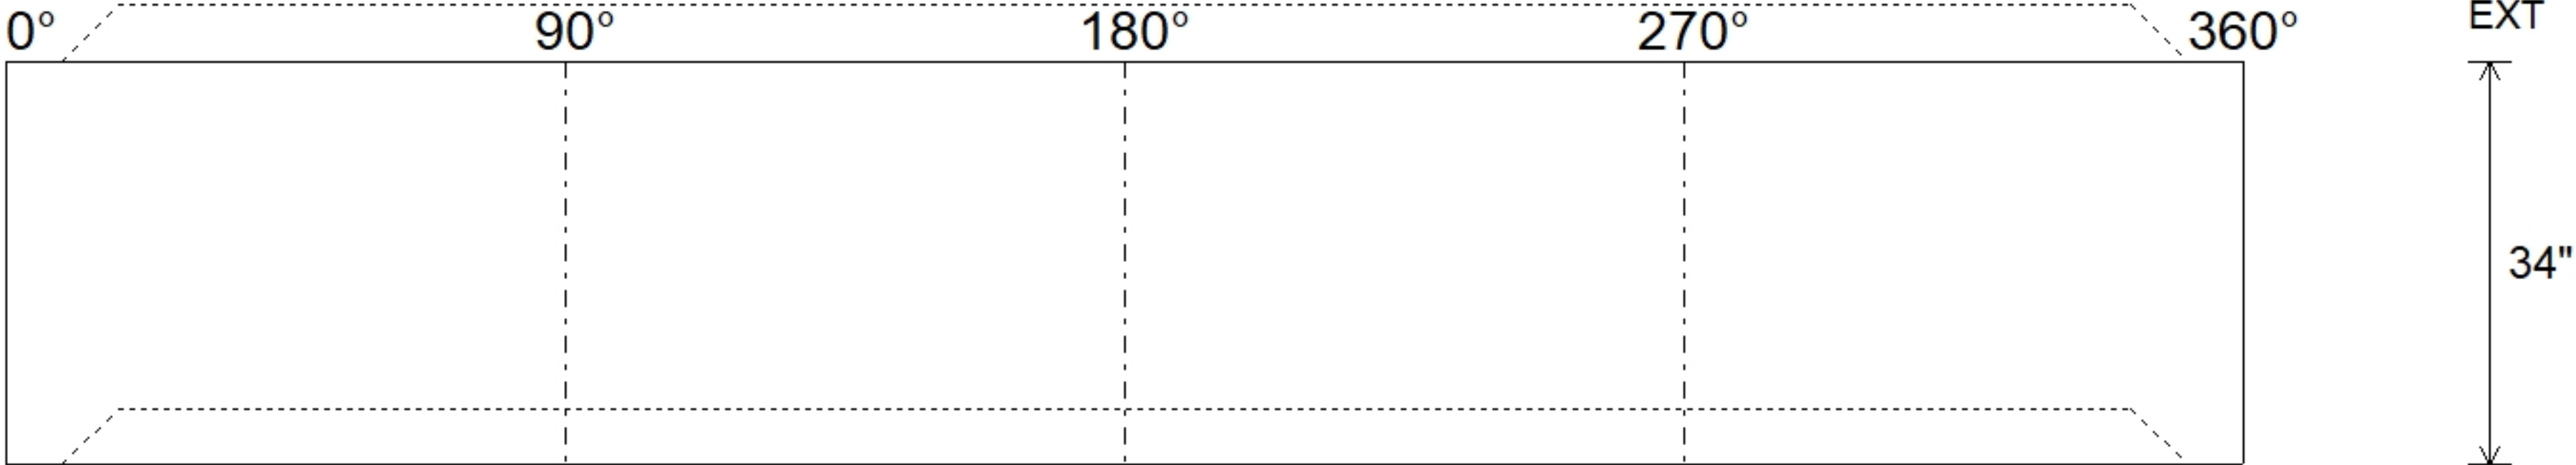


Job Name: 26-3200 906957 Austin Tri-Hawk Auto Job Location: Austin, IN Contractor: Contech Engineering Solutions				Plant: Beaver Dam 8/7/2026 1:03:44 PM		Tech: S. Felletter PC: C. Goff				
Structure ID: 10-CS-5										
P3		MH060RSVF		MH RISER Custom Ht T/G						
P5) 30" - CASTING HEIGHT - 4" P4) 60" - MH FLAT TOP SPEC. (30" ECC HOLE) F/G - 13" P3) 60" - MH RISER Custom Ht T/G - 34" P2) 60" - MH RISER SPECIAL T/G - 72" P1) 60" - MH BASE T/n - 18" 1) ASSEMBLY REQUIRED 1) CVSTENCILING 3) 60" - Conseal CS-102 1.00" 2) Hole - 20						0 lb 2589 lb 3549 lb 7195 lb 4612 lb 0 lb 0 lb 0 lb 0 lb ----- 17945 lb		Structure Notes: 4" CASTING BY OTHERS LIFTING ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE ICATS TO INSTALL THE INTERNALS CONTECH'S LOGO AS WELL AS THE INLET AND OUTLET MUST BE STENCILED ONTO THE STRUCTURE		
Rim: 560.1' Rim to Invert: 7.43' Slack: 6.276" Sump: 58.116" Step Position: 90										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (┘)	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										
RIGHT-SIDE UP VIEW (int. dimensions)										
										
INSIDE WALL DIMENSIONS										
										
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 6" Floor Height: 0"		Height (Int): 34" Height (Ext): 34"		Weight (Net): 3549 lb Volume (Net): 0.91cu.yd	
