

Job Name: 26-3200 906957 Austin Tri-Hawk Auto
Job Location: Austin, IN
Contractor: Contech Engineering Solutions

Plant: Beaver Dam
8/7/2026 1:03:34 PM

Tech: S. Felletter
PC: C. Goff



Structure ID: 10-CS-5

P4 MH060LD13-30ECC

MH FLAT TOP SPEC. (30" ECC HOLE) F/G



P5) 30" - CASTING HEIGHT - 4"
P4) 60" - MH FLAT TOP SPEC. (30" ECC HOLE) F/G - 13"
P3) 60" - MH RISER Custom Ht T/G - 34"
P2) 60" - MH RISER SPECIAL T/G - 72"
P1) 60" - MH BASE T/n - 18"
1) ASSEMBLY REQUIRED
1) CVSTENCILING
3) 60" - Conseal CS-102 1.00"
2) Hole - 20

Structure Total:

0 lb
2589 lb
3549 lb
7195 lb
4612 lb
0 lb
0 lb
0 lb
0 lb
17945 lb
Structure Notes:
4" CASTING BY OTHERS
LIFTING ANCHORS TO BE INSTALLED
ON THE OUTSIDE OF THE STRUCTURE
ICATS TO INSTALL THE INTERNALS
CONTECH'S LOGO AS WELL AS THE
INLET AND OUTLET MUST BE
STENCILED ONTO THE STRUCTURE

GENERAL NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE 5,000 PSI AT 28 DAYS.
3. REINFORCING: #4 @ 9" O.C. E.W. PER ASTM A615 (GRADE 60)

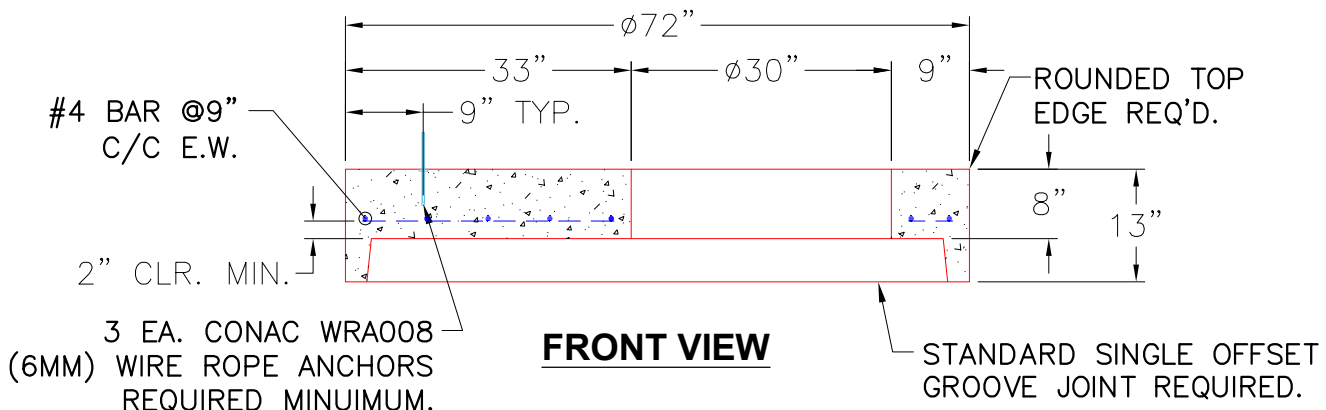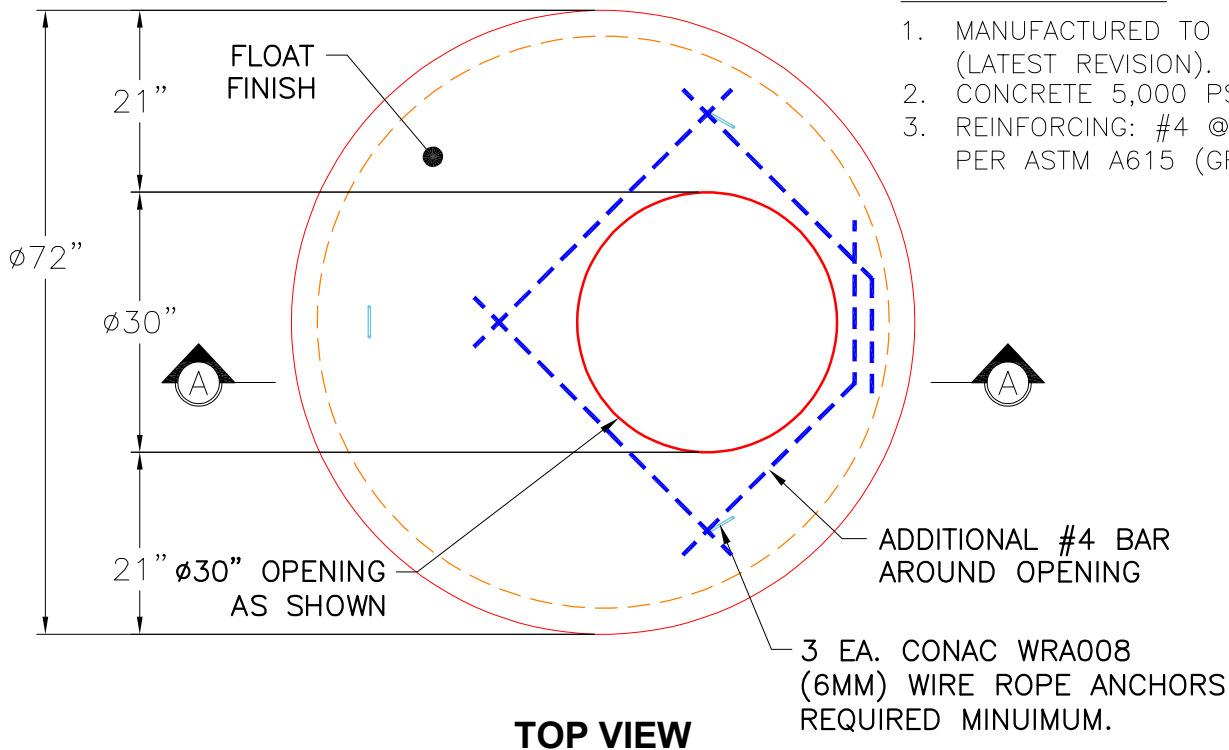

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 6"

Height (Ext): 13"

Weight (Net): 2589 lb
Volume (Net): 0.66cu.yd
