

Job Name: 26-3232 - 2-10 Hoop Drive
Job Location: Walton, KY
Contractor: Kemper Construction

Plant: 100
9/4/2026 1:15:31 PM

Tech: Jared - F
PC: E. Bradley



Structure ID: 3 CB2-2

P1 BX2424-08BA48

BOX BASE 8inW, 8inF

- P3) 24" x 24" - CASTING HEIGHT - 4"
P2) 24" x 24" - BOX RISER 8inW, Variable Ht - 22"
P1) 24" x 24" - BOX BASE 8inW, 8inF - 48"
1) CASTING - HOE 280T F/G
2) 24" x 24" - Conseal CS-102 1.00"
2) Hole - 18

0 lb
1890 lb
4857 lb
182 lb
0 lb
0 lb

Structure Total: 6929 lb




- Structure Notes:**
1. PER ASTM C913 SPECIFICATIONS.
 2. CONCRETE = 4,000 PSI AT 28 DAYS.
 3. NO STEPS AND NO INVERT CHANNEL.
 4. CASTING BY ICAST (HOE 280T F/G).
- REINFORCING PER ASTM A615 (GRADE 60).
- WALLS (As .12) #5 BARS AT 12" C.C.E.W.
 - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.

Rim: 944.41' Rim to Invert: 6.09' Slack: 1.08' Sump: 2' Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	938.32'	0°	20"	12" RCP B WALL	16"	Hole 18	18"	18"	0"	0"
Invert 2	939.8'	180°	20"	12" RCP B WALL	16"	Hole 18	18"	18"	17.76"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

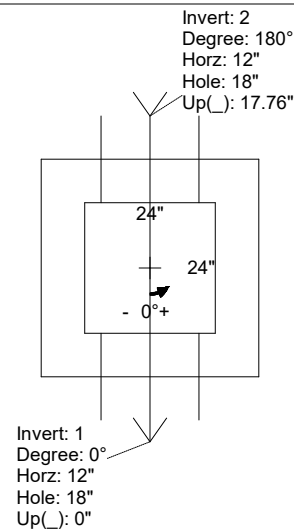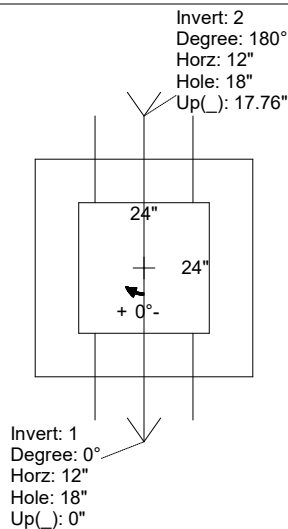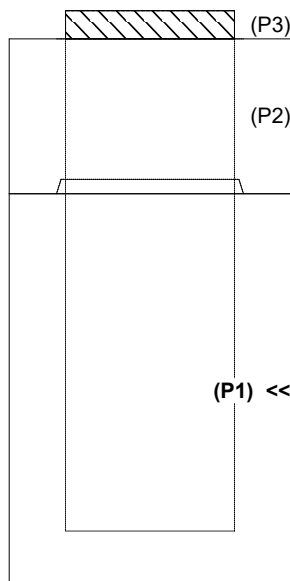

INSIDE WALL DIMENSIONS

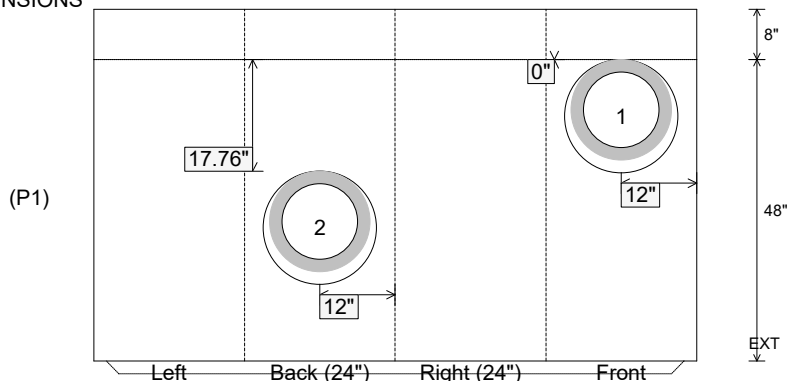

Coating (Int):
Coating (Ext):

Seam Up: Tongue
Seam Dn: n/a

Wall Thickness: 8"
Floor Height: 8"

Height (Int): 48"
Height (Ext): 56"

Weight (Net): 4857 lb
Volume (Net): 1.24cu.yd
