

Job Name: 26-3232 - 2-10 Hoop Drive
Job Location: Walton, KY
Contractor: Kemper Construction

Plant: 100
9/4/2026 1:16:27 PM

Tech: Jared - F
PC: E. Bradley



Structure ID: 3 CB2-2

P2 BX242408-VF

BOX RISER 8inW, Variable Ht

- P3) 24" x 24" - CASTING HEIGHT - 4"
P2) 24" x 24" - BOX RISER 8inW, Variable Ht - 22"
P1) 24" x 24" - BOX BASE 8inW, 8inF - 48"
1) CASTING - HOE 280T F/G
2) 24" x 24" - Conseal CS-102 1.00"
2) Hole - 18



- Structure Notes: .
1. PER ASTM C913 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO STEPS AND NO INVERT CHANNEL.
4. CASTING BY ICAST (HOE 280T F/G).
REINFORCING PER ASTM A615 (GRADE 60).
- WALLS (As .12) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .12) #5 BARS AT 12" C.C.E.W.

0 lb
1890 lb
4857 lb
182 lb
0 lb
0 lb
Structure Total: 6929 lb


Rim: 944.41' Rim to Invert: 6.09' Slack: 1.08" Sump: 2" Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

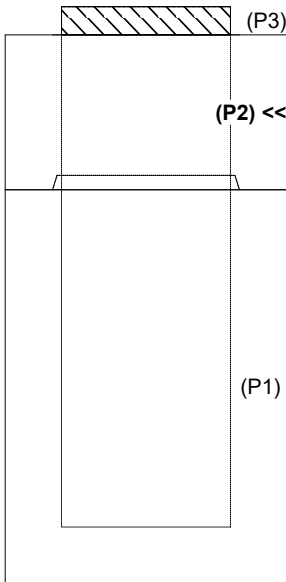

INSIDE WALL DIMENSIONS



Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 8" Floor Height: 0"	Height (Int): 22" Height (Ext): 22"	Weight (Net): 1890 lb Volume (Net): 0.48cu.yd
----------------------------------	----------------------------------	--	--	--
