

Contractor: PECCO, Inc.

TECH: Jared - F

Plant: 100



Size: 24" x 36"

Rim to Invert: 10.34'

Floor Height: 8"

Slack: 0.08"

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

0 lb

Structure Total: 19329 lb


Invert: 1
Degree: 0°

Invert: 3
Degree: 270°

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	946.36'							
Reducer								
Invert 1	936.02'	0°	18" HDPE	21.2"	24"	Hole 24	-1.6"	P1
Invert 2	941.68'	135°	15" HDPE	17.6"	20"	Hole 20	16.62"	P2
Invert 3	941.68'	270°	15" HDPE	17.6"	20"	Hole 20	16.62"	P2
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

24" x 36" - BOX BASE 8inW, 8inF - 48" - (P1)

Front Right Back Left

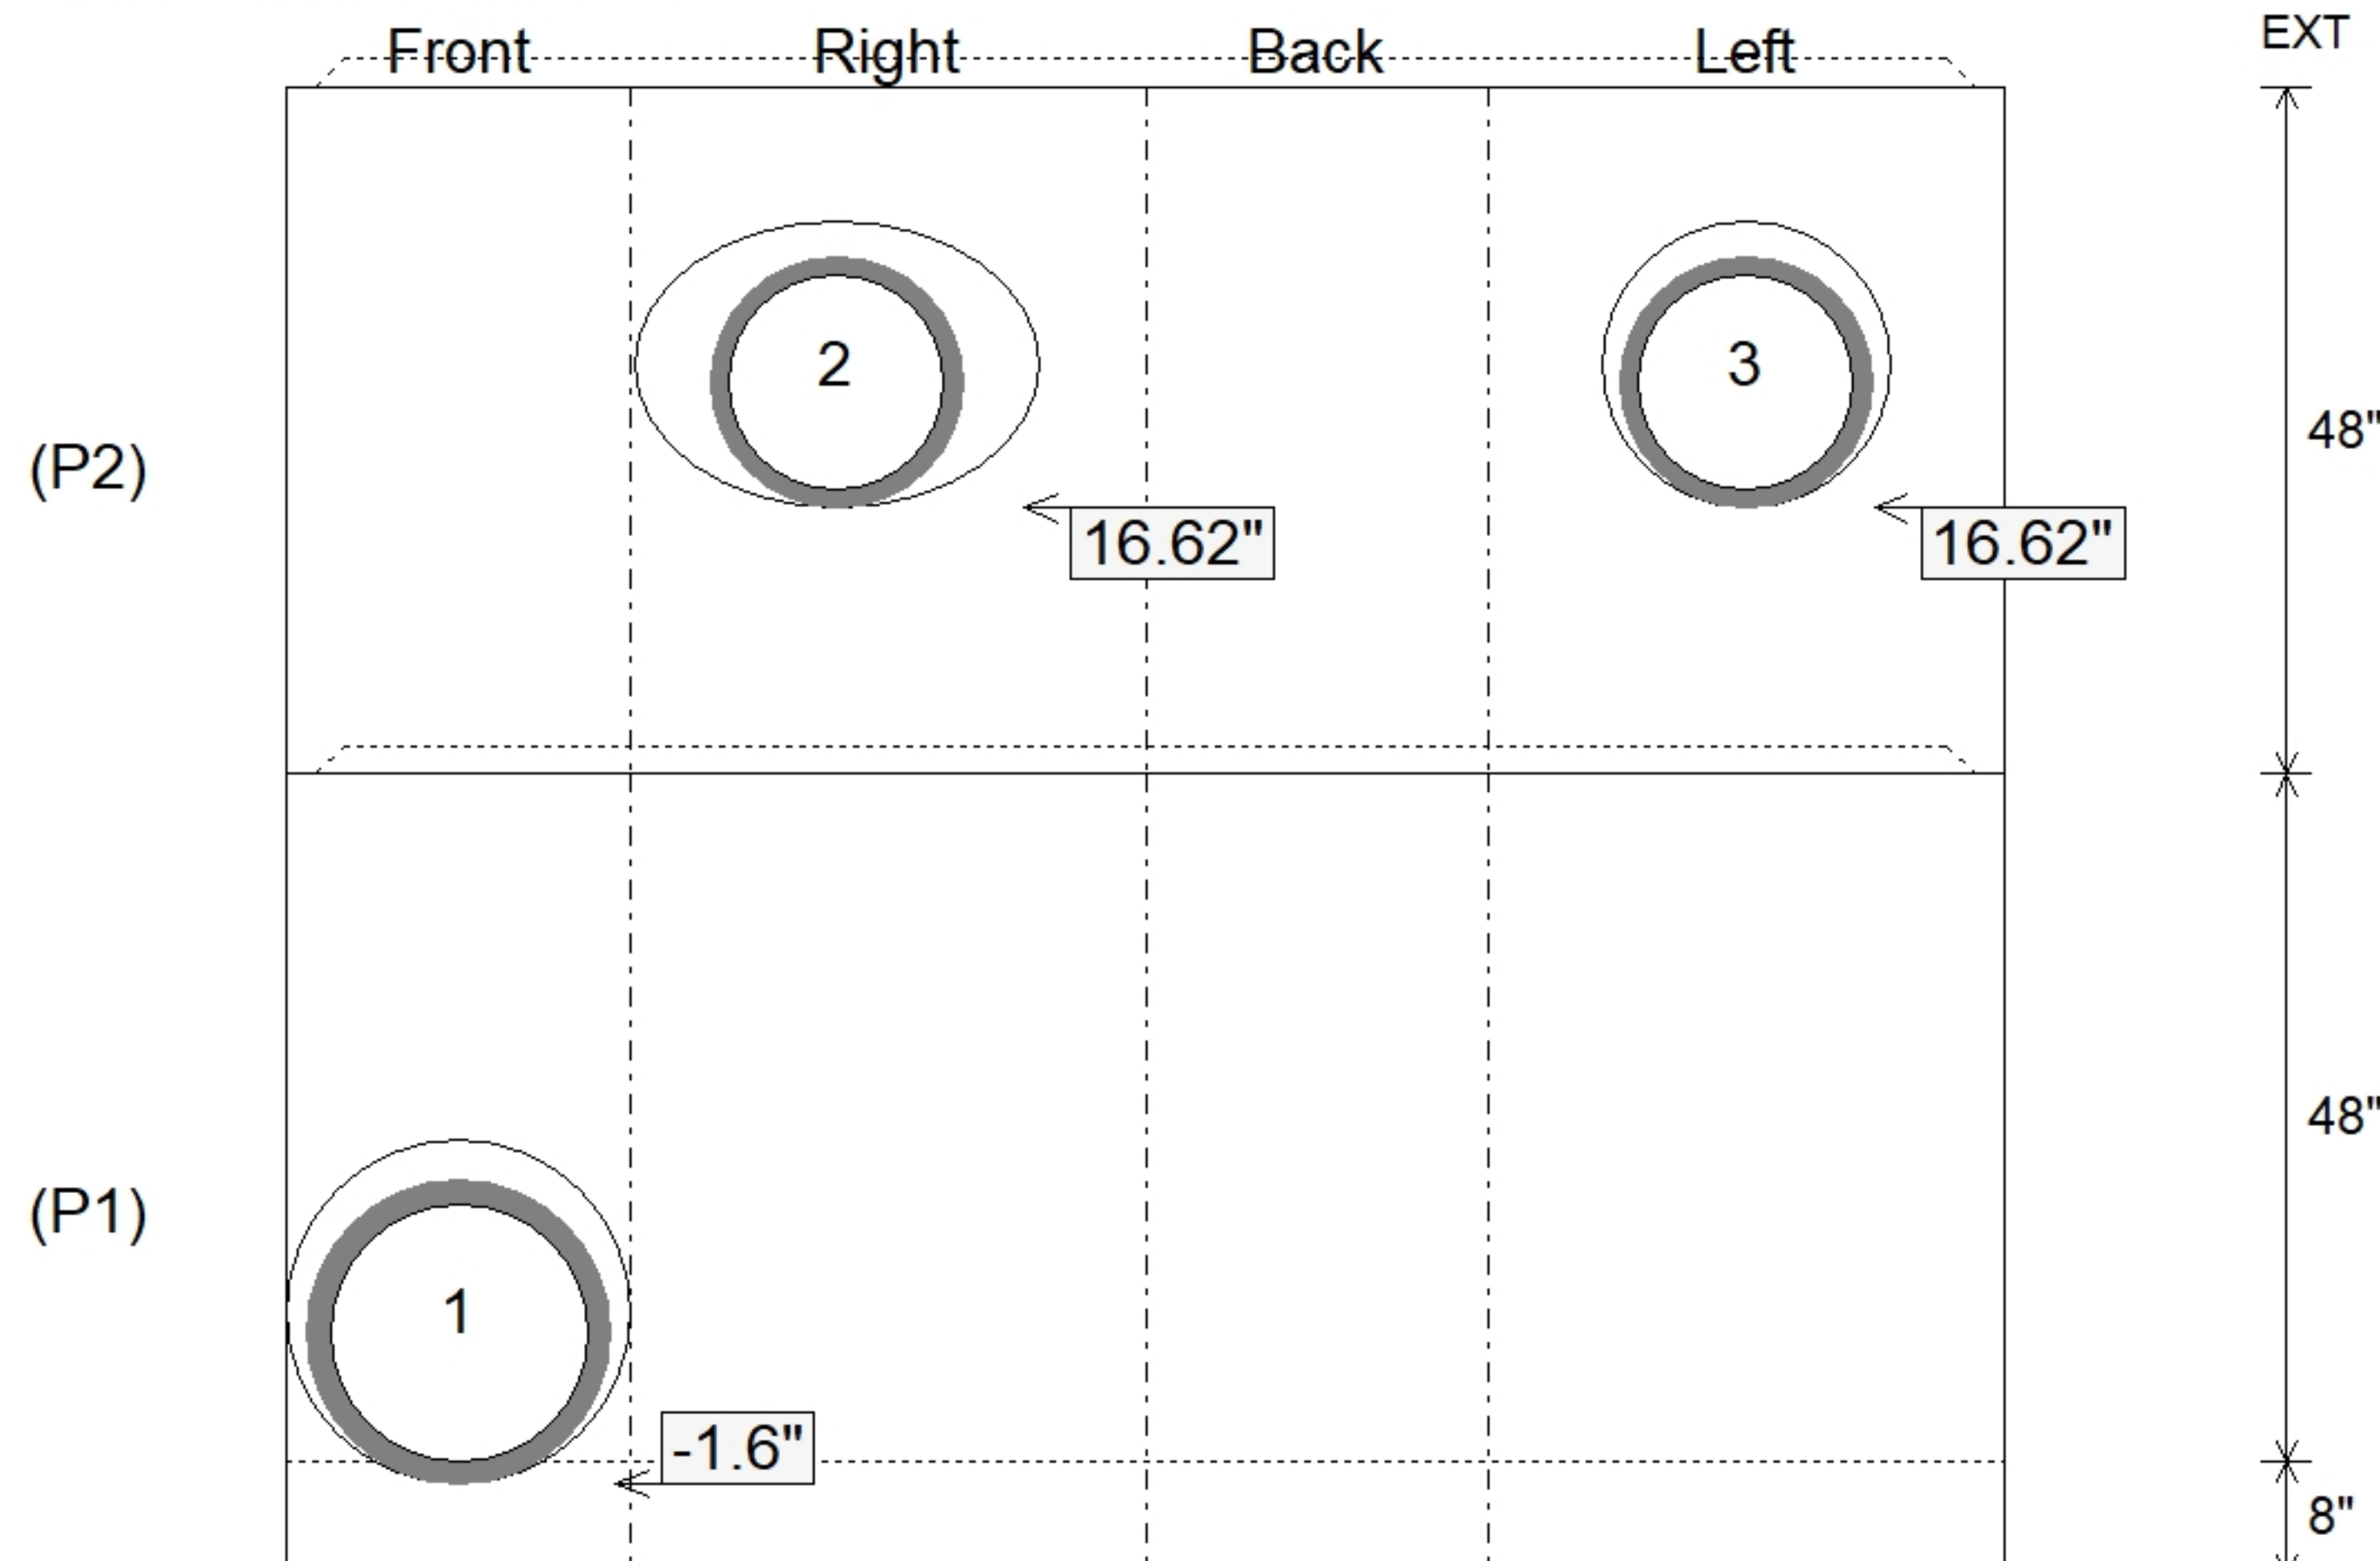

8/27/2026 12:16:05 PM

APPROVED BY:
