

Contractor: PECCO, Inc.

Plant: 100



Size: 24" x 36"

Rim to Invert: 4.53'

Floor Height: 8"


Slack: 0.36"

REINFORCING PER ASTM A615 (GRADE 60).

- TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W.
- WALLS/RISER (As .31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


0 lb

Structure Total:	24114 lb
------------------	----------

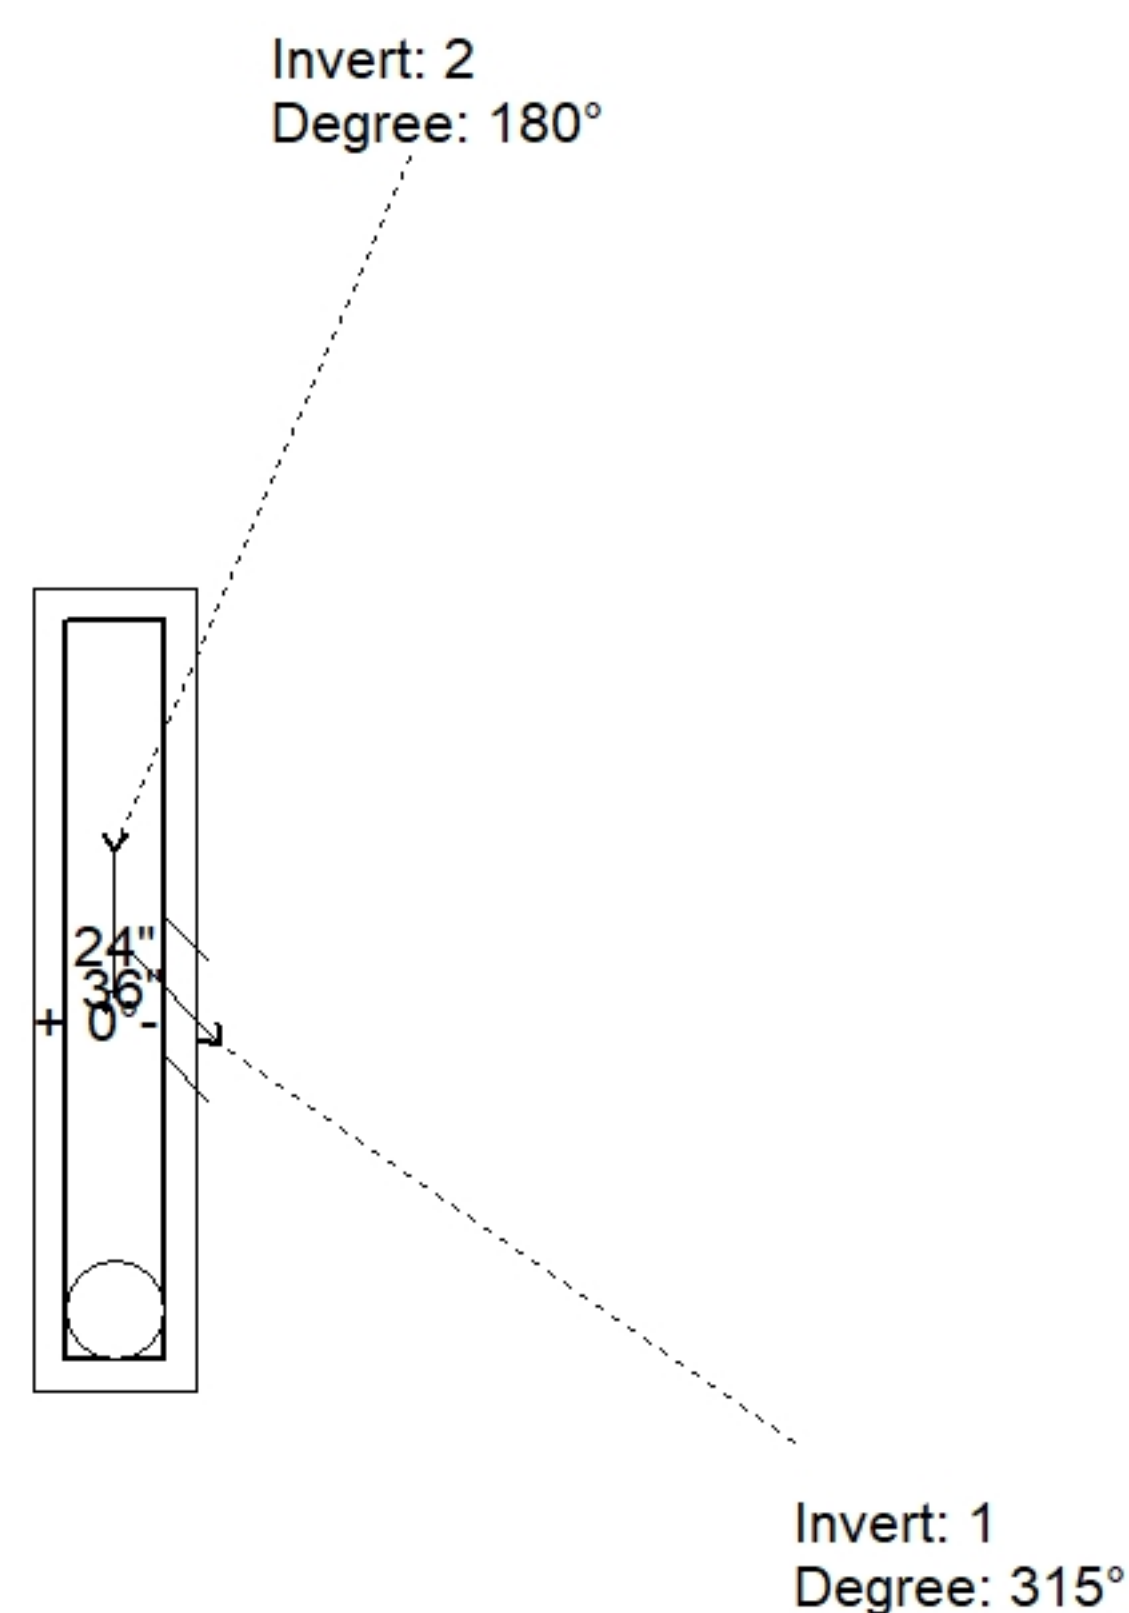

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	935.8'							
Reducer								
Invert 1	931.27'	315°	18" HDPE	21.2"	24" x 27.5"	DOGHOUSE INVRTD 24"x27.5"	6.4"	P2
Invert 2	931.27'	180°	18" HDPE	21.2"	24" x 27.5"	DOGHOUSE INVRTD 24"x27.5"	6.4"	P2
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

(P2)

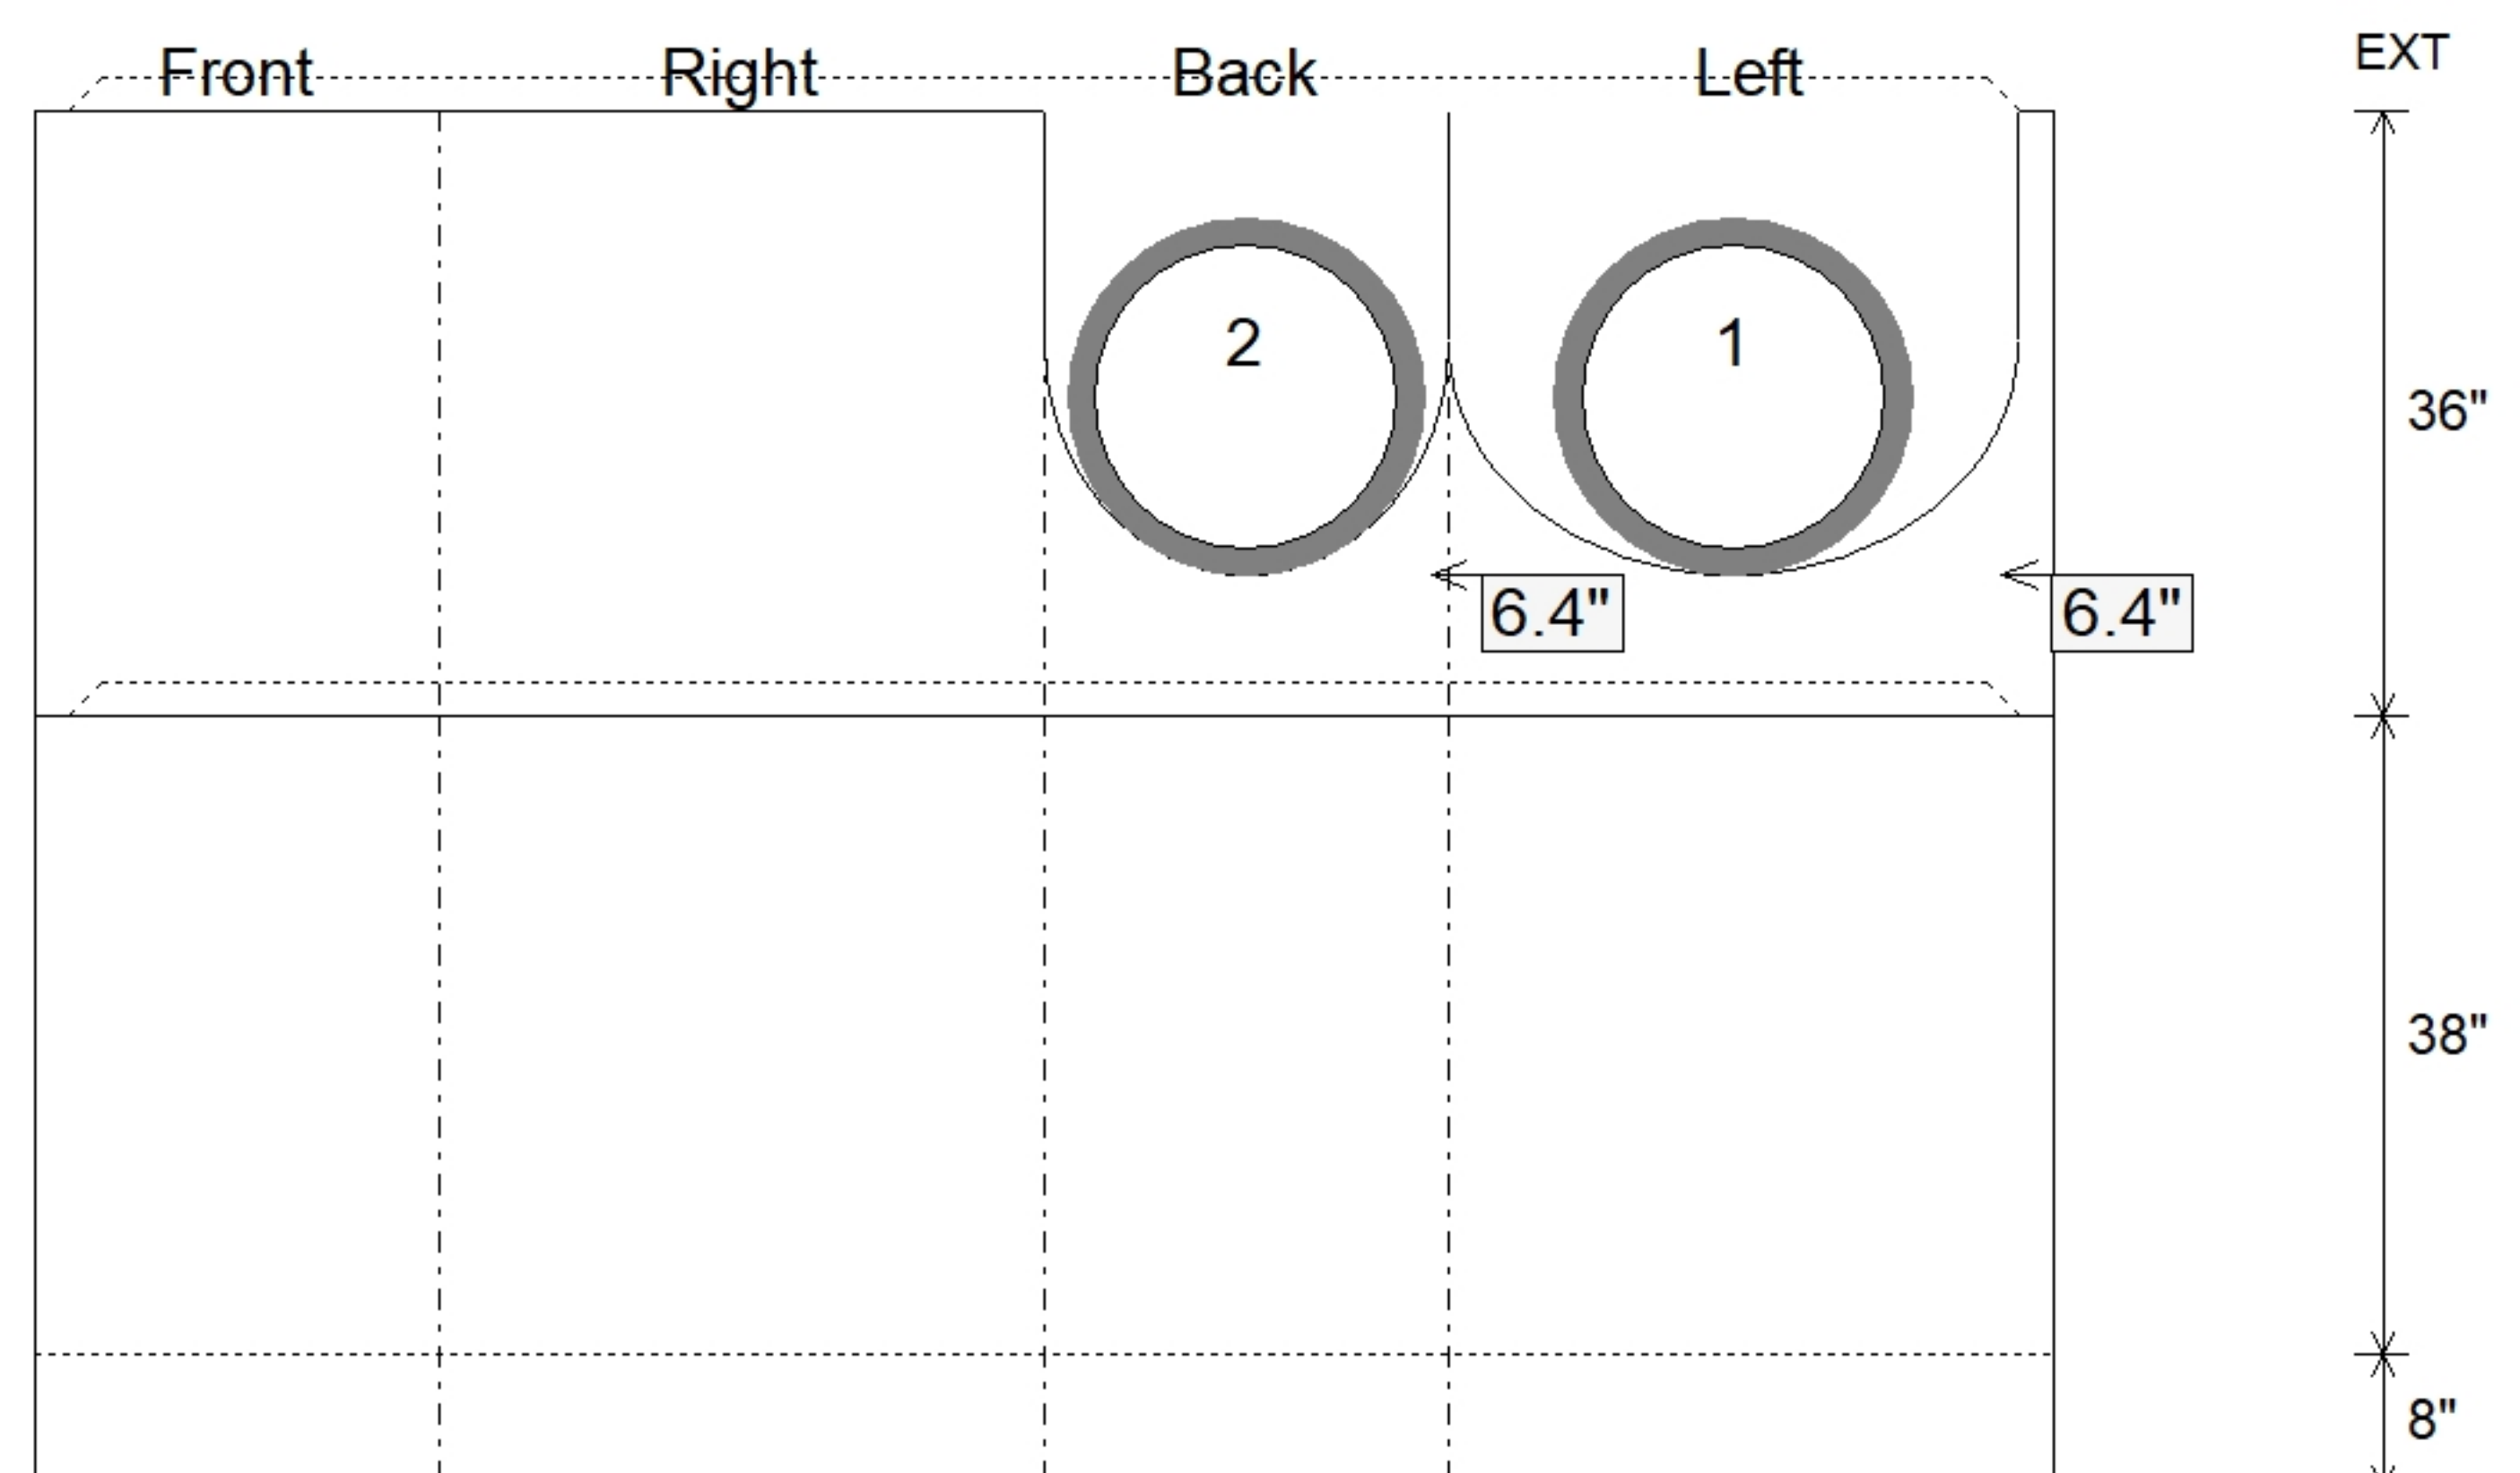

(P1)

SUBMITTAL
APPROVED BY:
