



Job Name: 26-3280 - G.N. Miles Estates Subdivision Ph.4 Job Location: Nicholasville, KY Contractor: PECCO, Inc.				Plant: 100 8/24/2026 11:00:48 AM		Tech: Jared - F PC: A. Chambers				
Structure ID: CI401 CBIA										
P1 BX24120-08BVF		BOX BASE 8inW, 8inF, Variable Ht T/n								
P2) 24" x 120" - CB INLET KY A 10' TOP SAG F/G - 10" P1) 24" x 120" - BOX BASE 8inW, 8inF, Variable Ht T/n - 28" 1) CASTING - HOE KY-206 F/C (KY CBI A) 1) 24" x 120" - Conseal CS-102 1.00" 1) DOGHOUSE INVRTD - 20"x20" 1) Horiz Slot n/n - 120"x8" 1) Orifice - 5"				3398 lb 8789 lb 206 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 12394 lb		Structure Notes: 1. PER KYTC CBI TYPE A / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PI AT 28 DAYS. 3. CASTING BY ICAST (HOE KY-206 F/C (KY CBI A)). 4. #5 BAR @ 12" C.C.E.W. (GRADE 60) TO BE STUBBED OUT OF 120"X8" THROAT (INVERT 2) FOR CURB POUR TIE-IN. REINFORCING PER ASTM A615 (GRADE 60). - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W. - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 950.82'		Rim to Invert: 3.22'		Slack: 0.64"		Sump: 0"		Step Position:		
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	947.6'	90°	68"	15" HDPE	17.6"	DOGHOUSE INVRTD 20"x20"	20" x 20"	20"	-2.5"	0"
Invert 2	949.265'	90°	68"	120" x 8" Horiz Slot	120" x 8"	Horiz Slot 120"x8"	120" x 8"	120"	20"	0"
Invert 3	948.52'	90°	86"	5" Orifice	5"	Orifice 5"	5"	5"	11"	18"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

FIRST POUR DRAWING

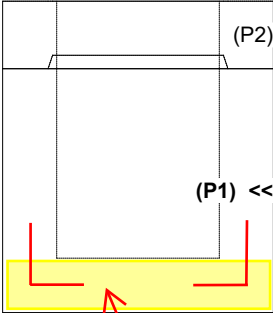

RIGHT-SIDE UP VIEW (int. dimensions)

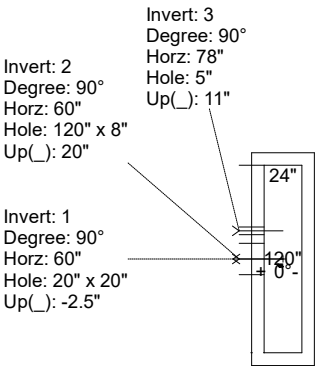

UPSIDE-DOWN VIEW (int. dimensions)


WEIGHTS

FIRST POUR - 3,652 LBS

SECOND POUR - 5,137 LBS

TOTAL - 8,789 LBS


INSIDE WALL DIMENSIONS




Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 28" Height (Ext): 36"	Weight (Net): 8789 lb Volume (Net): 2.24cu.yd
----------------------------------	---------------------------------	--	--	--

Job Name: 26-3280 - G.N. Miles Estates Subdivision Ph.4 Job Location: Nicholasville, KY Contractor: PECCO, Inc.				Plant: 100 8/24/2026 11:00:48 AM		Tech: Jared - F PC: A. Chambers				
Structure ID: CI401 CBIA										
P1 BX24120-08BVF		BOX BASE 8inW, 8inF, Variable Ht T/n								
P2) 24" x 120" - CB INLET KY A 10' TOP SAG F/G - 10" P1) 24" x 120" - BOX BASE 8inW, 8inF, Variable Ht T/n - 28" 1) CASTING - HOE KY-206 F/C (KY CBI A) 1) 24" x 120" - Conseal CS-102 1.00" 1) DOGHOUSE INVRTD - 20"x20" 1) Horiz Slot n/n - 120"x8" 1) Orifice - 5"				3398 lb 8789 lb 206 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 12394 lb		Structure Notes: 1. PER KYTC CBI TYPE A / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PI AT 28 DAYS. 3. CASTING BY ICAST (HOE KY-206 F/C (KY CBI A)). 4. #5 BAR @ 12" C.C.E.W. (GRADE 60) TO BE STUBBED OUT OF 120"X8" THROAT (INVERT 2) FOR CURB POUR TIE-IN. REINFORCING PER ASTM A615 (GRADE 60). - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W. - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 950.82'		Rim to Invert: 3.22'		Slack: 0.64"		Sump: 0"		Step Position:		
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	947.6'	90°	68"	15" HDPE	17.6"	DOGHOUSE INVRTD 20"x20"	20" x 20"	20"	-2.5"	0"
Invert 2	949.265'	90°	68"	120" x 8" Horiz Slot	120" x 8"	Horiz Slot 120"x8"	120" x 8"	120"	20"	0"
Invert 3	948.52'	90°	86"	5" Orifice	5"	Orifice 5"	5"	5"	11"	18"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

SECOND POUR DRAWING

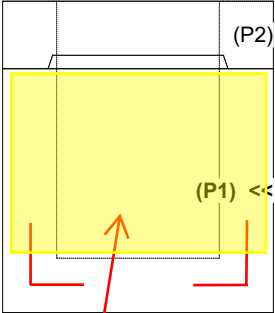


RIGHT-SIDE UP VIEW (int. dimensions)

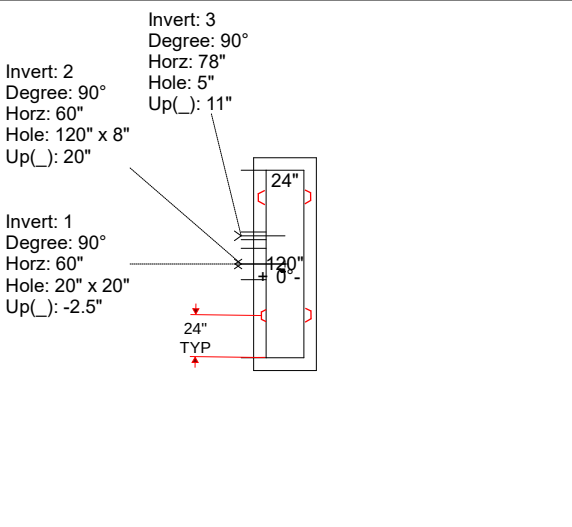


UPSIDE-DOWN VIEW (int. dimensions)

WEIGHTS
FIRST POUR - 3,652 LBS
SECOND POUR - 5,137 LBS
TOTAL - 8,789 LBS



REBAR STUB DETAIL

INSIDE WALL DIMENSIONS



Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 28" Height (Ext): 36"	Weight (Net): 8789 lb Volume (Net): 2.24cu.yd
----------------------------------	---------------------------------	--	--	--
