

Contractor: PECCO, Inc.

TECH: Jared - F

Plant: 100



Size: 24" x 120"

Rim to Invert: 3.36'

Floor Height: 8"

Slack: 0.32"

REINFORCING PER ASTM A615 (GRADE 60).

- TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W.
- WALLS (As .31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

1) Orifice - 5"

0 lb

Structure Total: 21785 lb


Invert: 3
Degree: 270°

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')_	Ref
Rim	950.75'							
Reducer								
Invert 1	947.39'	125°	15" HDPE	17.6"	20"	Hole 20	39.5"	P1
Invert 2	947.39'	270°	15" HDPE	17.6"	20"	Hole 20	39.5"	P1
Invert 3	949.223'	270°	120" x 8" Horiz Slot	120" x 8"	120" x 8"	Horiz Slot 120"x8"	63.996"	P1
Invert 4	948.47'	270°	5" Orifice	5"	5"	Orifice 5"	54.96"	P1
Invert 5								
Invert 6								
Invert 7								
Invert 8								

24" x 120" - CB INLET KY A 10' TOP LEFT - 10" - (P2)

24" x 120" - BOX BASE 8inW, 8inF, Variable Ht - 72" - (P1)

Default - Interior Dimensions

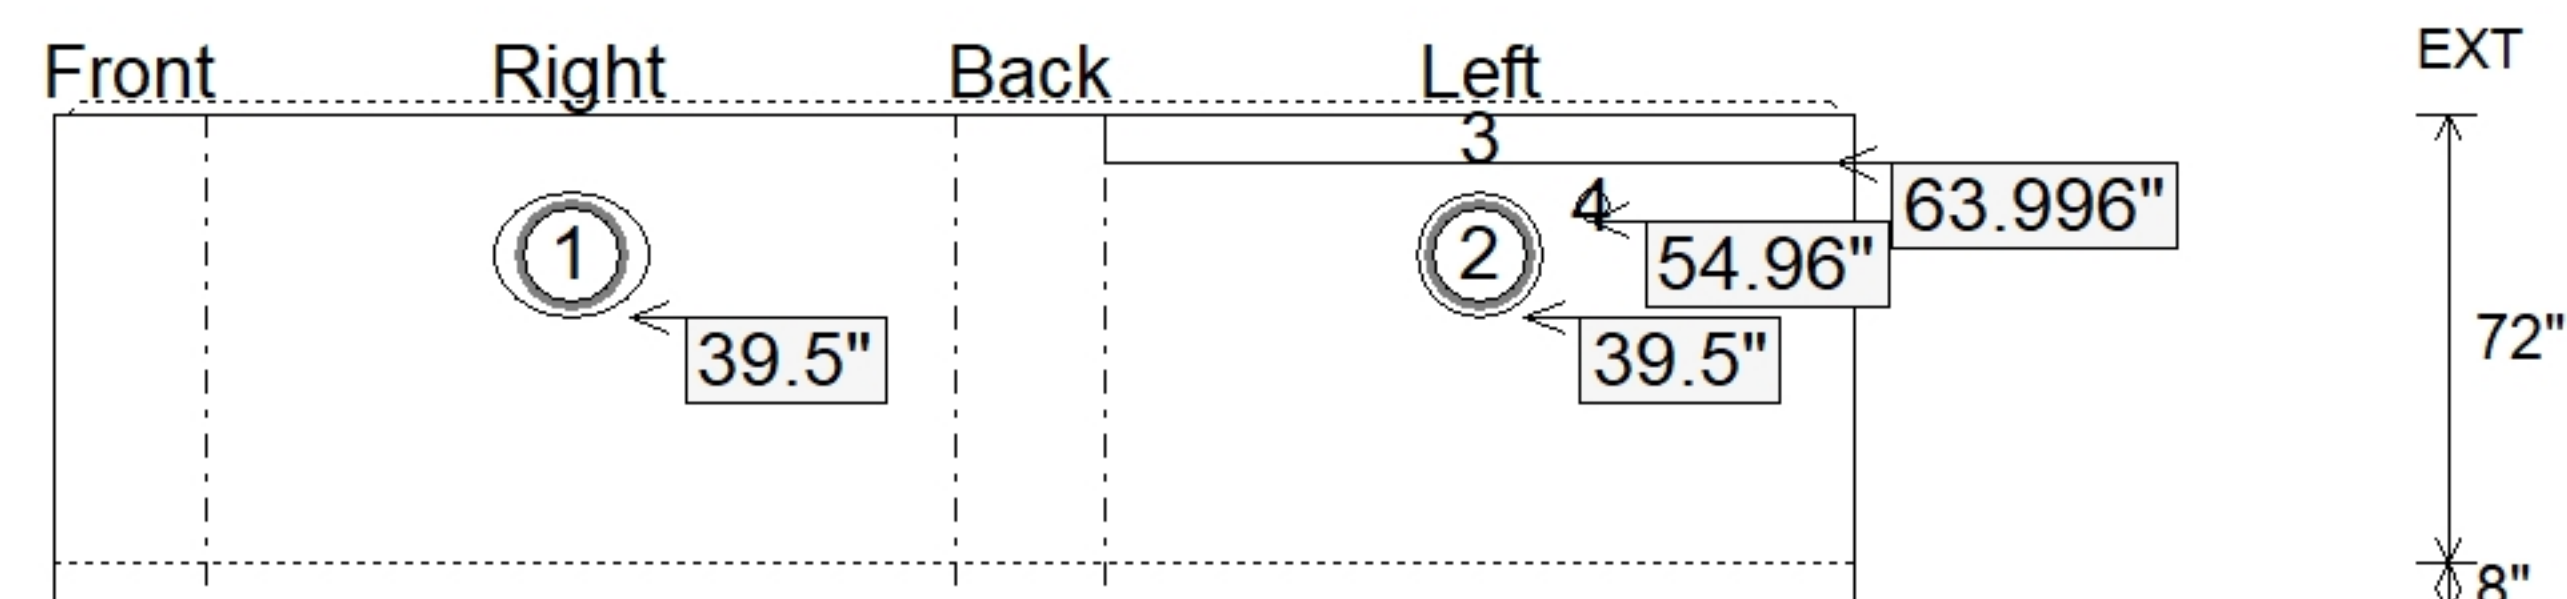

SUBMITTAL
APPROVED BY:
