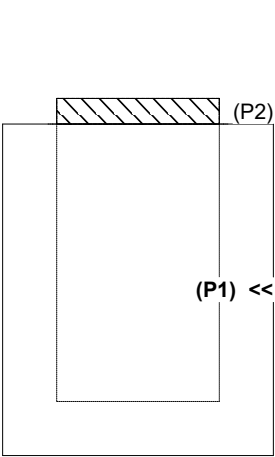

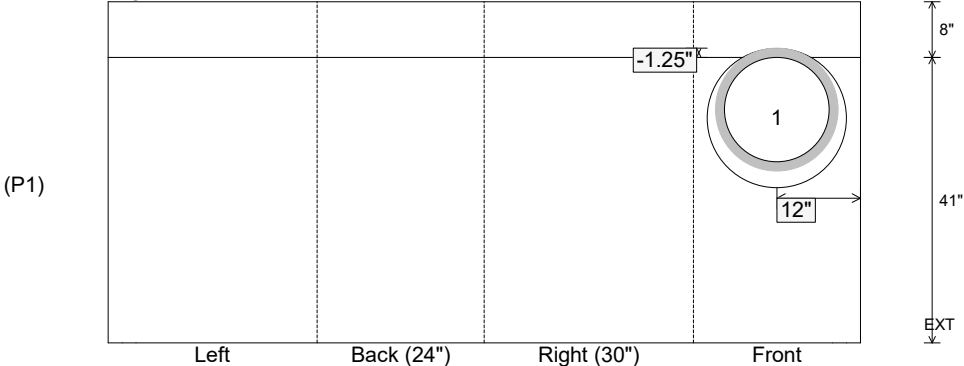


Job Name: 26-3280 - G.N. Miles Estates Subdivision Ph.4 Job Location: Nicholasville, KY Contractor: PECCO, Inc.				Plant: 100 8/24/2026 11:00:44 AM		Tech: Jared - F PC: A. Chambers				
Structure ID: DB201 DBI11										
P1 BX24300808VF				BOX BASE 8inW, 8inF, Variable Ht F/n						
P2) 24" x 30" - CASTING HEIGHT - 3.75" P1) 24" x 30" - BOX BASE 8inW, 8inF, Variable Ht F/n - 41" 1) CASTING - HOE KY-460-11 F/G (DBI 11) 1) 24" x 30" - Conseal CS-102 1.00" 1) Hole - 20"				0 lb 4878 lb 421 lb 0 lb 0 lb ----- Structure Total: 5299 lb		Structure Notes: 1. KYTC DBI TYPE 11 / ASTM C-913 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE KY-460-11 F/G (DBI 11)). REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W.. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 940.74' Rim to Invert: 3.8' Slack: 0.85" Sump: 0" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	936.94'	0°	20"	15" HDPE	17.6"	Hole 20	20"	20"	-1.25"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										
RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimensions)  INSIDE WALL DIMENSIONS 										
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 41" Height (Ext): 49"		Weight (Net): 4878 lb Volume (Net): 1.25cu.yd	
