

Job Name: 26-3292 ADS Kroger V#435
Job Location: Murray, KY
Contractor: ADS Advanced Drainage Systems, Inc.

Plant: Beaver Dam
8/20/2026 9:27:16 AM

Tech: S. Felletter
PC: T. Ryan



Structure ID: D3


P4 MH096LD17-CON

MH FLAT TOP w/ 24" Conc. Hole F/G

- P5) 24" - CASTING HEIGHT - 7"
P4) 96" - MH FLAT TOP w/ 24" Conc. Hole F/G - 17"
P3) 96" - MH RISER NO STEPS T/G - 66"
P2) 96" - MH RISER NO STEPS T/G - 84"
P1) 96" - MH BASE T/n - 24"
1) ASSEMBLY REQUIRED - BRACKETS ONLY
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) CASTING - HOE MC-375 F/C Storm
3) 96" - Conseal CS-102 1.25" (Double)
2) Hole - 30

0 lb
10473 lb
15359 lb
20926 lb
12831 lb
0 lb
0 lb
0 lb
271 lb
0 lb
0 lb
Structure Notes:
1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING BY ICAST (HOE MC-375 F/C "STORM").
4. ASSEMBLY REQUIRED - BRACKETS ONLY.
REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
- RISER/WALLS (As .24)
- FLOOR (As .47) #5 BARS AT 8" C.C.E.W.

Structure Total: 59859 lb

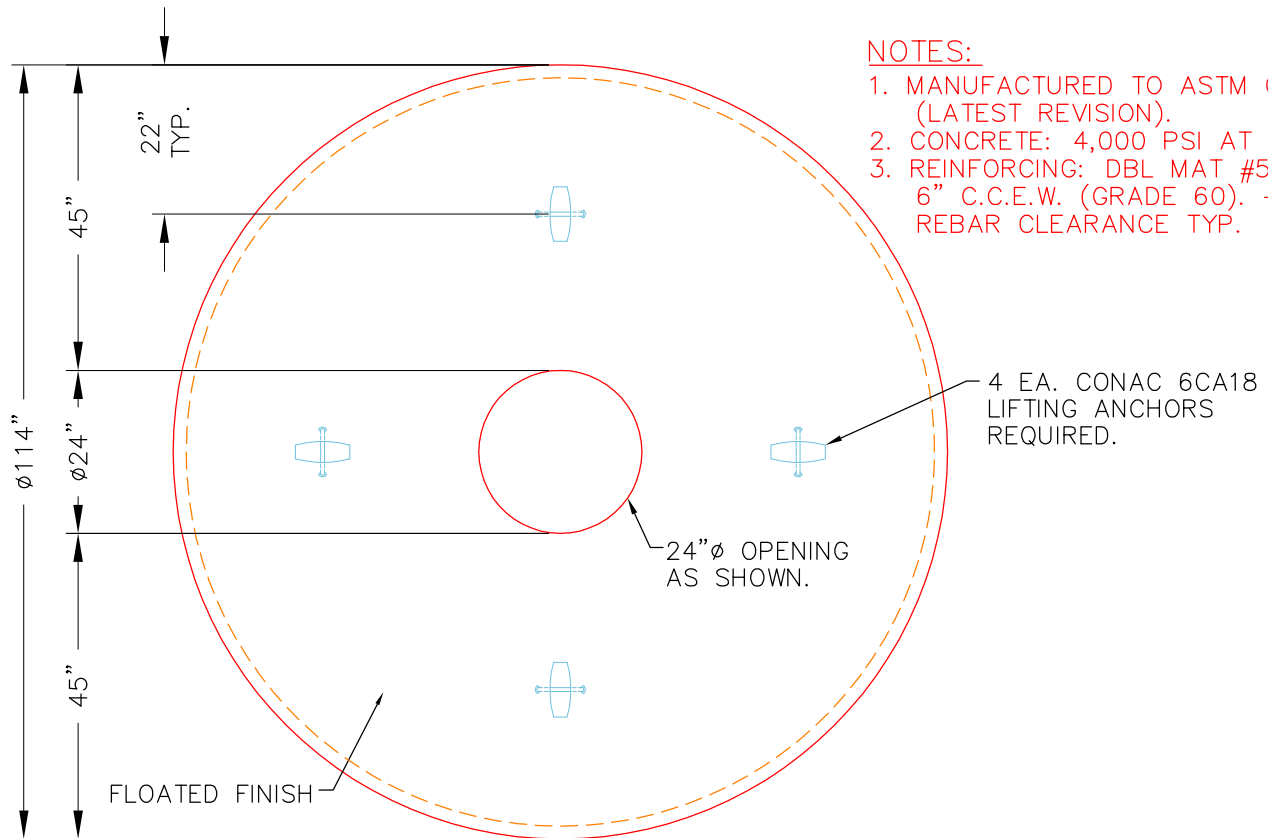

NOTES:


1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: DBL MAT #5 BAR @ 6" C.C.E.W. (GRADE 60). - 2" MIN. REBAR CLEARANCE TYP.

4 EA. CONAC 6CA18
LIFTING ANCHORS
REQUIRED.

24"Ø OPENING
AS SHOWN.

FLOATED FINISH

TOP VIEW

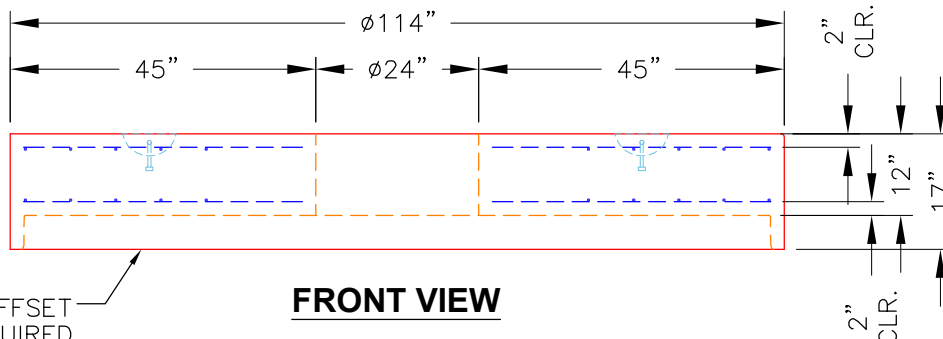

STANDARD SINGLE OFFSET
GROOVE JOINT REQUIRED

FRONT VIEW

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 9"	Height (Ext): 17"	Weight (Net): 10473 lb Volume (Net): 2.68cu.yd
----------------------------------	----------------------------------	--------------------	-------------------	---
