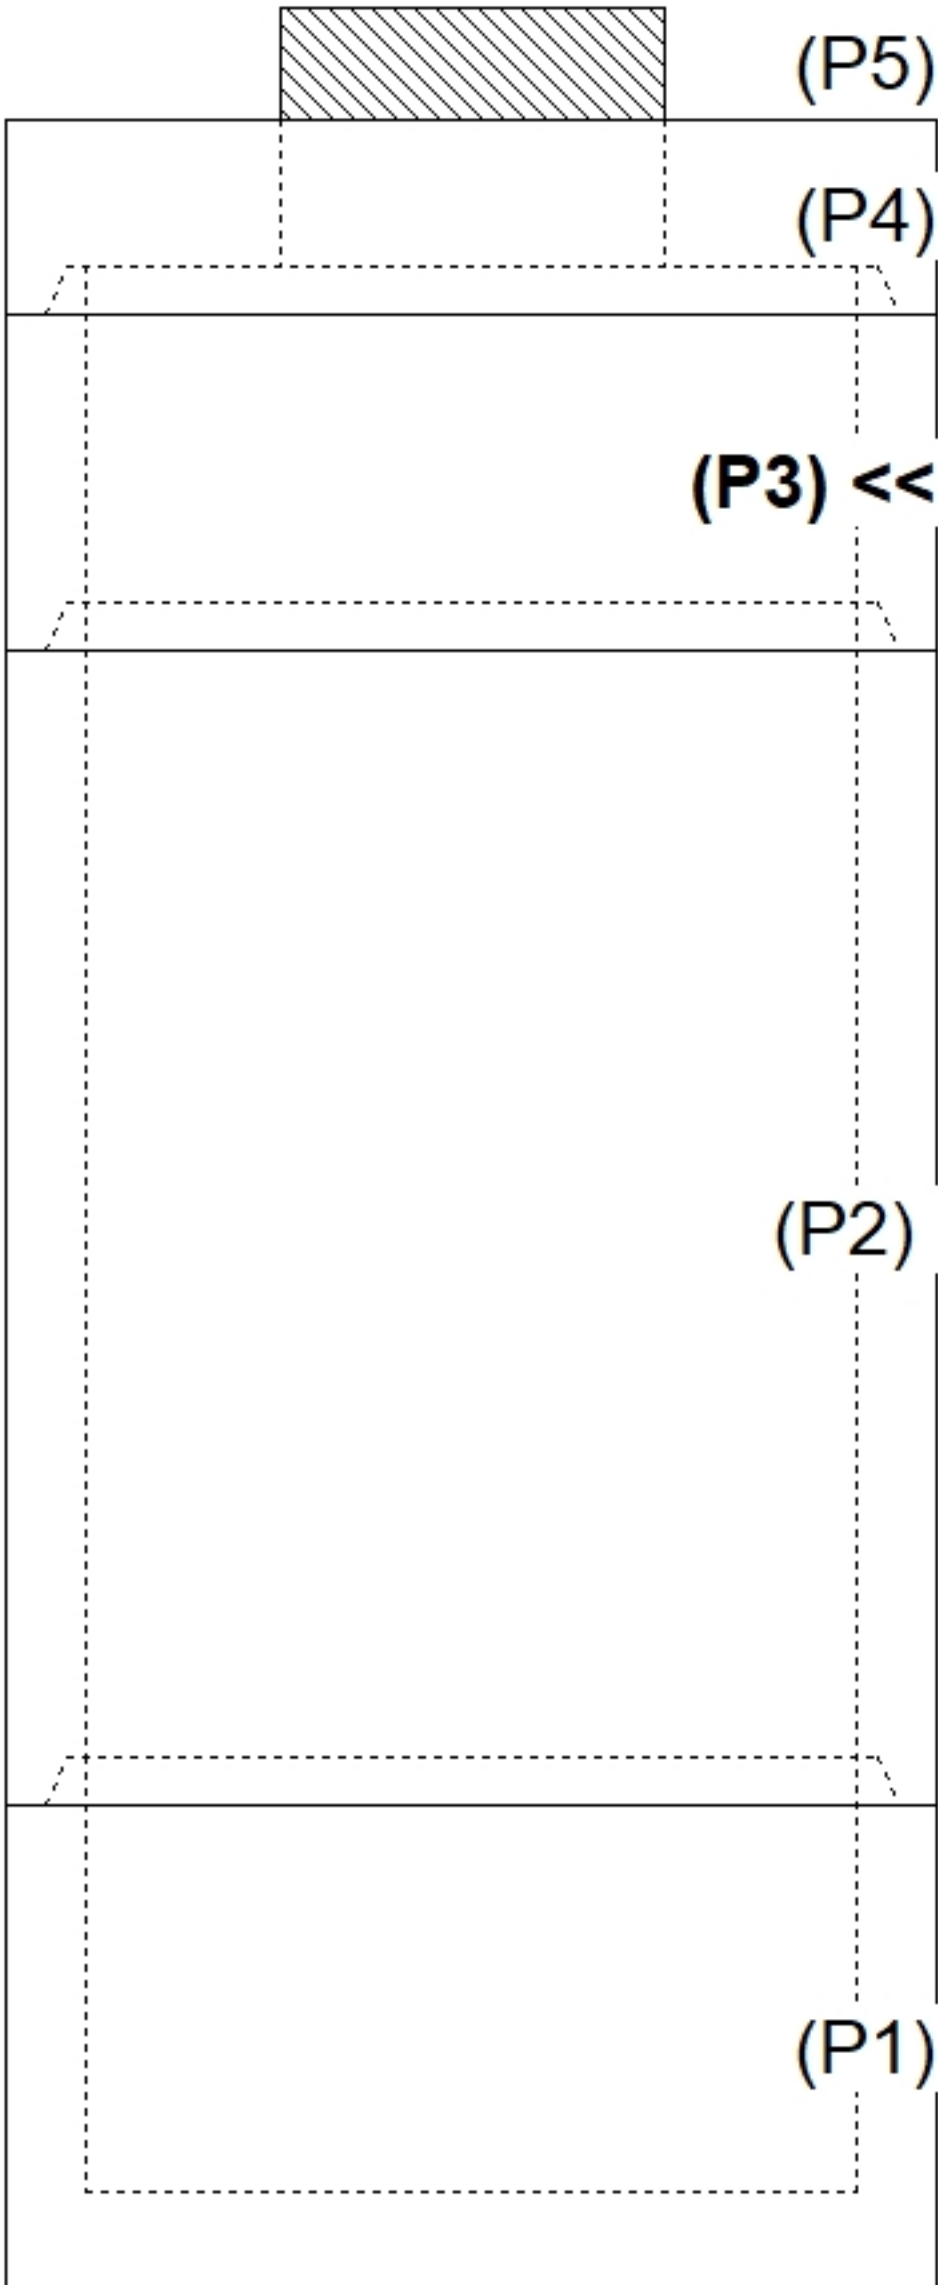
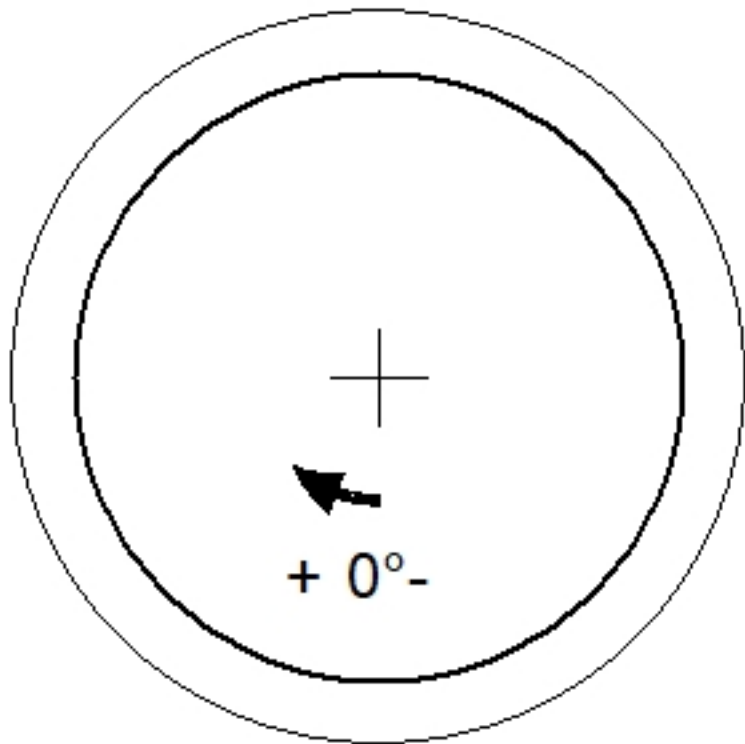
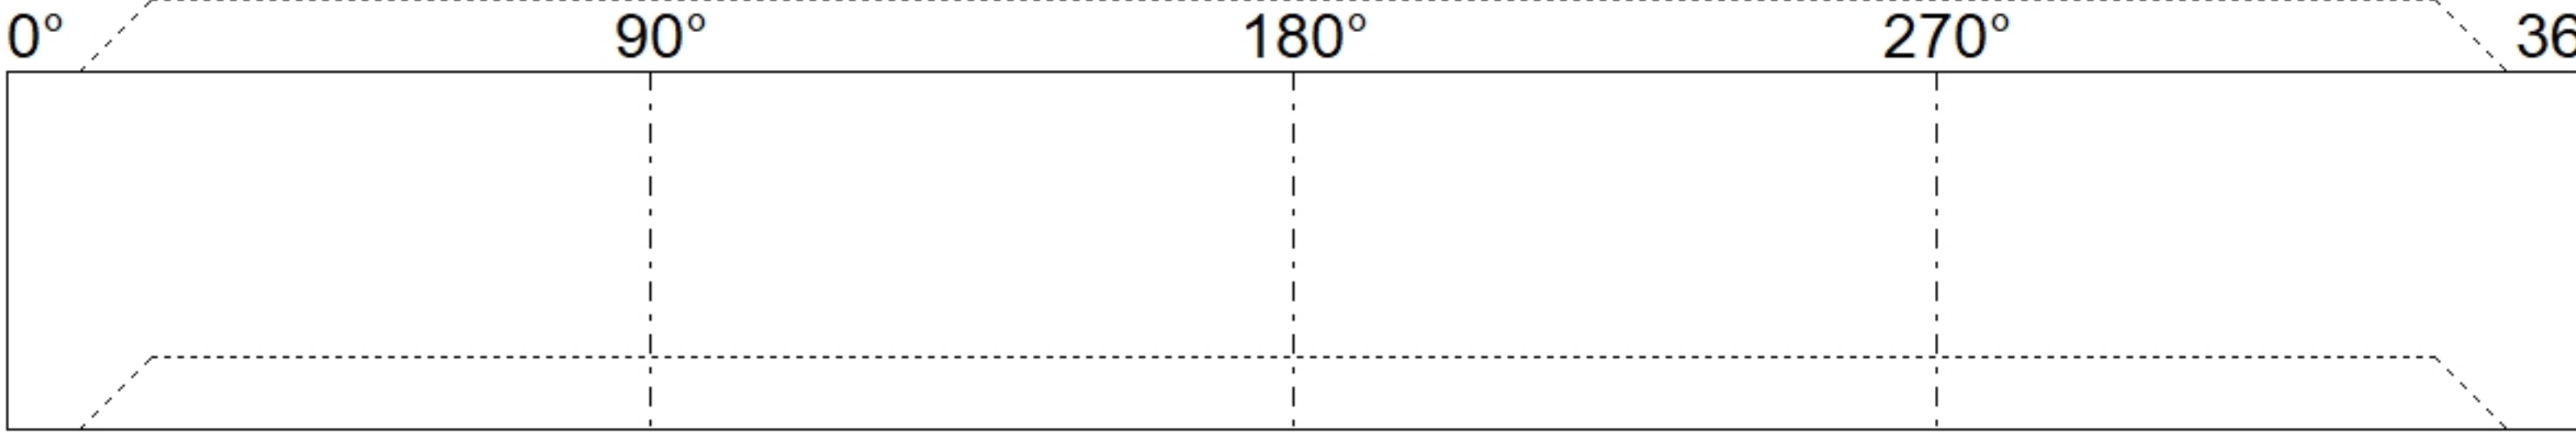


Job Name: 26-3424 ADS Speedway #42789 Job Location: Louisville, KY Contractor: ADS Advanced Drainage Systems, Inc.					Plant: Beaver Dam 8/26/2026 12:10:30 PM		Tech: S. Felletter PC: M. Sullivan						
Structure ID: WQU													
P3		MH048RSVF		MH RISER Custom Ht T/G									
P5) 24" - CASTING HEIGHT - 7" P4) 48" - MH FLAT LID w/24" Center Hole F/G - 12" P3) 48" - MH RISER Custom Ht T/G - 21" P2) 48" - MH RISER T/G - 72" P1) 48" - MH BASE T/n - 24" 1) ASSEMBLY REQUIRED 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-375 F/C Storm 3) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 1) Hole - 14 1) Hole - 16						0 lb 1580 lb 1467 lb 4810 lb 3007 lb 0 lb 0 lb 0 lb 271 lb 0 lb 0 lb 0 lb 0 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-375 F/C "STORM"). 4. LIFTING ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE. . REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.					
Rim: 544.9' Rim to Invert: 4.63' Slack: 0.56" Sump: 81" Step Position: 0°						Structure Total: 11135 lb							
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset			
Invert 1													
Invert 2													
Invert 3													
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													
RIGHT-SIDE UP VIEW (int. dimensions)													
													
INSIDE WALL DIMENSIONS													
				EXT 21"									
Coating (Int): Coating (Ext):				Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 5" Floor Height: 0"		Height (Int): 21" Height (Ext): 21"		Weight (Net): 1467 lb Volume (Net): 0.38cu.yd			
