

Contractor: Schroeder Construction, Inc.

Plant: Beaver Dam



Size: 48"

Rim to Invert: 12.77'

Floor Height: 6"


Slack: 0.24"

RFI: VERIFY ALL INVERT ELEVATIONS


12) MH Step ML-10-TDS-NCR - 10"

0 lb

Structure Total: 16605 lb

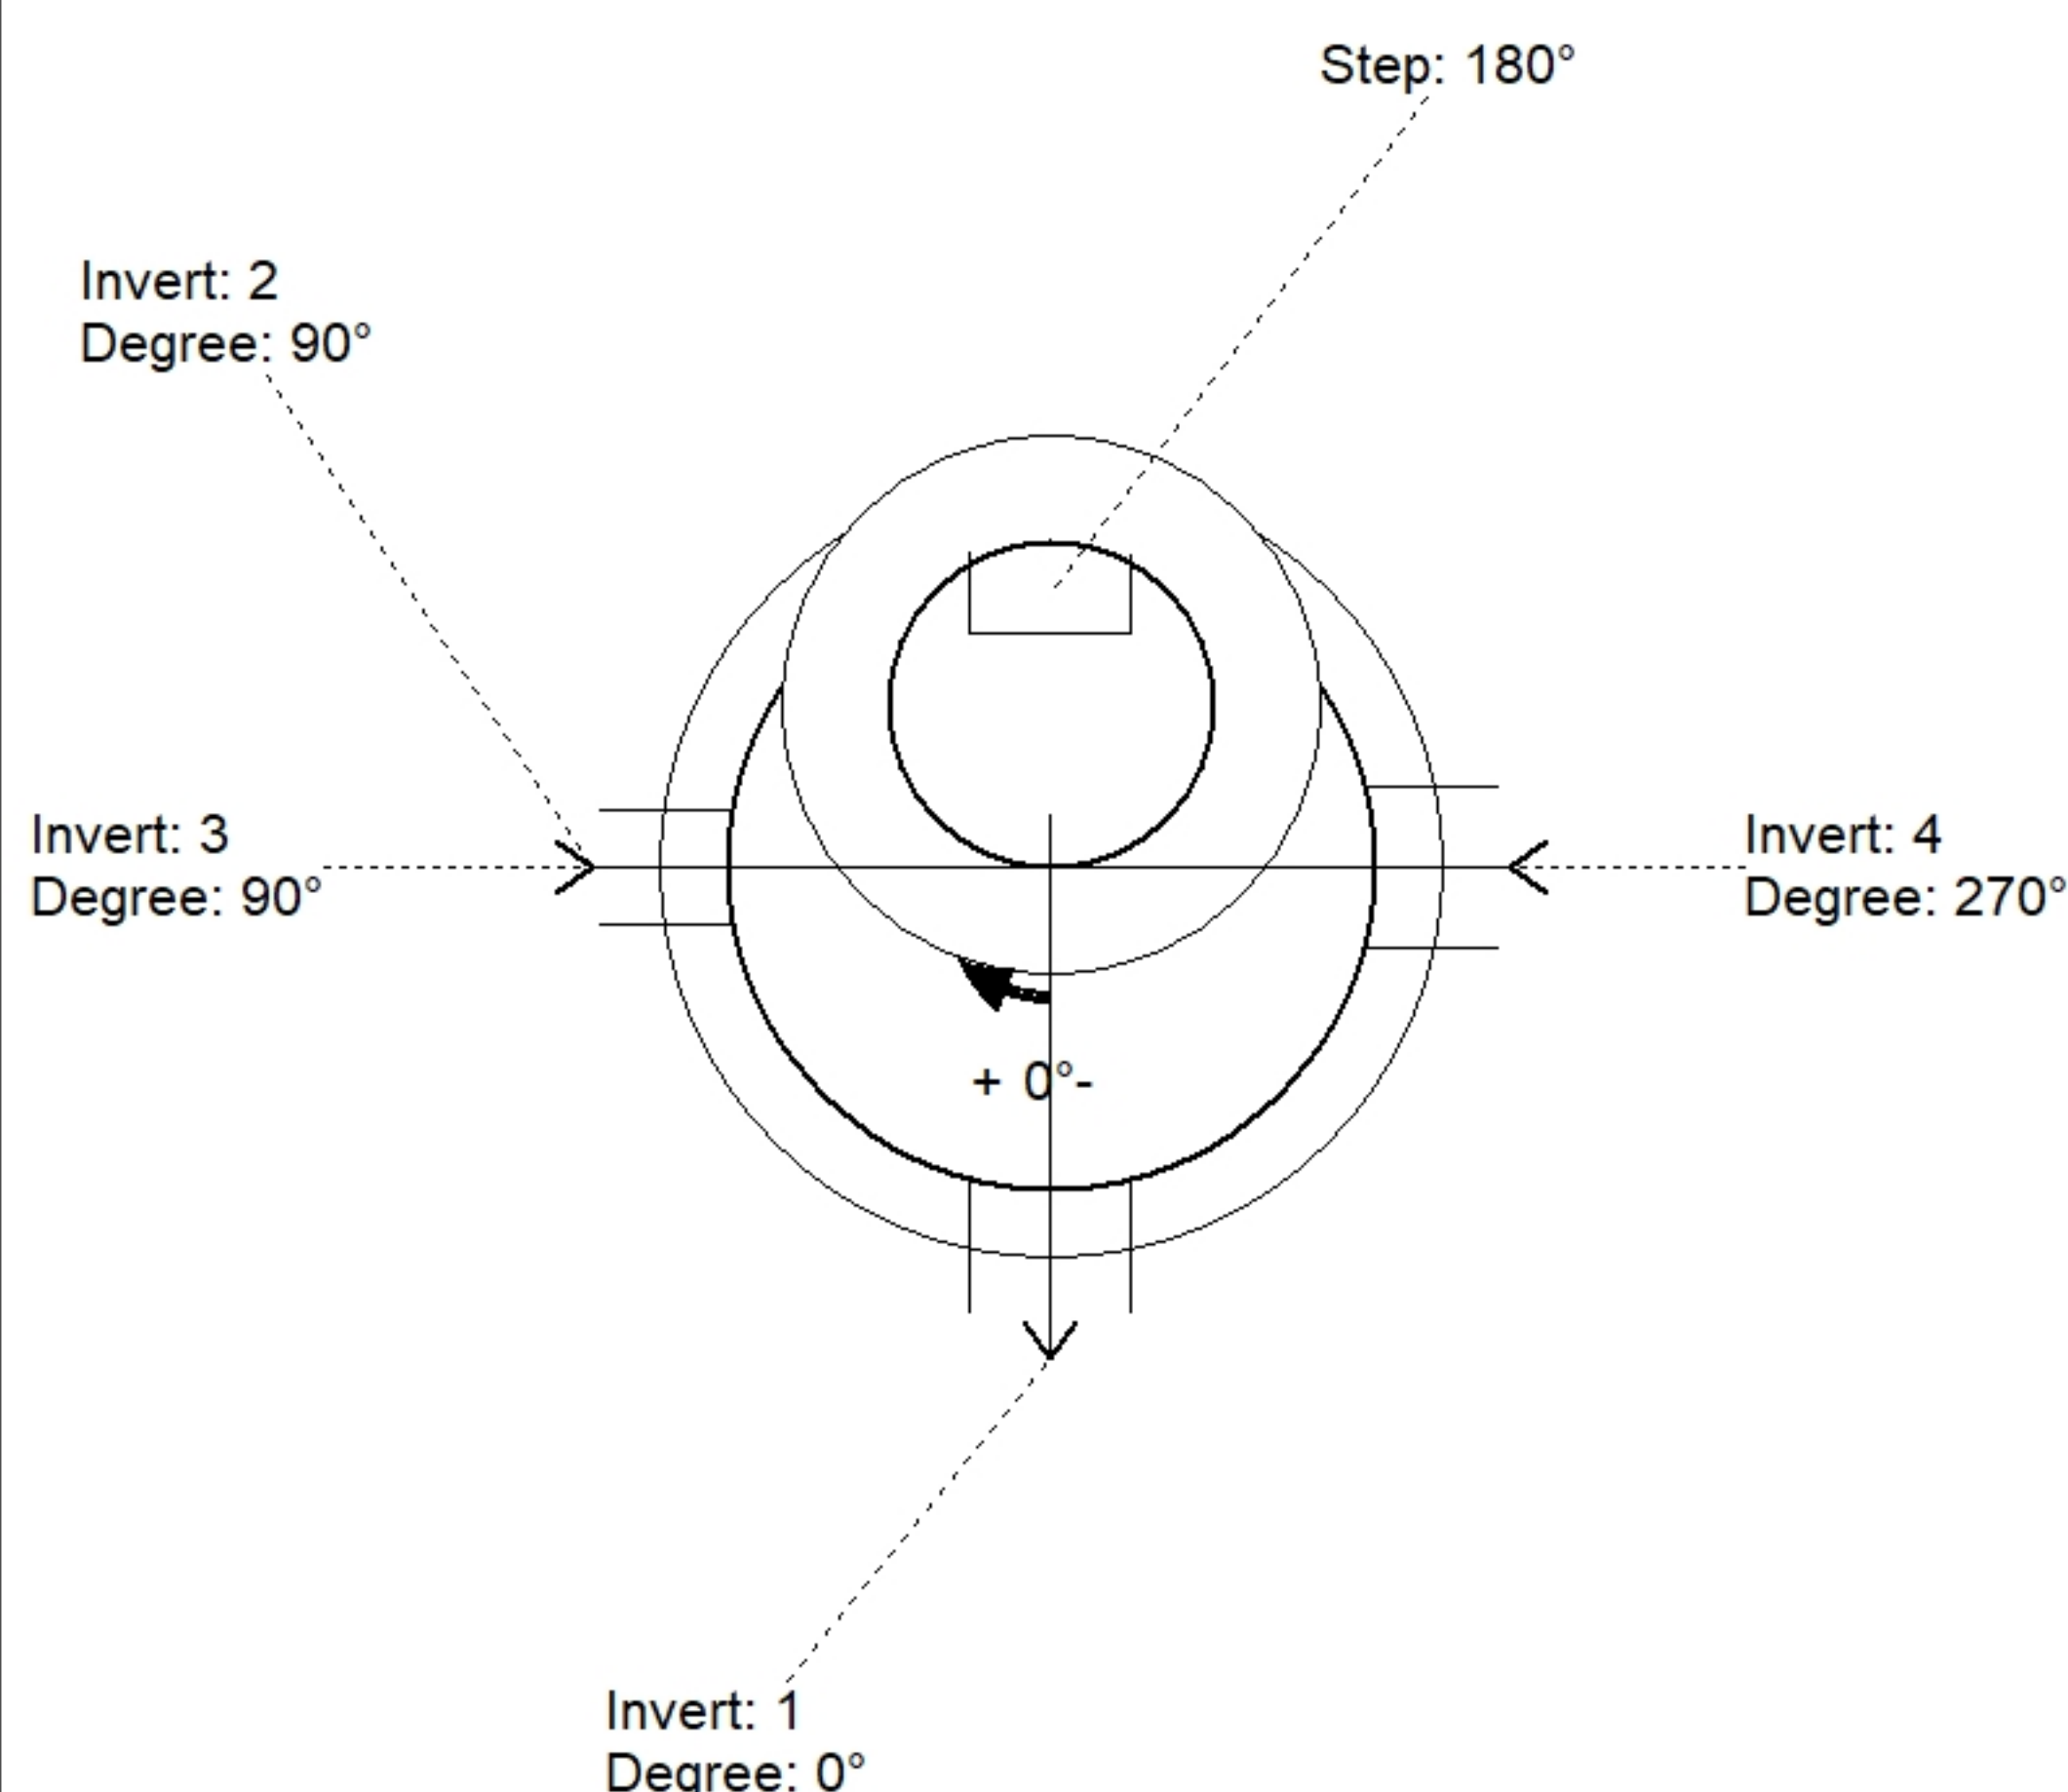

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	747.54'							
Reducer								
Invert 1	734.77'	0°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	0"	P1
Invert 2	742'	90°	8" PVC SDR35	8.5"	8.5"	Drop Tee 8" PVC	18.26"	P3
Invert 3	734.87'	90°	8" PVC SDR35	8.5"	8.5"	Drop Elbow 8" PVC	2.95"	P1
Invert 4	734.87'	270°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	1.2"	P1
Invert 5								
Invert 6								
Invert 7								
Invert 8								

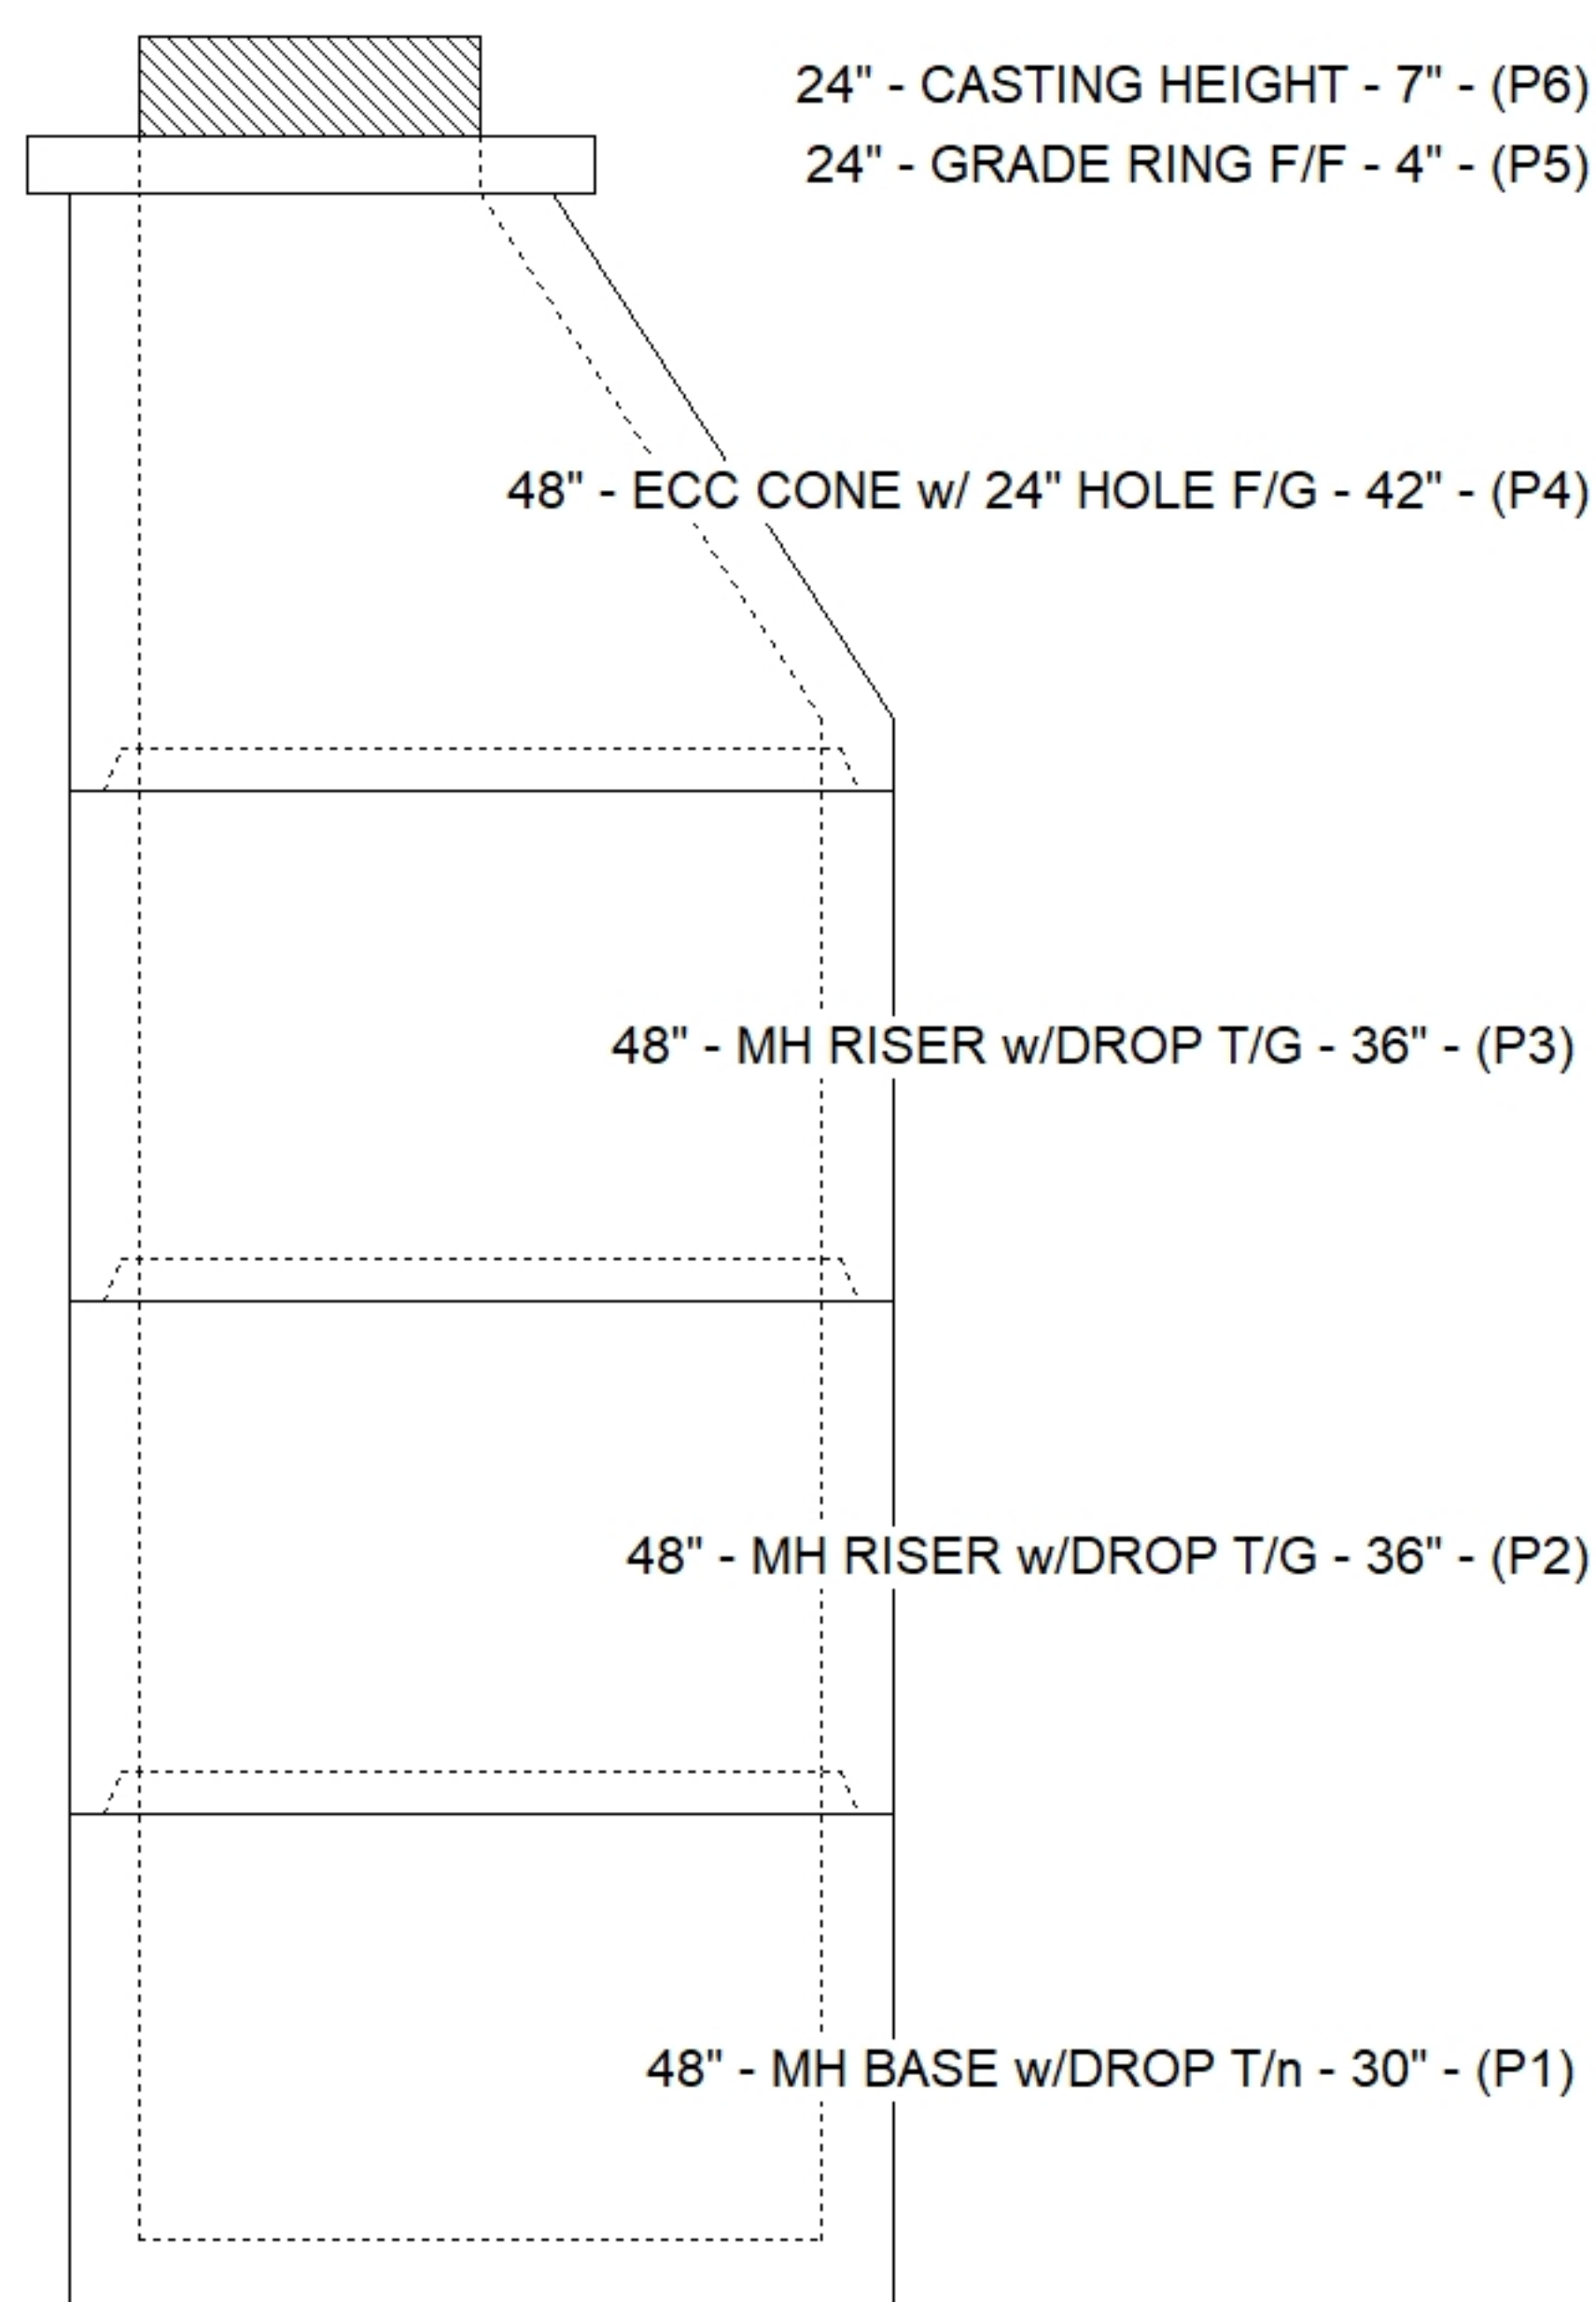

SUBMITTAL
APPROVED BY:
