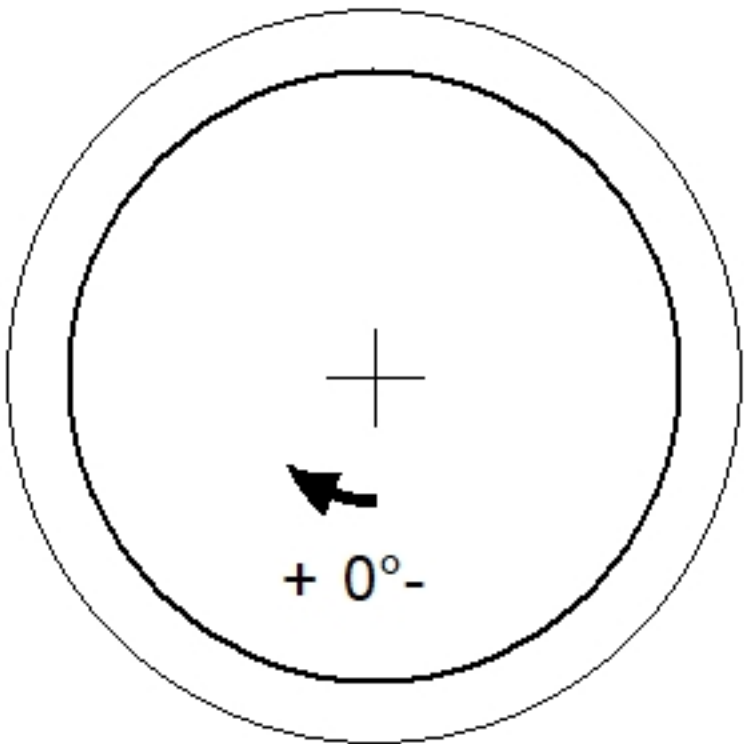
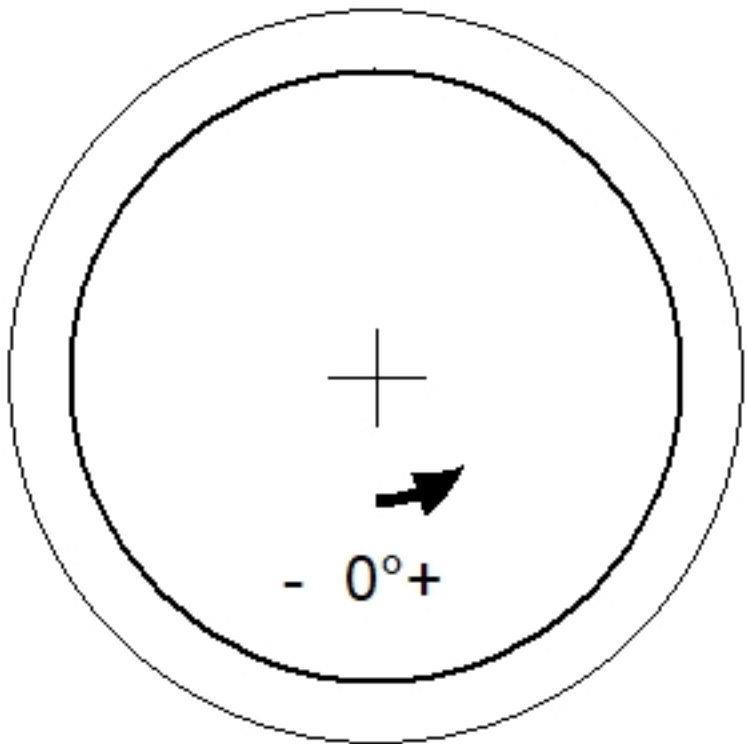
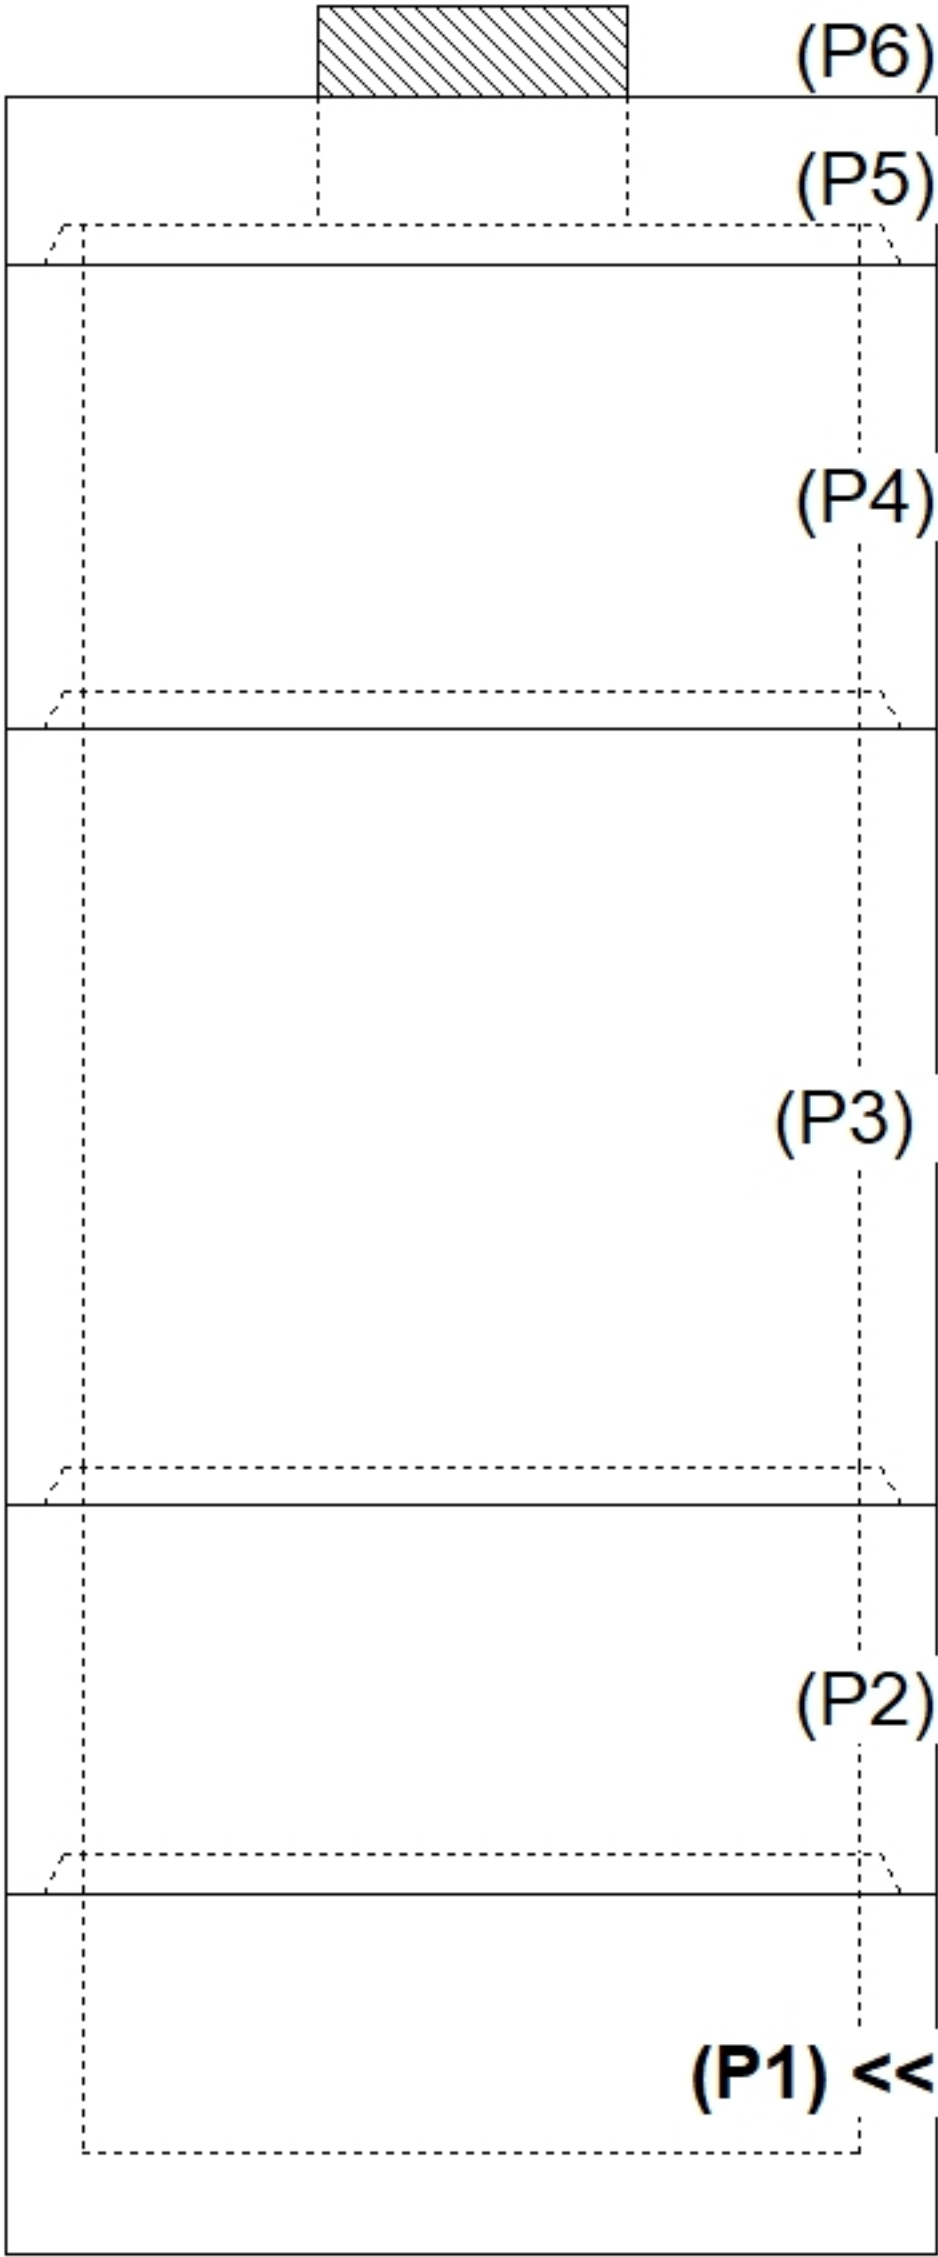
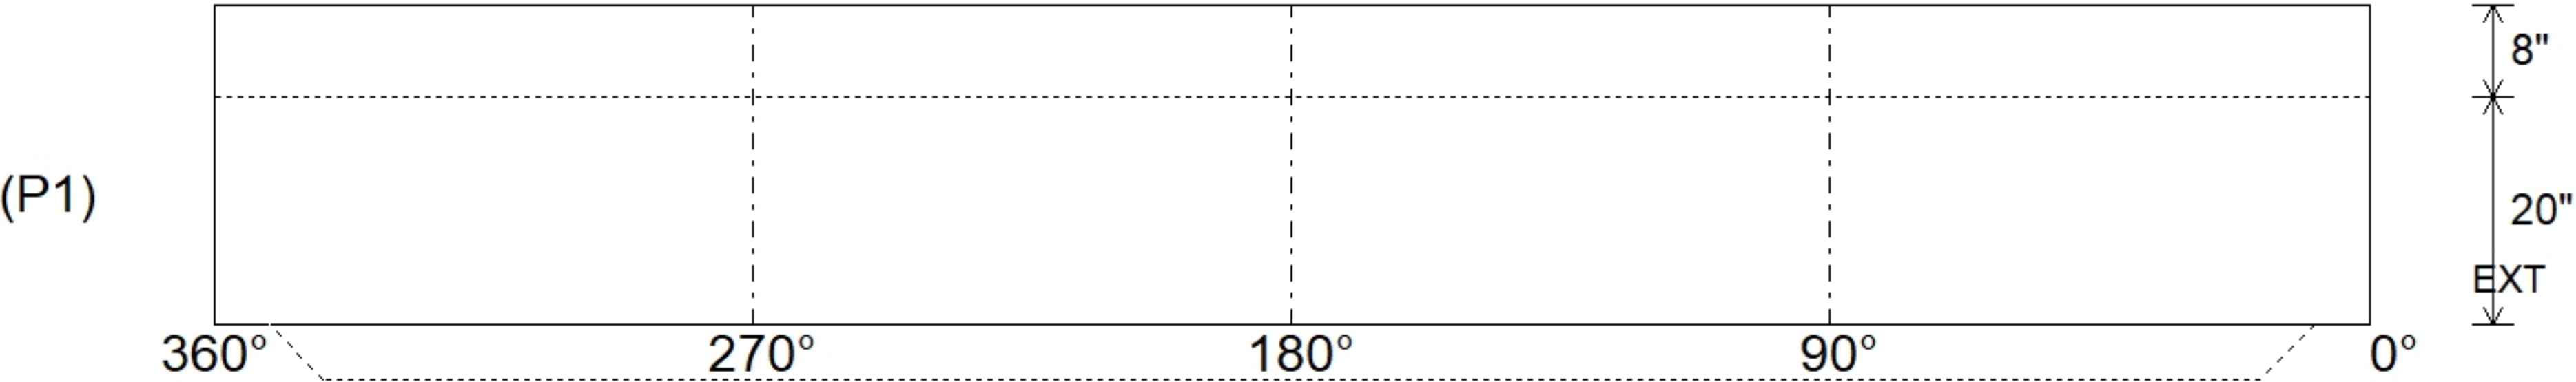


Job Name: 26-3632 ADS Wind Dance Farms Ph.2					Plant: Beaver Dam		Tech: S. Felletter					
Job Location: Fisherville, KY					9/18/2026 8:51:35 AM		PC: M. Sullivan					
Contractor: ADS Advanced Drainage Systems, Inc.												
Structure ID: WQU 2												
P1		MH060BAVF			MH BASE Custom Ht T/n							
P6) 24" - CASTING HEIGHT - 7" P5) 60" - MH FLAT TOP w/24" Ctr. Hole F/G - 13" P4) 60" - MH RISER SPECIAL T/G - 36" P3) 60" - MH RISER SPECIAL T/G - 60" P2) 60" - MH RISER SPECIAL T/G - 30" P1) 60" - MH BASE Custom Ht T/n - 20" 1) ASSEMBLY REQUIRED 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-375 F/C Storm 4) 60" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) Hole - 16					0 lb 2674 lb 3758 lb 6013 lb 3132 lb 4821 lb 0 lb 0 lb 0 lb 271 lb 0 lb 0 lb 0 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-375 F/C "STORM"). 4. LIFTING ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE. 5. P2 & P3 RISERS TO BE MECHANICALLY ATTACHED PRIOR TO INTERNALL INSTALLATION/DELIVERY. . REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - RISER/WALLS (As .18) - FLOOR (As .37) #5 BARS AT 10" C.C.E.W.					
Rim: 674.5' Rim to Invert: 7.1' Slack: 0.2" Sump: 81" Step Position: 0°					Structure Total: 20669 lb							
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset		
Invert 1												
Invert 2												
Invert 3												
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimenions)   INSIDE WALL DIMENSIONS  												
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 6" Floor Height: 8"		Height (Int): 20" Height (Ext): 28"		Weight (Net): 4821 lb Volume (Net): 1.23cu.yd			
