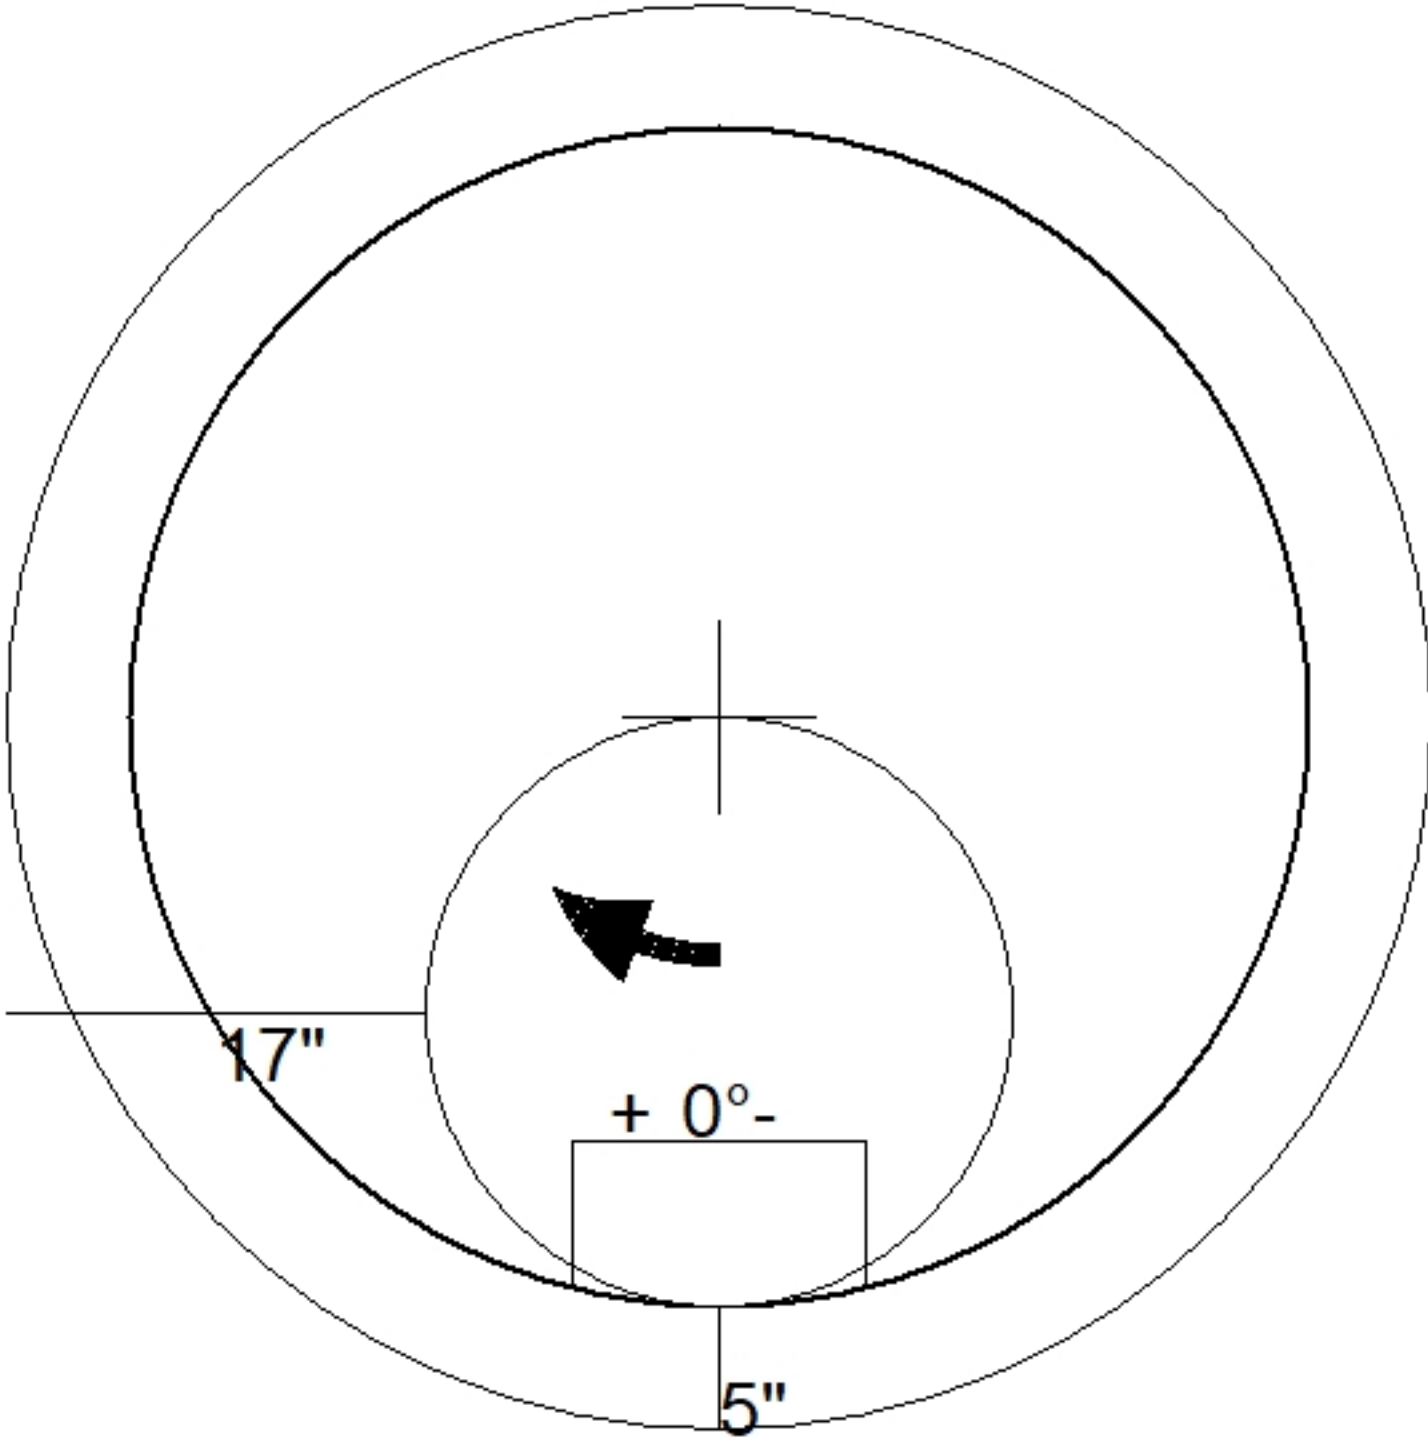
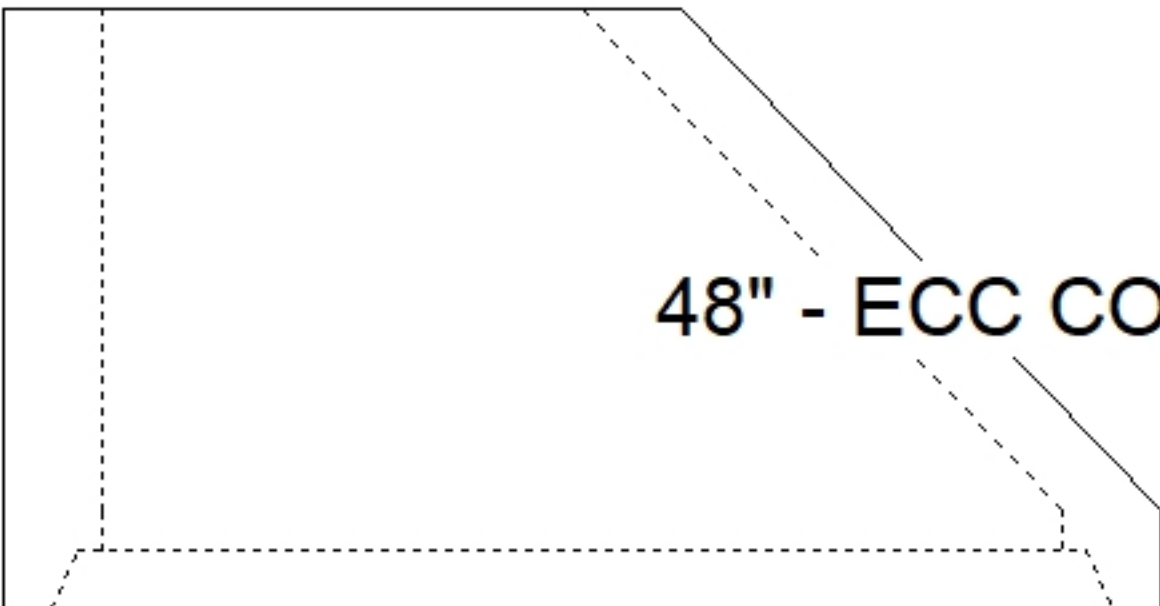


Job Name: 26-3703 Honeysuckle Way Sewer Ext Job Location: Springfield, KY Contractor: Hale Contracting		Plant: Beaver Dam 10/7/2026 4:03:55 PM	Tech: S. Felletter PC: M. Sullivan	
Structure ID: A9				
P3 MH048CN30		ECC CONE w/ 24" HOLE F/G		
P5) 24" - CASTING HEIGHT - 7" P4) 24" - GRADE RING F/F - 3" P3) 48" - ECC CONE w/ 24" HOLE F/G - 30" P2) 48" - MH RISER T/G - 36" P1) 48" - MH BASE w/FLANGE T/n - 24" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 2) 48" - Conseal CS-102 1.00" (Double) 2) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 7) MH Step ML-10-TDS-NCR - 10"		0 lb 202 lb 2050 lb 2515 lb 4468 lb 0 lb 0 lb 1440 lb 0 lb 0 lb 16 lb 0 lb ----- 10691 lb Structure Total:	Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING PROVIDED BY OTHERS. . REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.	
				
				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 30"	Weight (Net): 2050 lb Volume (Net): 0.41cu.yd
